


Inspection Pass Rate

Inspection Pass Rate

Inspection Summary

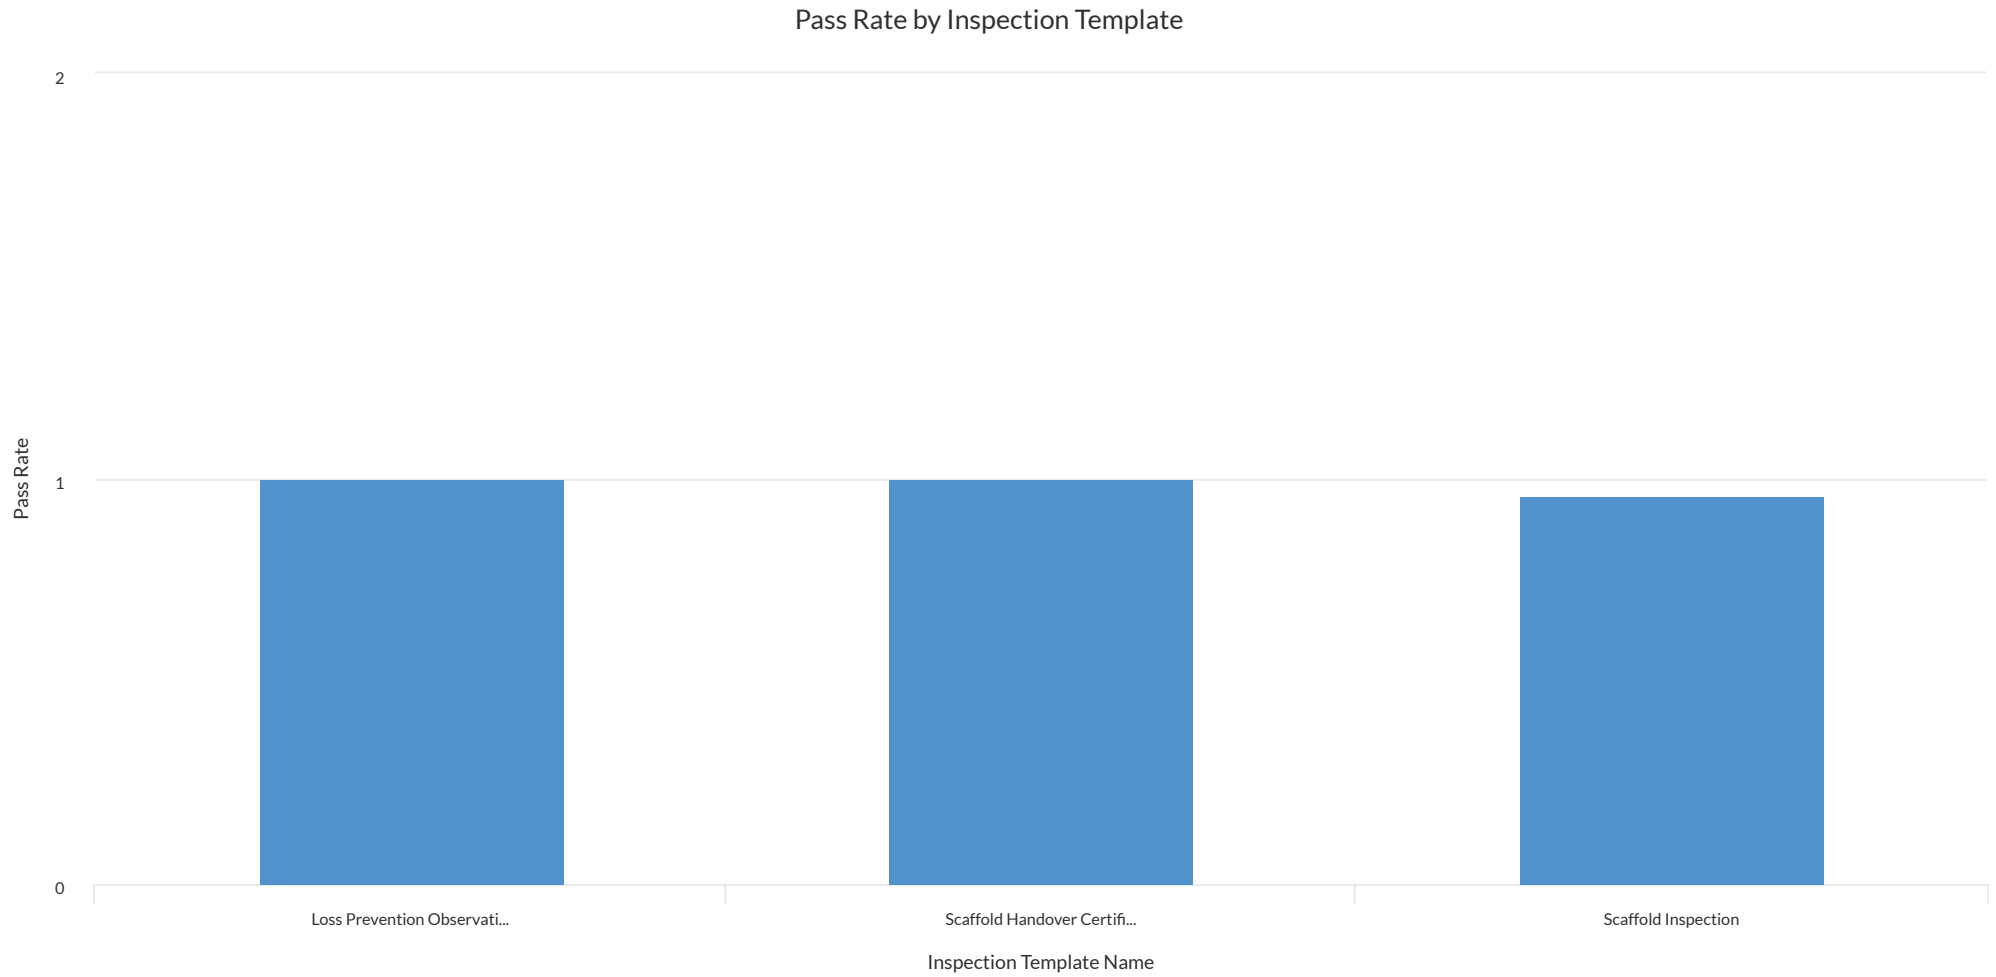

Group	Description	Inspection Date	x	✓	Passed + Failed	Pass Rate
Type: Handover Certificate						Avg: 1
Inspection Template Name: Scaffold Handover Certificate						Avg: 1
	Install 3m of edge protection handrail along concrete steps from raft slab to slab.	30/5/2022	0	2	2	1
	Relocate 8m craneable stretcher stair access and modify handrail for access	6/6/2022	0	2	2	1
	Install 4x swing gates for access around site Install 11m of handrail around crib shed area for access around site	15/6/2022	0	2	2	1
	Install construction stair for access to tower crane base	17/6/2022	0	2	2	1
	Install stretcher stair access to tower crane base	20/6/2022	0	0	0	
	Install handrail for tower crane base	21/6/2022	0	1	1	1
	Install 8m stretcher stair on pour 1 eastern side from B3 to Ground level	22/6/2022	0	1	1	1
	Install 30m of handrail along pour 1 slab edge, handrail to access tower crane base, handrail and swing gate access for Action form workers to strip their for work in the stair core	23/6/2022	0	1	1	1
	Stretcher stair access to tower crane base	28/6/2022	0	1	1	1
	Installed scaffolding cable tray bay for keeping water pipes off ground in walkway access	28/6/2022	0	1	1	1
	Dismantle and reinstall of handrail access to tower crane base	28/6/2022	0	1	1	1
	8m stretcher stair access from B03 to level 1 northern wall	29/6/2022	0	1	1	1
	Crane liftable stretcher stair -1m stair risers kwickstsg	30/6/2022	0	1	1	1
	2x Relocation of craneable 1m stair riser stretcher stair access	7/7/2022	0	1	1	1
	Relocated craneable 1m stair riser stretcher stair B03 from inside form deck to edge of formdeck	12/7/2022	0	1	1	1
	Install handrail edge protection Pour 1	12/7/2022	0	1	1	1
	5 board scaffold to stair core, ramp lives edges and access to B02 pour 1 from B3 to B2	12/7/2022	0	1	1	1
	Installed B03HR3	15/7/2022	0	1	1	1
	Installed B03CS2 stretcher stair access from B03 to B02 form deck	15/7/2022	0	1	1	1
	Installed access from fire stair scaffold to action form shutter roof working platform	15/7/2022	0	1	1	1
	Installed B02HR7	20/7/2022	0	1	1	1
	Handrail for B02 Pour 1 slab penetrations around stretcher stair B03SS1	20/7/2022	0	1	1	1
	Install handrail B02 pour 1 lifting penetration	21/7/2022	0	1	1	1

Group	Description	Inspection Date	x	✓	Passed + Failed	Pass Rate
	Install handrail B02 pour 1 fir stair core and ramp	21/7/2022	0	1	1	1
	5 board scaffold to stair core and ramp live edge from B2 to B1.	26/7/2022	0	1	1	1
	Relocation of 1m stair riser stretcher stair access from B3 pour 2 to B2 pour 1	26/7/2022	0	1	1	1
	Relocation of craneable 1m stretcher stair riser from B02 pour 1 to B03 pour 6	29/7/2022	0	1	1	1
	Install handrail along ramp edge 8m	29/7/2022	0	1	1	1
	Slab penetration handrail	1/8/2022	0	1	1	1
	Stretcher stair access from intermediate level (b02) to b01 pour 1	1/8/2022	0	1	1	1
	Fire stair scaffold Stretcher stair access to stair core platform	2/8/2022	0	1	1	1
	Handrail along B02 pour 2	2/8/2022	0	1	1	1
	Relocate 1m stretcher stair riser from b03 pour 6 to b02 pour 2	2/8/2022	0	1	1	1
	Slab edge handrail b02 pour 2	4/8/2022	0	1	1	1
	Installed extra 1.2m scaffold bay of exisiting ramp edge scaffold from B03 to B01	28/7/2022	0	1	1	1
	Topped up stretcher stair access to stair core platform deck	1/8/2022	0	1	1	1
	Relocated CSS1 from B02 pour 2 to B02 pour 3	11/8/2022	0	1	1	1
	Installed hoist penetration handrails	11/8/2022	0	1	1	1
	Installed handrails for lifting penetration	11/8/2022	0	1	1	1
	Slab handrail in front of stair core and ramp edge	16/8/2022	0	1	1	1
	Slab handrail remaining edge front	16/8/2022	0	1	1	1
	Install handrail along slab edge	19/8/2022	0	1	1	1
	Handrail around lifting penetration	19/8/2022	0	1	1	1
	Handrail around vent penetration	19/8/2022	0	1	1	1
	Handrail along ramp	19/8/2022	0	1	1	1
	Relocate CSS1 from B02 pour 3 to B01 pour 2	19/8/2022	0	1	1	1
	Install 2m handrail and extend handrail under the soffit for edge protection	19/8/2022	0	1	1	1
	Handrail along slab edge in front of ramp	19/8/2022	0	1	1	1

Group	Description	Inspection Date	x	✓	Passed + Failed	Pass Rate
	Install handrail around B01SS1	19/8/2022	0	1	1	1
	Relocate CSS1 from b02 pour 2 to B01 pour 1	25/8/2022	0	1	1	1
	Install level 1 Northern D wall edge protection	24/8/2022	0	1	1	1
	Installed B02HR1 along slab edge	29/8/2022	0	1	1	1
	Installed handrail around the crane penetration	29/8/2022	0	1	1	1
	Install handrail b02 pour 3 southern slab edge	29/8/2022	0	1	1	1
	Installed handrail down ramp b02 pour 3 to b02 pour 1	29/8/2022	0	1	1	1
	Install handrail around stretcher stair B02SS2 penetration b02 pour 3	29/8/2022	0	1	1	1
	Install handrail on lip before ramp and next to B02 HR3	1/9/2022	0	1	1	1
	Install handrail along slab edge	15/9/2022	0	1	1	1
	Install handrail around stair case next to b01 ramp south/west side	15/9/2022	0	1	1	1
	Install handrail around B01SS2	16/9/2022	0	1	1	1
	Install handrail down b01 ramp	16/9/2022	0	1	1	1
	Install handrail around crane penetration	15/9/2022	0	1	1	1
	Install handrail along northern slab edge by stair 3 past lift core	15/9/2022	0	1	1	1
	Relocation of CSS1 from b01 pour 1 to b01 pour 3	20/9/2022	0	1	1	1
	Scaffold perimeter level 1 pour 1	6/10/2022	0	1	1	1
	Install ladder beam for access way for gear removal on level 1	6/10/2022	0	1	1	1
	Construction stair access to jump	10/10/2022	0	1	1	1
	Install handrail around hoist penetration	5/10/2022	0	1	1	1
	Handrail around crane penetration pour 2	11/10/2022	0	1	1	1
	Scaffold perimeter eastern drive way	12/10/2022	0	1	1	1
	Perimeter scaffold western elevation	13/10/2022	0	1	1	1
	Install ladderbeam for access through perimeter scaffold south western elevation	17/10/2022	0	1	1	1
	Install scaffold perimeter south western elevation	17/10/2022	0	1	1	1

Group	Description	Inspection Date	x	✓	Passed + Failed	Pass Rate
	Install perimeter scaffold southern elevation	19/10/2022	0	1	1	1
	Install perimeter scaffold eastern elevation along eastern drive way	20/10/2022	0	1	1	1
	Install perimeter scaffold south-eastern elevation	21/10/2022	0	1	1	1
	Install northern elevation stretcher stair from L01 to L02 perimeter scaffold	6/10/2022	0	1	1	1
	Install stretcher stair access south-western elevation from L01 to L02 perimeter scaffold	17/10/2022	0	1	1	1
	Perimeter scaffold level 2-3 north/ western elevation	11/11/2022	0	1	1	1
	Stretcher stair access level 2 - 3 perimeter scaffold	11/11/2022	0	1	1	1
	Perimeter scaffold level 2-3 western elevation pour 1	11/11/2022	0	1	1	1
	Install stretcher stair access level 2-3 western elevation perimeter scaffold	11/11/2022	0	1	1	1
	Install handrail around crane penetration level 2 western elevation	11/11/2022	0	1	1	1
	Handrail around hoist penetration	14/11/2022	0	1	1	1
	Handrail around slab edge pour 1 level 2 western elevation	14/11/2022	0	1	1	1
	Handrails around slab edge level 2 pour 1 eastern elevation	14/11/2022	0	1	1	1
	Scaffold perimeter level 2-3 east to south/east elevation	21/11/2022	0	1	1	1
	Perimeter scaffold level 2-3 western elevation pour 2	23/11/2022	0	0	0	
	Handrail along slab edge level 2 pour 2 eastern elevation and around egg	21/11/2022	0	1	1	1
	Handrail along slab edge level 2 pour 2 western elevation	23/11/2022	0	1	1	1
	Install handrail L02 slab edge eastern elevation	13/12/2022	0	1	1	1
	Perimeter scaffold L03	14/11/2022	0	0	0	
	Stretcher stair access off perimeter scaffold	14/11/2022	0	1	1	1
	Handrail edge protection around slab edge level 2 from eastern to western elevation 34m	6/1/2023	0	1	1	1
	Handrail around penetration B02 north/east corner	12/1/2023	0	1	1	1
	Install handrail inside L02 main core penetration	19/1/2023	0	1	1	1
	Handrail around north/eastern corner penetration	24/1/2023	0	1	1	1
	Handrail B01HR4 north/eastern corner	31/1/2023	0	1	1	1

Group	Description	Inspection Date	x	✓	Passed + Failed	Pass Rate
	Handrail inside main core	8/2/2023	0	1	1	1
	Pigpen Handrail for Preston loading bay install L03 western elevation	10/2/2023	0	1	1	1
	5x Planter box handrail	17/2/2023	0	1	1	1
	Handrail around Preston Loading Bay	24/2/2023	0	1	1	1
	Handrail around penetration behind main core	24/2/2023	0	1	1	1
	Install core handrail L04 behind lift core	28/2/2023	0	1	1	1
	VOID - Double Up Install planter box handrail L04	3/3/2023	0	1	1	1
	Install planter box handrail L04	3/3/2023	0	1	1	1
	Install handrail for penetration behind main core western elevation	6/3/2023	0	1	1	1
	Handrail for Preston L05	6/3/2023	0	1	1	1
	Handrail penetrations behind main core L05	14/3/2023	0	1	1	1
	Install handrail for Preston install L06 14m	21/3/2023	0	1	1	1
	Install handrail behind main core L06 10m	21/3/2023	0	1	1	1
	Install planter box handrail L05 32m	21/3/2023	0	1	1	1
	Install handrail for Preston loading bay western elevation L07	4/4/2023	0	1	1	1
	Install handrail behind main core L07 western elevation	6/4/2023	0	1	1	1
	Install loading bay Preston handrail L08 western elevation	20/4/2023	0	1	1	1
	Install planter box handrail L06	17/4/2023	0	1	1	1
	Install handrail penetration behind main core L08 condenser deck	20/4/2023	0	1	1	1
	Install planter box handrail L07	9/5/2023	0	1	1	1
	Install Preston loading bay handrail L09 pour 2 western elevation 14m	15/5/2023	0	1	1	1
	Install planter box handrail L08	18/5/2023	0	1	1	1
	Install handrail pig pen for L10 loading bay 14m	24/5/2023	0	1	1	1
	Install planter box handrail L09	29/5/2023	0	1	1	1
	Install handrail in front of penetration behind main core condenser deck	29/5/2023	0	1	1	1

Group	Description	Inspection Date	x	✓	Passed + Failed	Pass Rate
	Install loading bay handrail L11	1/6/2023	0	1	1	1
	Install handrail behind main core condenser deck L11	2/6/2023	0	1	1	1
	Planter box handrail L10	13/6/2023	0	1	1	1
	Install handrail behind condenser deck L11 (1x2.4) + (2x1.8m)	14/6/2023	0	1	1	1
	Install planter box handrail L11	23/6/2023	0	1	1	1
	Install handrail condenser deck L09 (1x1.8m)+(1x2.4) = 4.2m	1/6/2023	0	1	1	1
	Install loading bay handrail L13	27/6/2023	0	1	1	1
	Install handrail behind condenser deck L13	27/6/2023	0	1	1	1
	Install handrail around slab load out penetration L12 - instead of Preston handrail on this level. Level 12 doesn't have a loading bay	27/6/2023	0	1	1	1
	Install handrail behind main core condenser deck	4/7/2023	0	1	1	1
	Install planter box hand rail level 12	7/7/2023	0	1	1	1
	Install handrail around slab penetration instead of loading bay handrails due to no loading bay L14. As Per contract	18/7/2023	0	1	1	1
	Install planter box handrail L13 As per contract	18/7/2023	0	0	0	
	Install loading bay handrail L15 As per contact	26/7/2023	0	1	1	1
	Install handrail behind main core condenser deck L14 As per contact	28/7/2023	0	1	1	1
	Install handrail behind main core condenser deck L15 As per contact	28/7/2023	0	1	1	1
	Planter box handrail L14 As per contact	31/7/2023	0	1	1	1
	Install handrail around bin shoot penetration where Preston loading bay can't be installed L16 As per contact	3/8/2023	0	1	1	1
	Install handrail next to hoist right and left hand side L15	18/8/2023	0	1	1	1
	Install handrail around Preston L15	22/8/2023	0	1	1	1
	Install handrail behind main core condenser deck L15	22/8/2023	0	1	1	1
	Install planter box handrail L16	26/8/2023	0	1	1	1
	Install handrail behind main core condenser deck L17	24/8/2023	0	1	1	1
	Install tube n clip handrail on hob where Preston use to be located L9	25/8/2023	0	1	1	1
	Install loading bay handrail for Preston install L18	4/9/2023	0	1	1	1

Group	Description	Inspection Date	x	✓	Passed + Failed	Pass Rate
	Handrail next to hoist L16	31/8/2023	0	1	1	1
	Install planter box handrail L7 & L9 since crane ties have been removed	31/8/2023	0	1	1	1
	Install planter box handrail L17	1/9/2023	0	1	1	1
	Install handrail behind main core L18	1/9/2023	0	1	1	1
	Installed handrail level 17 next to hoist and preston	14/9/2023	0	1	1	1
	Hob hand rail replacing the preston level 10	20/9/2023	0	1	1	1
	Planter box handrail level 18	20/9/2023	0	1	1	1
	Install planter box handrail level 15	7/8/2023	0	1	1	1
	Installed preston handrail level 19	22/9/2023	0	1	1	1
	Install handrail next to hoist and preston	22/9/2023	0	1	1	1
	Install hob handrail level 11	27/9/2023	0	1	1	1
	Installed main core handrails level 19	27/9/2023	0	1	1	1
	Fixed bent planter box standard level 15	27/9/2023	0	1	1	1
	Installed handrail next to Preston level 19	27/9/2023	0	1	1	1
	Build 1.2m wide scaffold for block layers down the ramp to b1	6/10/2023	0	1	1	1
	Level 19 planter box handrail	10/10/2023	0	1	1	1
	Installed main core handrail level 20	10/10/2023	0	1	1	1
	Handrail around bin shoot level 20 instead of preston	13/10/2023	0	1	1	1
	Hoist handrail level 20	13/10/2023	0	1	1	1
	Installed 2.5m screen level 2 condenser deck to capsulat any following objects when Precision strip stairwell pressure riser penos	13/10/2023	0	1	1	1
	Scaffolding around gas cupboard for form work	18/10/2023	0	1	1	1
	Hob hand rail level 13	23/10/2023	0	1	1	1
	Installed hand rail for preston Install	26/10/2023	0	1	1	1
	Level 21 main core handrail	31/10/2023	0	1	1	1
	Install hob handrail level 15	1/11/2023	0	1	1	1

Group	Description	Inspection Date	x	✓	Passed + Failed	Pass Rate
	level 20 planter box handrail	31/10/2023	0	1	1	1
	Hob hand rail level 17	9/11/2023	0	1	1	1
Type: Loss Prevention Observation						Avg: 1
Inspection Template Name: Loss Prevention Observation						Avg: 1
	LPO	13/12/2022	0	8	8	1
Type: Monthly Scaffold Inspections						Avg: 0.96
Inspection Template Name: Scaffold Inspection						Avg: 0.96
	Type and purpose of scaffold? Craneable Construction stair Reason for inspection? Monthly inspection	21/11/2022	0	32	32	1
	Type and purpose of scaffold? Handrail Reason for inspection? 30 day	7/3/2023	0	5	5	1
	Type and purpose of scaffold? Reason for inspection?	15/4/2023	0	31	31	1
	Type and purpose of scaffold? Reason for inspection?	15/5/2023	0	34	34	1
	Type and purpose of scaffold? Reason for inspection?	4/5/2023	0	26	26	1
	Type and purpose of scaffold? Reason for inspection?	4/6/2023	0	29	29	1
	Type and purpose of scaffold? Reason for inspection?	4/7/2023	0	5	5	1
	Type and purpose of scaffold? Reason for inspection? Result of a scaffold incident on another project not related to Cogent Scaffolding	27/7/2023	0	34	34	1
	Type and purpose of scaffold? Access to level 1 pour 1 and Edge protection Reason for inspection? 30 day inspection	22/9/2022	1	30	31	0.97
	Type and purpose of scaffold? Stretcher stair access B03SS1 Reason for inspection? 30 day inspection	22/9/2022	1	31	32	0.97
	Type and purpose of scaffold? Stretcher stair access Reason for inspection? 30 day inspection	13/9/2022	1	30	31	0.97
	Type and purpose of scaffold? Stretcher stair access B03SS2 Reason for inspection? 30 day inspection	22/9/2022	1	30	31	0.97
	Type and purpose of scaffold? 3x stretcher stairs level 1-2 Reason for inspection? Monthly inspection	26/11/2022	1	31	32	0.97
	Type and purpose of scaffold? Stretcher stair B01 -L01 SS1 and B01 - L01 SS2 Reason for inspection? Monthly inspection	21/11/2022	1	32	33	0.97
	Type and purpose of scaffold? Craneable stretcher stair layher Reason for inspection? Monthly inspection	21/11/2022	1	32	33	0.97
	Type and purpose of scaffold? Perimeter scaffold level 1-2 Reason for inspection? Monthly inspection	21/11/2022	1	34	35	0.97
	Type and purpose of scaffold? Perimeter scaffold level 2-3 Reason for inspection? Monthly inspection	21/11/2022	1	29	30	0.97
	Type and purpose of scaffold? 2x Stretcher stair access level 2-3 Reason for inspection? Monthly inspection	21/11/2022	1	31	32	0.97

Group	Description	Inspection Date	x	✓	Passed + Failed	Pass Rate
	Type and purpose of scaffold? Stretcher stair access B02-L01 Reason for inspection? 30 day inspection	17/1/2023	1	29	30	0.97
	Type and purpose of scaffold? Stretcher stair access Reason for inspection? 30 day inspection	17/1/2023	1	30	31	0.97
	Type and purpose of scaffold? Stretcher stair access Reason for inspection? 30 day inspection	17/1/2023	1	31	32	0.97
	Type and purpose of scaffold? Stretcher stair Access Reason for inspection? 30 day inspection	17/1/2023	1	31	32	0.97
	Type and purpose of scaffold? Stretcher stair access into crane base Reason for inspection? 30 day	7/3/2023	1	24	25	0.96
	Type and purpose of scaffold? Whole tower inspection Reason for inspection? Safety	4/10/2023	1	29	30	0.97
	Type and purpose of scaffold? Edge protection perimeter scaffold Reason for inspection? 30 day inspection	21/10/2022	2	30	32	0.94
	Type and purpose of scaffold? Perimeter scaffold and 3x stretcher stairs access Reason for inspection? 30 day inspection	21/10/2022	2	31	33	0.94
	Type and purpose of scaffold? Stretcher stair Reason for inspection? 30 day	7/3/2023	2	28	30	0.93
	Type and purpose of scaffold? Planter box handrail Reason for inspection? 30 day inspection	23/3/2023	2	23	25	0.92
	Type and purpose of scaffold? Stretcher stair access SS2 Reason for inspection? 30 day inspection	21/10/2022	3	31	34	0.91
	Type and purpose of scaffold? Craneable stretcher stair access CSS1 Reason for inspection? 30 day inspection	21/10/2022	3	31	34	0.91
	Type and purpose of scaffold? Stretcher stair access SS1 Reason for inspection? 30 day inspection	21/10/2022	4	31	35	0.89
	Type and purpose of scaffold? Craneable construction stair Reason for inspection? 30 day inspection	13/10/2022	4	28	32	0.88
	Type and purpose of scaffold? Craneable layher stretcher stair Reason for inspection? 30 day inspection	21/10/2022	4	30	34	0.88
Type: Safety						Avg: 0.97
Inspection Template Name: Scaffold Inspection						Avg: 0.97
	Type and purpose of scaffold? Reason for inspection?	20/4/2022	0	33	33	1
	Type and purpose of scaffold? Reason for inspection?	20/4/2022	0	35	35	1
	Type and purpose of scaffold? Reason for inspection?	4/5/2022	0	0	0	
	Type and purpose of scaffold? Handrail edge protection Reason for inspection? Monthly inspection	9/6/2022	0	6	6	1
	Type and purpose of scaffold? Bridge bay access Reason for inspection? Monthly inspection Notes- can't see soleboards as covered by water	9/6/2022	0	30	30	1
	Type and purpose of scaffold? Handrail edge protection Reason for inspection? 30 day	21/7/2022	0	6	6	1
	Type and purpose of scaffold? 8m stretcher stair access Reason for inspection? Monthly inspection	9/6/2022	1	34	35	0.97
	Type and purpose of scaffold? Stretcher stair access B03SS1 Reason for inspection? 30 day	21/7/2022	1	30	31	0.97

Group	Description	Inspection Date	x	✓	Passed + Failed	Pass Rate
	Type and purpose of scaffold? Stretcher stair access B03SS2 Reason for inspection? 30 day	21/7/2022	1	30	31	0.97
	Type and purpose of scaffold? Craneable stretcher stair access CSS1 Reason for inspection? 30 day	21/7/2022	1	27	28	0.96
	Type and purpose of scaffold? 5 board scaffold for stair core and live ramp Reason for inspection? 30 day	21/7/2022	1	30	31	0.97
	Type and purpose of scaffold? Stretcher stair access Reason for inspection? 30 day inspection	21/7/2022	1	25	26	0.96
	Type and purpose of scaffold? Crainable stretcher stair access CSS1 Reason for inspection? 30 day inspection	22/8/2022	1	30	31	0.97
	Type and purpose of scaffold? Stretcher stair access B02 CS2 Reason for inspection? 30 Day inspection	22/8/2022	1	28	29	0.97
	Type and purpose of scaffold? 10m stretcher stair access Reason for inspection? Monthly inspection	9/6/2022	2	34	36	0.94
	Type and purpose of scaffold? Stretcher stair access B03SS1 Reason for inspection? 30 day inspection	22/8/2022	2	32	34	0.94
	Type and purpose of scaffold? Stretcher stair access B03SS2 Reason for inspection? 30 day inspection	22/8/2022	2	32	34	0.94
Grand Totals:						Avg: 0.99
