



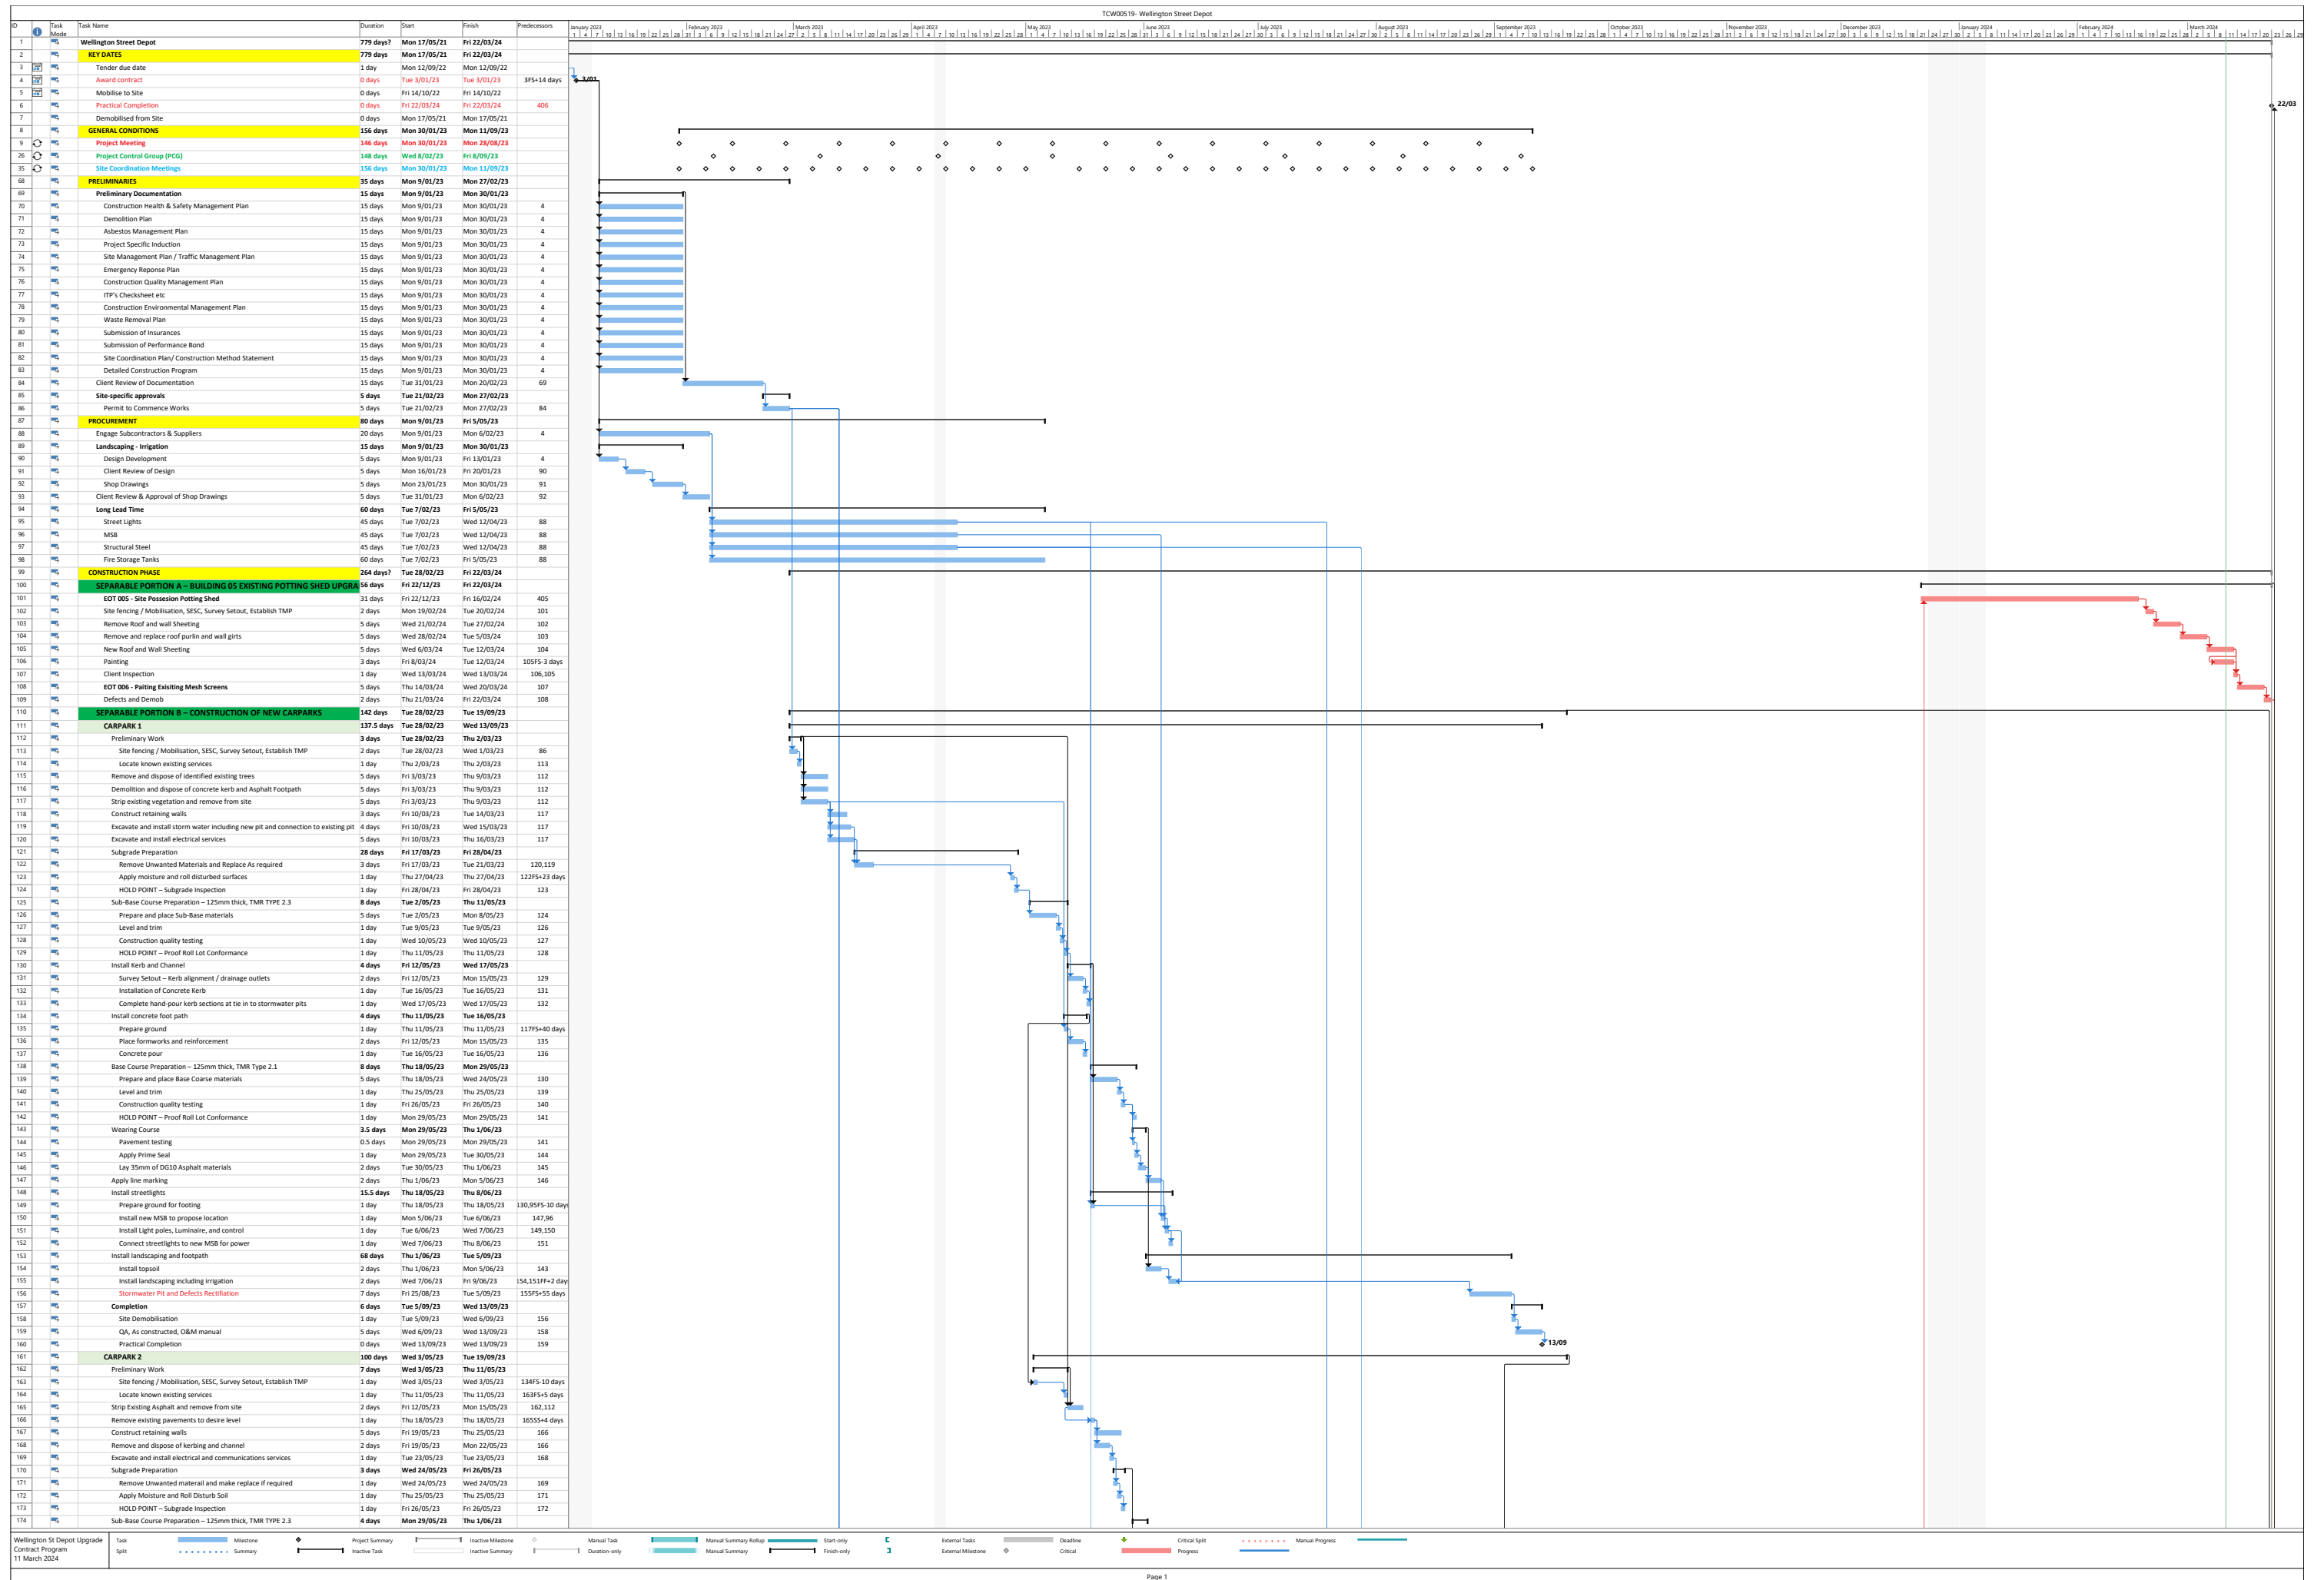

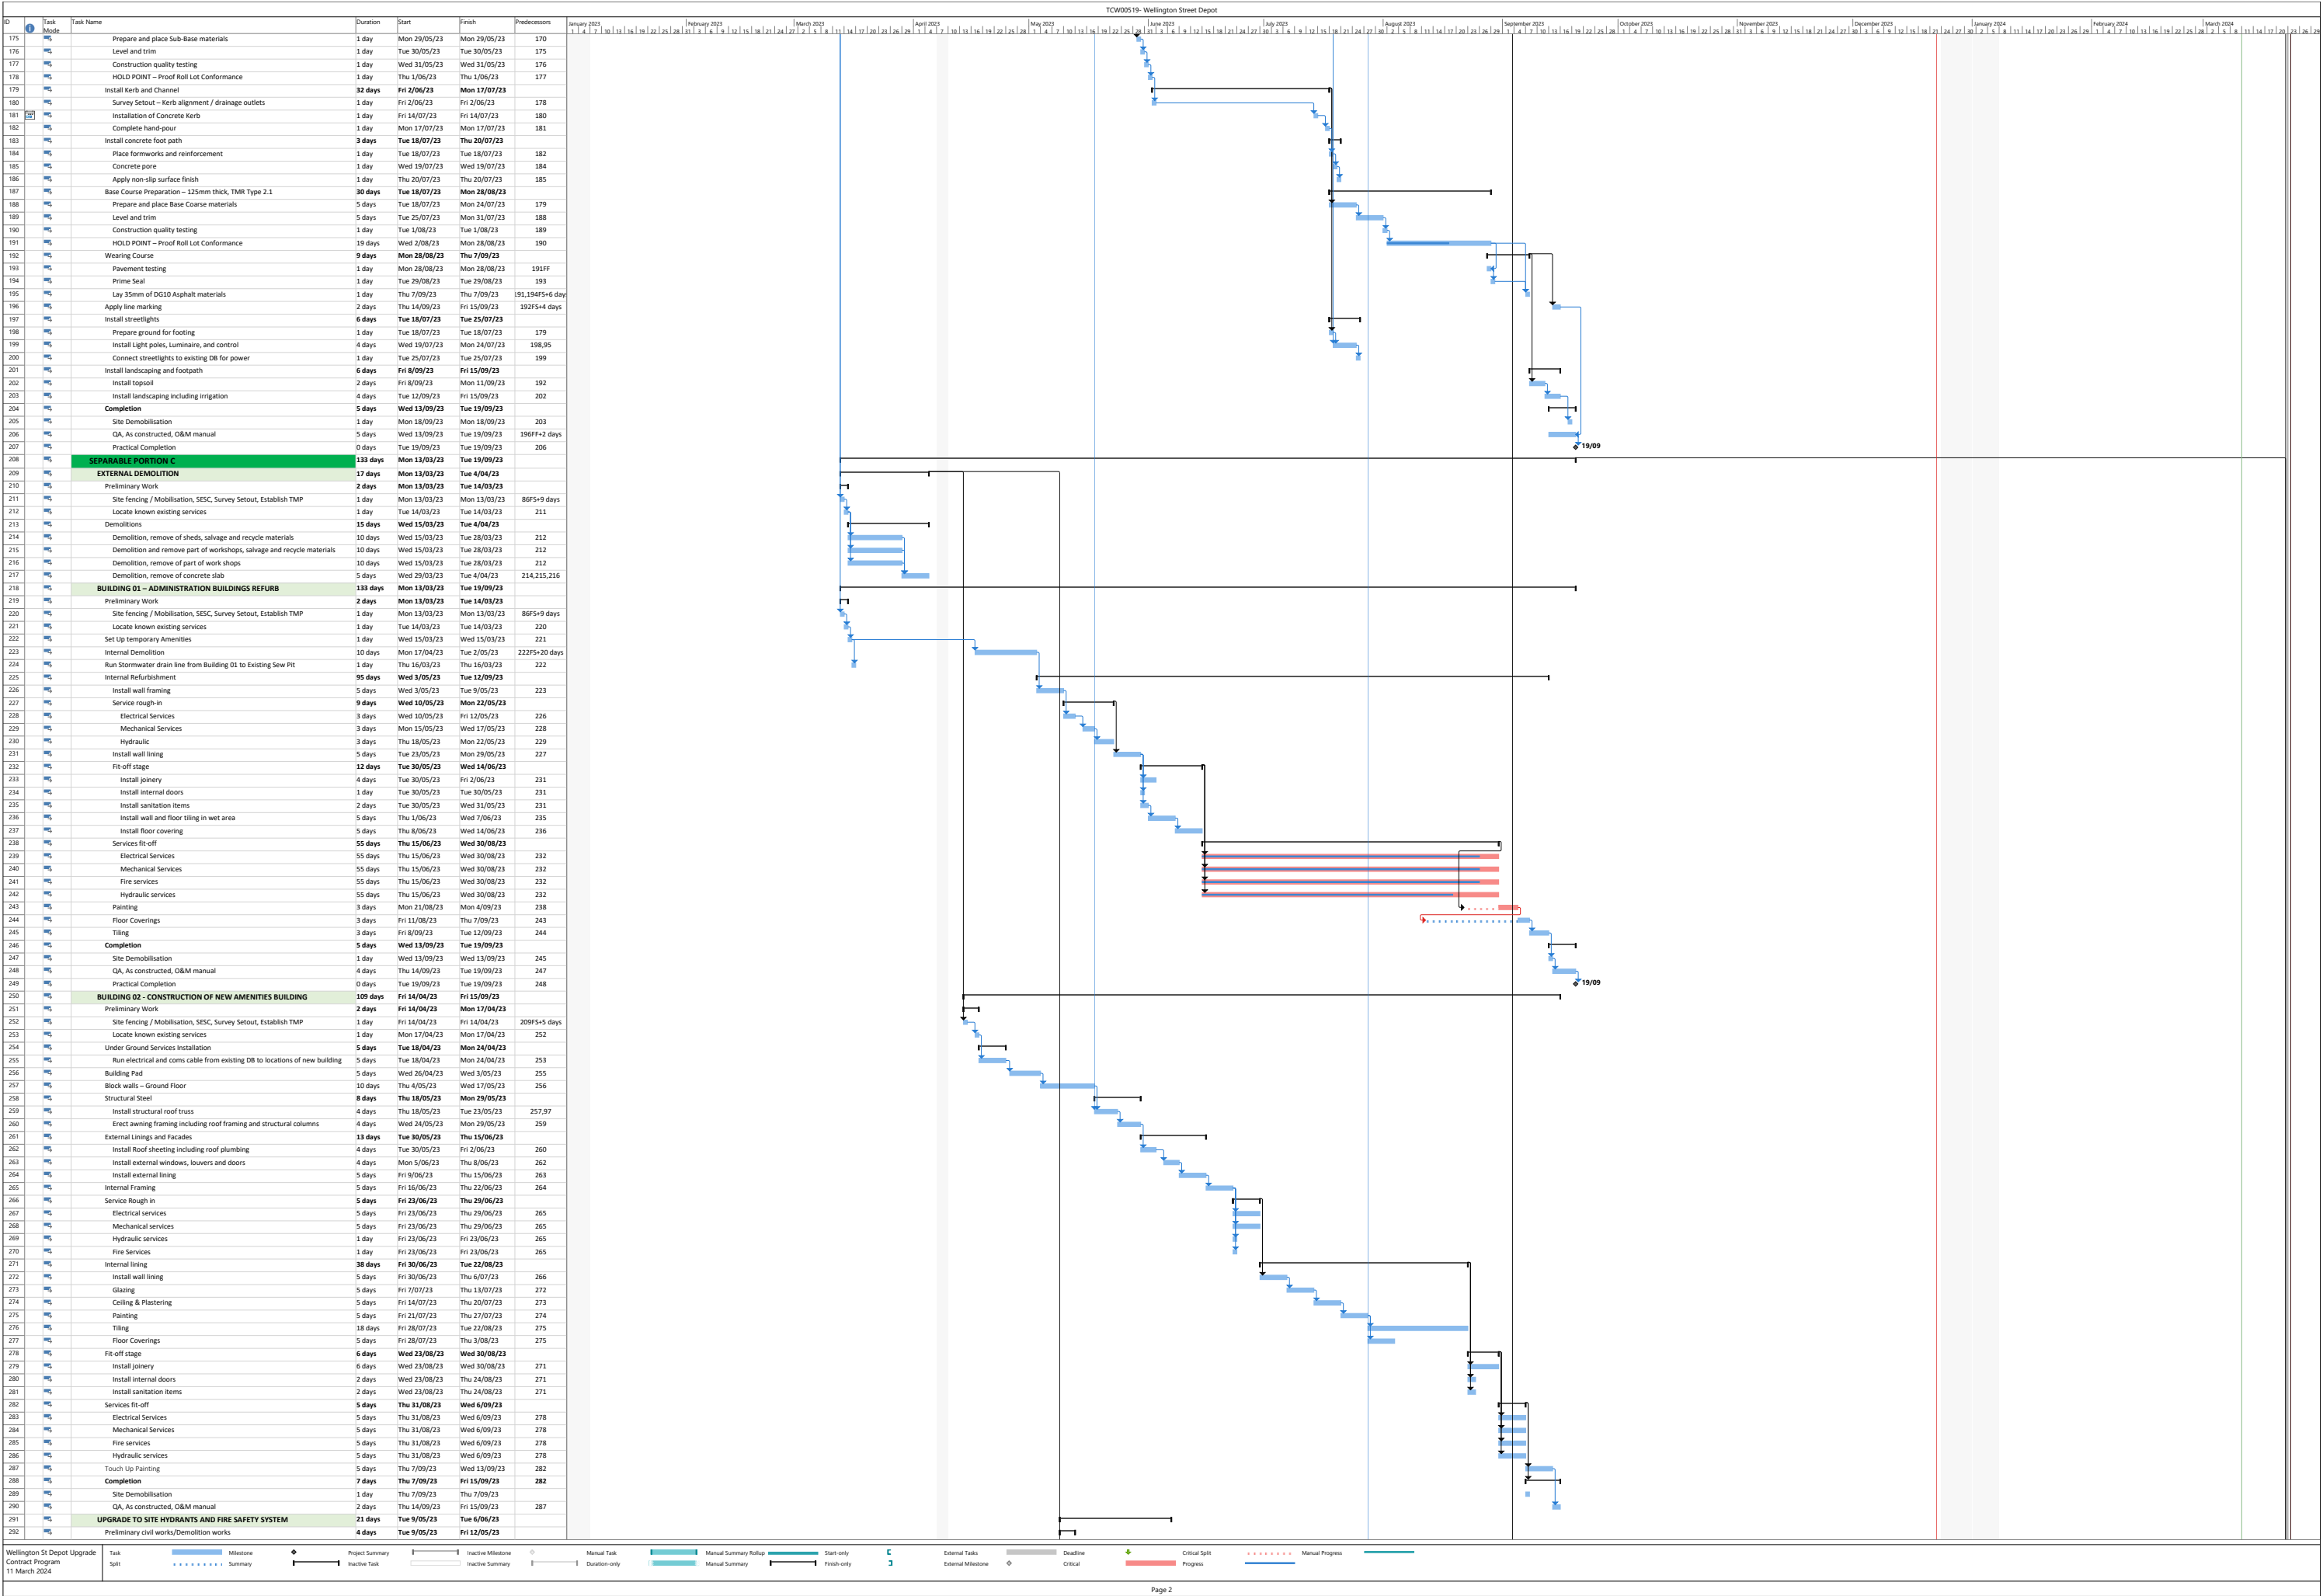

Task Mode

Task Name

Duration

Start

Finish

Predecessors

293

Remove trees

1 day

Tue 9/05/23

Tue 9/05/23

209FS+20 days

294

Remove bunding walls

2 days

Wed 10/05/23

Thu 11/05/23

293

295

Level ground to desire height

1 day

Fri 12/05/23

Fri 12/05/23

294

296

Hydraulic works

17 days

Mon 15/05/23

Tue 6/06/23

297

Install effective storage fire tanks

5 days

Mon 15/05/23

Fri 18/05/23

295

298

Run Pipeline from existing water main to tanks

5 days

Mon 22/05/23

Fri 26/05/23

297

299

Install valves, water meter, fire booster pumps and hydraulic fittings and etc

5 days

Mon 29/05/23

Fri 2/06/23

298

300

Run fire pipeline thru site as per hydraulic layouts

2 days

Mon 5/06/23

Tue 6/06/23

299

301

SEPARABLE PORTION D

141 days

Mon 29/05/23

Tue 12/12/23

302

BUILDING 03 - CONSTRUCTION OF UNDERCOVER TRAILER & VEHICLE BAYS

90 days

Mon 29/05/23

Fri 29/09/23

303

Preliminary Work

2 days

Fri 16/06/23

Mon 19/06/23

304

Site fencing / Mobilisation, SESC, Survey Setout, Establish TMP

1 day

Fri 16/06/23

Fri 16/06/23

305

Locate known existing services

1 day

Mon 19/06/23

Mon 19/06/23

304

306

Preliminary Civil works

1 day

Tue 20/06/23

Tue 20/06/23

305

307

Under Ground Services

3 days

Wed 21/06/23

Fri 23/06/23

308

Elect and comms

3 days

Wed 21/06/23

Fri 23/06/23

306

309

hydraulic

3 days

Wed 21/06/23

Fri 23/06/23

306

310

Building Pad

4 days

Mon 26/06/23

Thu 29/06/23

307

311

Covered area Concrete Pavement

70 days

Mon 29/05/23

Fri 1/09/23

310

312

Block walls

0 days

Mon 31/07/23

Mon 31/07/23

311

313

Erect Structural steel

10 days

Tue 1/08/23

Mon 14/08/23

312

314

Roofing Works

0 days

Thu 31/08/23

Thu 31/08/23

313

315

External Linings and Facades

20 days

Tue 1/08/23

Mon 28/08/23

316

Install Roof sheeting including roof plumbing

19 days

Tue 1/08/23

Fri 25/08/23

313

317

Install external windows, louvers and Roller doors

20 days

Tue 1/08/23

Mon 28/08/23

313

318

Internal Framing

3 days

Tue 29/08/23

Thu 31/08/23

317

319

Service Rough in

2 days

Fri 1/09/23

Mon 4/09/23

320

Electrical services

2 days

Fri 1/09/23

Mon 4/09/23

318

321

Mechanical services

2 days

Fri 1/09/23

Mon 4/09/23

318

322

Hydraulic services

2 days

Fri 1/09/23

Mon 4/09/23

318

323

Internal lining

3 days

Tue 5/09/23

Thu 7/09/23

322

324

Fit-off stage

10 days

Fri 8/09/23

Thu 21/09/23

325

Install joinery

5 days

Fri 8/09/23

Thu 14/09/23

323

326

Install sanitation items

5 days

Fri 8/09/23

Thu 14/09/23

323

327

Install wall and floor tiling in wet area

5 days

Fri 8/09/23

Thu 14/09/23

323

328

Install floor covering

5 days

Fri 8/09/23

Thu 14/09/23

323

329

Install tactile

2 days

Fri 15/09/23

Mon 18/09/23

328

330

Install Line marking

3 days

Tue 19/09/23

Thu 21/09/23

329

331

Services fit-off

4 days

Fri 22/09/23

Wed 27/09/23

332

Electrical Services

4 days

Fri 22/09/23

Wed 27/09/23

324

333

Mechanical Services

4 days

Fri 22/09/23

Wed 27/09/23

324

334

Hydraulic services

4 days

Fri 22/09/23

Wed 27/09/23

324

335

Painting

2 days

Thu 28/09/23

Fri 29/09/23

331

336

BUILDING 04 - CONSTRUCTION OF IRRIGATION WORKSHOP / STORAGE BUILDING

116 days

Mon 3/07/23

Tue 12/12/23

337

Preliminary Work

2 days

Mon 3/07/23

Tue 4/07/23

338

Site fencing / Mobilisation, SESC, Survey Setout, Establish TMP

1 day

Mon 3/07/23

Mon 3/07/23

339

Locate known existing services

1 day

Tue 4/07/23

Tue 4/07/23

338

340

Preliminary Civil works

1 day

Wed 5/07/23

Wed 5/07/23

339

341

Under Ground Services –

6 days

Thu 6/07/23

Thu 13/07/23

342

Elect and comms

3 days

Thu 6/07/23

Mon 10/07/23

340

343

Hydraulic

3 days

Tue 11/07/23

Thu 13/07/23

342

344

Building Pad

5 days

Fri 14/07/23

Thu 20/07/23

343

345

Block walls

5 days

Fri 21/07/23

Thu 27/07/23

344

346

Erect Structural steel

5 days

Fri 28/07/23

Thu 3/08/23

345,97

347

Roof Sheetting

5 days

Mon 7/08/23

Fri 11/08/23

348

External Linings and Facades

5 days

Fri 4/08/23

Thu 10/08/23

349

Install Roof sheeting including roof plumbing

5 days

Fri 4/08/23

Thu 10/08/23

346

350

Install external windows, louvers and Roller doors

5 days

Fri 4/08/23

Thu 10/08/23

346

351

Install aluminium fencing

5 days

Fri 4/08/23

Thu 10/08/23

346

352

Internal Framing

3 days

Fri 11/08/23

Tue 15/08/23

351

353

Service Rough in

5 days

Wed 16/08/23

Tue 22/08/23

354

Electrical services

5 days

Wed 16/08/23

Tue 22/08/23

352

355

Mechanical services

5 days

Wed 16/08/23

Tue 22/08/23

352

356

Hydraulic services

5 days

Wed 16/08/23

Tue 22/08/23

352

357

Internal lining

1 day

Wed 23/08/23

Wed 23/08/23

353

358

Ceiling & Plaster

5 days

Mon 14/08/23

Fri 18/08/23

347

359

Services fit-off

59 days

Tue 18/07/23

Mon 9/10/23

360

Electrical Services

35 days

Tue 18/07/23

Mon 9/09/23

358

361

Mechanical Services

35 days

Mon 21/08/23

Mon 9/10/23

358

362

Hydraulic services

35 days

Mon 21/08/23

Mon 9/10/23

358

363

Painting

5 days

Tue 10/10/23

Mon 16/10/23

359

364

Completion

4 days

Thu 7/12/23

Tue 12/12/23

365

Site Demobilisation

1 day

Thu 7/12/23

Thu 7/12/23

363,400

366

QA, As constructed, O&M manual

3 days

Fri 8/12/23

Tue 12/12/23

365

367

Practical Completion

0 days

Tue 12/12/23

Tue 12/12/23

366

368

EXTENT OF FLEXIBLE HARDSTAND AREA

67 days?

Tue 5/09/23

Thu 7/12/23

369

Subgrade Preparation

22 days

Tue 5/09/23

Thu 5/10/23

370

Remove Unwanted material and make replace if required

6 days

Tue 5/09/23

Tue 12/09/23

161FS+20 days

371

Apply Moisture and Roll Disturb Soil

2 days

Wed 13/09/23

Thu 14/09/23

370

372

HOLD POINT – Subgrade Inspection

1 day

Fri 15/09/23

Fri 15/09/23

371

373

EOT 003 (6 Days)

13 days

Mon 18/09/23

Thu 5/10/23

372

374

Sub-Base Course Preparation – 125mm thick, TMR TYPE 2.3

7 days

Fri 6/10/23

Mon 16/10/23

375

Prepare and place Sub-Base materials

4 days

Fri 6/10/23

Wed 11/10/23

373

376

Level and trim

3 days

Thu 12/10/23

Mon 16/10/23

375

377

Construction quality testing

0 days

Mon 16/10/23

Mon 16/10/23

376

378

HOLD POINT – Proof Roll Lot Conformance

0 days

Mon 16/10/23

Mon 16/10/23

377

379

Base Course Preparation – 125mm thick, TMR Type 2.1

7 days?

Tue 17/10/23

Wed 25/10/23

378

380

Prepare and place Base Coarse materials

4 days

Tue 17/10/23

Fri 20/10/23

378

381

Level and trim

1 day

Mon 23/10/23

Mon 23/10/23

380

382

Construction quality testing

1 day?

Tue 24/10/23

Tue 24/10/23

381

383

HOLD POINT – Proof Roll Lot Conformance

1 day?

Wed 25/10/23

Wed 25/10/23

382

384

Install Kerb and Channel

19 days

Mon 2/10/23

Fri 27/10/23

385

Survey Setout – Kerb alignment / drainage outlets

2 days

Mon 23/10/23

Tue 24/10/23

380

386

Installation of Concrete Kerb

2 days

Mon 2/10/23

Thu 26/10/23

385

387

Complete hand-pour

1 day

Fri 27/10/23

Fri 27/10/23

386

388

Hardstand to Potting Shed End

26 days

Mon 16/10/23

Mon 20/11/23

389

Sub Grade Excavation and Prep

5 days

Mon 16/10/23

Fri 20/10/23

378FS+1 day

390

EOT 004 (9 Days)

9 days

Mon 23/10/23

Thu 2/11/23

389

391

Proof Roll

0 days

Thu 2/11/23

Thu 2/11/23

390

392

Sub-Base

3 days

Fri 3/11/23

Tue 7/11/23

391

393

Base Course

4 days

Wed 8/11/23

Mon 13/11/23

392

394

Kerb

2 days

Tue 14/11/23

Wed 15/11/23

393

395

Base Course (outer)

3 days

Thu 16/11/23

Mon 20/11/23

394

396

Wearing Course

8 days

Tue 21/11/23

Thu 30/11/23

397

Pavement testing

1 day

Tue 21/11/23

Tue 21/11/23

395

398

Prime Seal

2 days

Mon 27/11/23

Tue 28/11/23

395FS+4 days

399

Lay 35mm of DG10 Asphalt materials

2 days

Wed 29/11/23

Thu 30/11/23

398

400

Apply line marking

3 days

Mon 4/12/23

Wed 6/12/23

399FS+1 day

401

Install Signage

1 day

Thu 7/12/23

Thu 7/12/23

400

402

Completion

10 days

Fri 8/12/23

Thu 21/12/23

403

Final Site Inspections - Client

1 day

Fri 8/12/23

Fri 8/12/23

401

404

Defects and Demob

5 days

Mon 11/12/23

Fri 15/12/23

403

405

QA, As constructed, O&M manual

10 days

Fri 8/12/23

Thu 21/12/23

401

406

Practical Completion

0 days

Fri 22/03/24

Fri 22/03/24

0,110,208,301,1

Wellington St Depot Upgrade Contract Program

11 March 2024

Task Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress

Page 3
