

ID	Task Name	Duration	Resource Names	Start	Finish	Predecessors	% Complete	Gantt Chart																											
198	Prep	1 day		Fri 5/08/22	Fri 5/08/22	170	0%																												
199	Fence Posts	1 day	About Time	Sat 6/08/22	Sat 6/08/22	198	0%																												
200	Soil and Mulch	1 day		Mon 8/08/22	Mon 8/08/22	199	0%																												
201	Fencing	2 days	About Time	Tue 9/08/22	Thu 11/08/22	200	0%																												
202	Planting	2 days		Fri 12/08/22	Sat 13/08/22	201	0%																												
203	Turf	1 day		Mon 15/08/22	Mon 15/08/22	202	0%																												
204	External Clean	2 days		Tue 16/08/22	Wed 17/08/22	203	0%																												
205	Garden Sheds	1 day	Fourward	Tue 16/08/22	Tue 16/08/22	203	0%																												
206	Line Marking	1 day	Brushfast	Thu 18/08/22	Thu 18/08/22	204	0%																												
207	Fitout	281 days		Mon 13/09/21	Fri 2/09/22		9%																												
208	Units 1-4	93 days		Tue 17/05/22	Fri 2/09/22		23%																												
209	Grind Floors	2 days	Proline	Thu 19/05/22	Fri 20/05/22		100%																												
210	Stackwork	4 days	Cahill	Tue 17/05/22	Fri 20/05/22	122	100%																												
211	Framing	5 days	Rotovated	Wed 25/05/22	Mon 30/05/22	210	100%																												
212	Joinery Measure	1 day	Corona	Wed 8/06/22	Wed 8/06/22	211	100%																												
213	Electrical Roughin	4 days	Focus	Tue 31/05/22	Fri 3/06/22	211	100%																												
214	Plumbing Roughin	4 days	Cahill	Tue 31/05/22	Wed 8/06/22	211	100%																												
215	Mechanical Roughin	1 day	Focus	Tue 31/05/22	Tue 31/05/22	211	100%																												
216	Ply Install	2 days	Rotovated	Thu 9/06/22	Fri 10/06/22	214	0%																												
217	Sheeting	4 days	Rotovated	Thu 7/07/22	Mon 11/07/22	213,214,137SS+2 c	0%																												
218	Setting and Cornice	5 days	Rotovated	Tue 12/07/22	Sat 16/07/22	217	0%																												
219	Texture Ceilings	5 days	Top Trade	Thu 14/07/22	Tue 19/07/22	218FS-3 days	0%																												
220	Entry Door	1 day	Bris Fire Doors	Mon 18/07/22	Mon 18/07/22	218	0%																												
221	Carpentry Fitout	3 days	Fourward	Wed 20/07/22	Fri 22/07/22	219	0%																												
222	Measure Robe Doors	1 day	Civic	Sat 23/07/22	Sat 23/07/22	221	0%																												
223	Measure Accordian Doors	1 day	Nileport	Sat 23/07/22	Sat 23/07/22	221	0%																												
224	Paint - Ceilings, Wall 1 Coat	4 days	Top Trade	Sat 23/07/22	Wed 27/07/22	221	0%																												
225	Waterproofing	2 days	Concrete Seal	Thu 28/07/22	Fri 29/07/22	224	0%																												
226	Tiling	5 days	York	Sat 30/07/22	Thu 4/08/22	225	0%																												
227	Measure Shower Screens	1 day	Civic	Fri 5/08/22	Fri 5/08/22	226	0%																												
228	Joinery	4 days	Corona	Thu 28/07/22	Mon 1/08/22	224	0%																												
229	Tile Splashbacks	1 day	York	Tue 2/08/22	Tue 2/08/22	228	0%																												
230	Final Paint	4 days	Top Trade	Fri 5/08/22	Tue 9/08/22	226,228	0%																												
231	Electrical Fitoff	4 days	Focus	Thu 11/08/22	Mon 15/08/22	230	0%																												
232	Plumbing Fitoff	4 days	Cahill	Thu 11/08/22	Mon 15/08/22	230	0%																												
233	Ancillary Fitoff	2 days	Fourward	Thu 11/08/22	Fri 12/08/22	230	0%																												
234	NBN Install	1 day	Ventia	Sat 20/08/22	Sat 20/08/22	230,304SS	0%																												
235	Builders Clean	1 day		Tue 16/08/22	Tue 16/08/22	231,232,233	0%																												
236	Robe Doors	1 day	Civic	Wed 17/08/22	Wed 17/08/22	235	0%																												
237	Accordion Doors	1 day	Fourward	Wed 17/08/22	Wed 17/08/22	235	0%																												

Project: Quentin Street Capalaba Site

Date: Tue 14/06/22

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Progress

Deadline

Page 3

ID	Task Name	Duration	Resource Names	Start	Finish	Predecessors	% Complete	6 Jun '22							13 Jun '22							20 Jun '22							27 Jun '22							4 Jul '22							11 Jul '22								
								M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M								
238	Shower Screens	1 day	Civic	Wed 17/08/22	Wed 17/08/22	235	0%																																												
239	Vinyl Install	3 days	Comflor	Wed 17/08/22	Fri 19/08/22	235	0%																																												
240	Carpet Install	1 day	Comflor	Sat 20/08/22	Sat 20/08/22	239	0%																																												
241	Clothslines	1 day	Sunni	Mon 22/08/22	Mon 22/08/22	239,240	0%																																												
242	Defects	2 days		Mon 22/08/22	Tue 23/08/22	239,240	0%																																												
243	Door Closers Ect	1 day	Bris Fire Doors	Mon 22/08/22	Mon 22/08/22	239,240	0%																																												
244	Final Clean	1 day		Wed 24/08/22	Wed 24/08/22	242	0%																																												
245	Curtains	1 day	Fourward	Fri 2/09/22	Fri 2/09/22	244,315SS	0%																																												
246	Fit Crimsafe Screens	1 day	Dowell	Fri 2/09/22	Fri 2/09/22	316SS	0%																																												
247	Units 5-8	59 days		Sat 25/06/22	Fri 2/09/22		0%																																												
248	Framing	3 days	Rotovated	Sat 25/06/22	Tue 28/06/22	134,129,130	0%																																												
249	Joinery Measure	1 day	Corona	Wed 29/06/22	Wed 29/06/22	248	0%																																												
250	Electrical Roughin	4 days	Focus	Thu 7/07/22	Mon 11/07/22	137SS+2 days	0%																																												
251	Plumbing Roughin	4 days	Cahill	Thu 7/07/22	Mon 11/07/22	137SS+2 days	0%																																												
252	Mechanical Roughin	1 day	Focus	Sat 9/07/22	Sat 9/07/22	137SS+4 days	0%																																												
253	Sheeting	4 days	Rotovated	Tue 12/07/22	Fri 15/07/22	250,251,252,217	0%																																												
254	Setting and Cornice	5 days	Rotovated	Sat 16/07/22	Thu 21/07/22	253	0%																																												
255	Entry Door	1 day	Bris Fire Doors	Fri 22/07/22	Fri 22/07/22	254	0%																																												
256	Carpentry Fitout	3 days	Fourward	Sat 23/07/22	Tue 26/07/22	254,221	0%																																												
257	Measure Robe Doors	1 day	Civic	Wed 27/07/22	Wed 27/07/22	256	0%																																												
258	Measure Accordion Doors	1 day	Nileport	Wed 27/07/22	Wed 27/07/22	256	0%																																												
259	Paint - Ceilings, Wall 1 Coat	4 days	Top Trade	Wed 27/07/22	Sat 30/07/22	256	0%																																												
260	Waterproofing	2 days	Concrete Seal	Mon 1/08/22	Tue 2/08/22	259	0%																																												
261	Tiling	5 days	York	Fri 5/08/22	Thu 11/08/22	260,226	0%																																												
262	Measure Shower Screens	1 day	Civic	Fri 12/08/22	Fri 12/08/22	261	0%																																												
263	Joinery	4 days	Corona	Mon 1/08/22	Thu 4/08/22	259	0%																									</																			

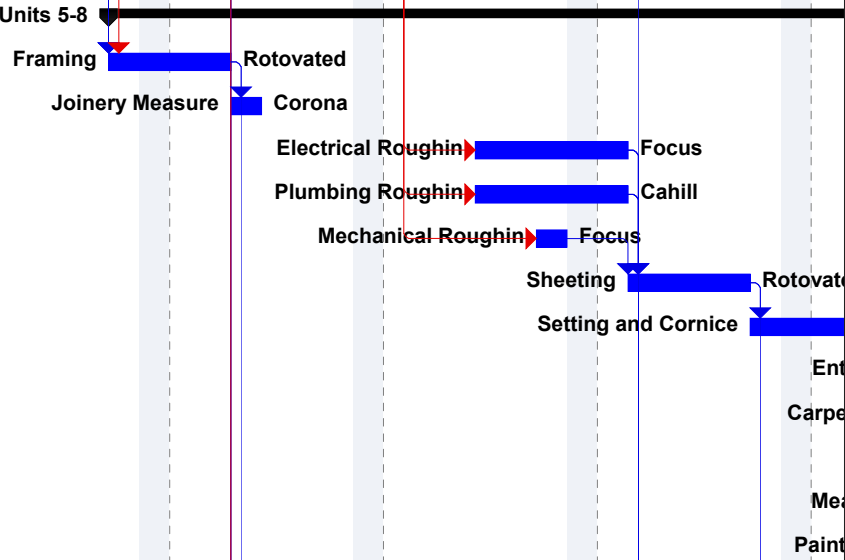

Project: Quentin Street Capalaba Site
Date: Tue 14/06/22

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Progress

Deadline

Page 4

