


		Name	Duration	Start	Finish	Predecessors	Resource Names	21 Nov
								S M
1		Back yard project	45.4 days?	24/11/21 8:00 AM	25/01/22 3:00 PM			
2		design	1.6 days	24/11/21 8:00 AM	25/11/21 5:00 PM		Nigel phillips (project manag...	
3		site preperation ...	9.9 days?	4/12/21 2:00 PM	16/12/21 5:00 PM			
4		demolition	6.7 days	4/12/21 2:00 PM	12/12/21 5:00 PM			
5		remove old bird...	1.1 days	4/12/21 2:00 PM	5/12/21 5:00 PM	2	Steven adamson (owner)	
6		remove old edg...	1 day	11/12/21 9:00 AM	12/12/21 11:00 AM	5	Steven adamson (owner)	
7		remove rubbish	4.5 days	7/12/21 11:00 AM	12/12/21 5:00 PM		Steven adamson (owner);ru...	
8		order materials	0.8 days	6/12/21 8:00 AM	6/12/21 5:00 PM	2FF	Nigel phillips (project manag...	
9		level site	0.8 days	13/12/21 8:00 AM	13/12/21 5:00 PM	6	Neil Hole (mini dig SEQ);Nig...	
10		install drainage	0.6 days	14/12/21 8:00 AM	14/12/21 3:00 PM	6;9	Nigel phillips (project manag...	
11		install electrical (u...	0.4 days	9/12/21 8:00 AM	15/12/21 5:00 PM		Nigel phillips (project manag...	
12		Footings	1.6 days?	15/12/21 8:00 AM	16/12/21 5:00 PM			
13		dig footing (mini...	0.8 days	15/12/21 8:00 AM	15/12/21 5:00 PM	9	Neil Hole (mini dig SEQ);Nig...	
14		concrete footings	0.8 days?	16/12/21 8:00 AM	16/12/21 5:00 PM	13	concrete ;Nigel phillips (proj...	
15		construction (sta...	28.6 days?	17/12/21 8:00 AM	25/01/22 3:00 PM			
16		delivery of bric...	1.6 days	17/12/21 8:00 AM	18/12/21 5:00 PM			
17		relocation of bri...	1.6 days	17/12/21 8:00 AM	18/12/21 5:00 PM		Steven adamson (owner)	
18		brick walls	6.4 days?	5/01/22 8:00 AM	12/01/22 5:00 PM			
19		bricking of wall	2.4 days?	5/01/22 8:00 AM	7/01/22 5:00 PM	14	Nigel phillips (project manag...	
20		rendering of wall	1.4 days?	10/01/22 8:00 AM	11/01/22 3:00 PM	19	sand & cerment ;Nigel phillip...	
21		painting of wall	0.8 days?	12/01/22 8:00 AM	12/01/22 5:00 PM	20	Steven adamson (owner);p...	
22		edgeing	2.4 days	7/01/22 8:00 AM	9/01/22 5:00 PM	14	Nigel phillips (project manag...	
23		pavers	1.6 days	13/01/22 8:00 AM	14/01/22 5:00 PM		Nigel phillips (project manag...	
24		timber shade r...	3.6 days	13/01/22 1:00 PM	17/01/22 5:00 PM			
25		install timber ba...	1.2 days	13/01/22 1:00 PM	14/01/22 5:00 PM	20	timber & consumables ;Nigel...	
26		paint timber bat...	1.1 days	15/01/22 2:00 PM	16/01/22 5:00 PM	25	paint ;Steven adamson (ow...	
27		install shed cloth	0.4 days	17/01/22 12:00 PM	17/01/22 5:00 PM	26	Nigel phillips (project manag...	
28		seating	2.4 days	18/01/22 8:00 AM	20/01/22 5:00 PM			
29		install timber se...	1.5 days	18/01/22 8:00 AM	19/01/22 4:00 PM		timber & consumables ;Nigel...	

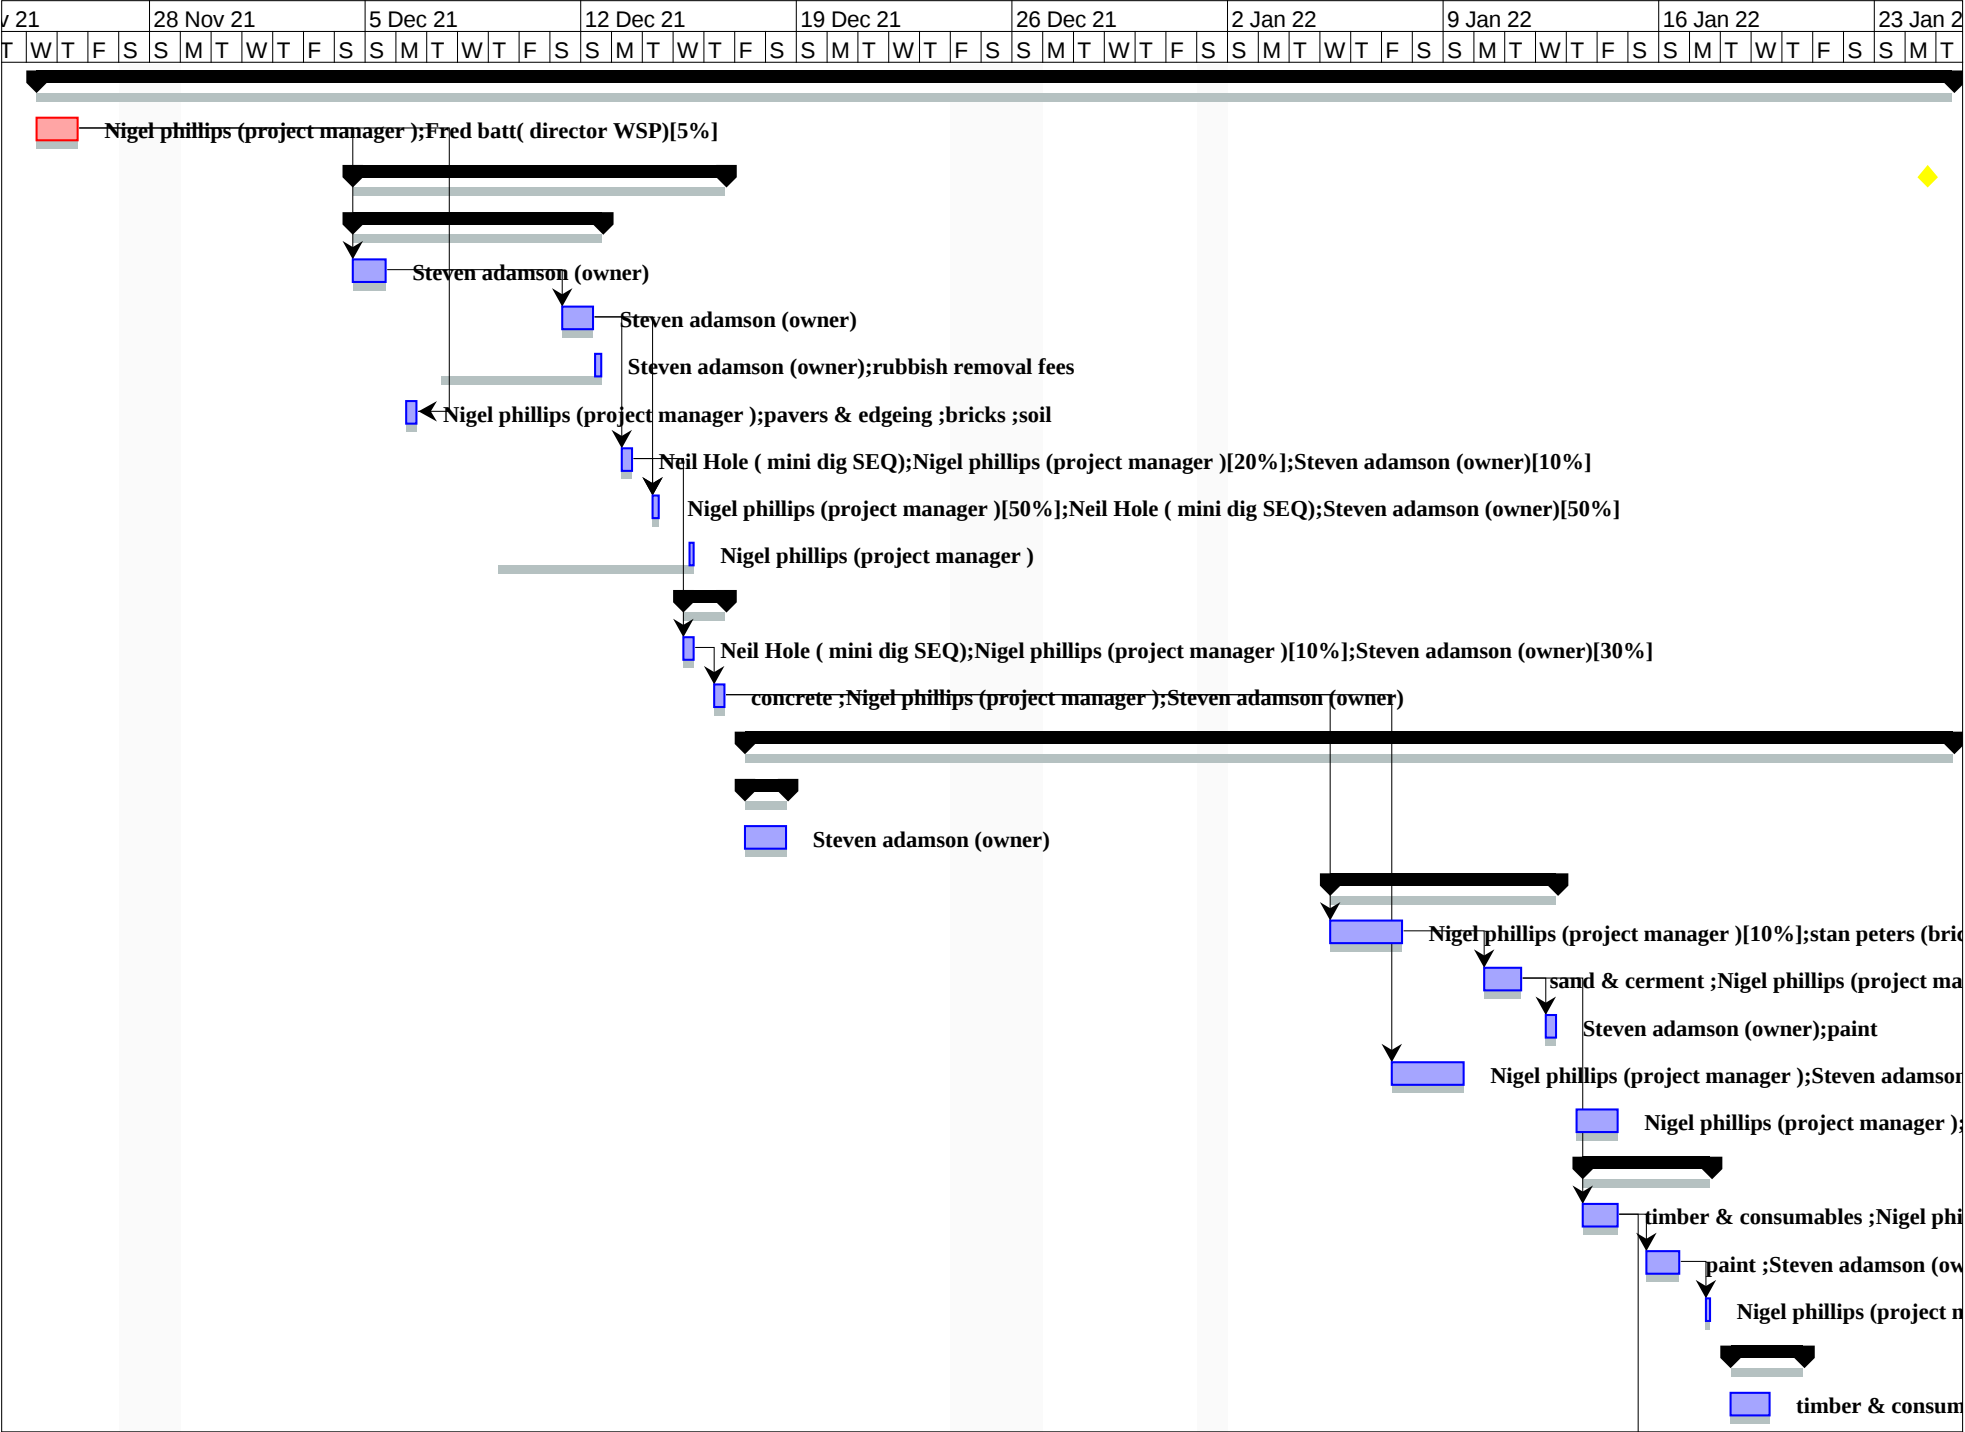

2				30 Jan 22				6 Feb 22				13 Feb 22				20 Feb 22													
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T
</																													

		Name	Duration	Start	Finish	Predecessors	Resource Names	21 Nov
								S M
30		seal/ paint timb...	0.8 days	20/01/22 8:00 AM	20/01/22 5:00 PM		paint ;Steven adamson (ow...	
31		gardens and la...	3.782 days	20/01/22 8:00 AM	24/01/22 2:49 PM			
32		back fill soil in g...	0.8 days	20/01/22 8:00 AM	20/01/22 5:00 PM		soil ;Nigel phillips (project m...	
33		install turf	2.4 days	21/01/22 8:00 AM	23/01/22 5:00 PM		turf;Nigel phillips (project m...	
34		plant gadens	1.982 days	22/01/22 10:00 AM	24/01/22 2:49 PM		plants ;Steven adamson (o...	
35		project comple...	0.9 days	24/01/22 2:00 PM	25/01/22 3:00 PM			
36		remove all rubbi...	0.3 days	24/01/22 2:00 PM	24/01/22 5:00 PM		rubbish removal fees	
37		review with ow...	0.6 days	25/01/22 8:00 AM	25/01/22 3:00 PM	36	Fred batt(director WSP)[20...	
38		lighting ad pow...	0.8 days	15/01/22 8:00 AM	15/01/22 5:00 PM			
39		lighting and po...	0.8 days	15/01/22 8:00 AM	15/01/22 5:00 PM	25	Lighting and poweroutlet ;Ni...	

21 Nov 21					28 Nov 21					5 Dec 21					12 Dec 21					19 Dec 21					26 Dec 21					2 Jan 22					9 Jan 22					16 Jan 22					23 Jan 22		
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T					
																																										paint ;Steven					
																																										soil ;Nigel phi					
																																										turf;					
																																										p					
																																										r					
																																										Lighting and poweroutlet ;Nig					

