



CMA Slab Checklist

Conducted on

28/4/20, 4:37 pm

Prepared by

Rik Chetcuti

Location

Score

3/3 - 100%

Completed on

28/4/20, 5:05 pm

Audit - 3/3 - 100%

Question	Response	Details
	28/4/20, 4:38 pm	
Termite protection installed run pipes inside of slab?	Yes	
 Appendix 1  Appendix 2  Appendix 3  Appendix 4		
Provide photos of termite collars installed to slab/penetrations.		
STA Inspection passed?	Yes	
Are Pier(s) applicable to this job?	Yes	
Are Piers clear of any loose dirt/debris to bottom?	Yes	
Please provide photo(s) of free and clear pier(s).		
 Appendix 5		
All measurements checked?	Yes	
Board generally looking straight?	Yes	
Is there an internal A/C unit that needs a pipe?	No	
Earth bar installed?	Yes	
Please provide photo of installed earth bar.		




Appendix 6

Is there cladded walls to this job?	No	
Are point loads clear of waffle pods under? (Point loads are located under steel posts etc)	Yes	
Zero boundary wall correct height?	Yes	
Recessed sliding doors timber in place?	No	
Recessed shower timber in place?	No	
Are all plumbing pipes free and clear of brick rebate/external boxing?	Yes	
Recessed garage floor timber in place?	No	
Is there any downpipe that needs to come through the slab? I.e - In alfresco or portico areas	No	
Is the silt fence installed, site bin & building sign done?	Yes	

Provide 1 clear photo of block with above installed/delivered.



Appendix 7

	Josh Casey	28/4/20 5:04 pm	
--	------------	--------------------	---

Media



Appendix 1




Appendix 2



Appendix 3



Appendix 4

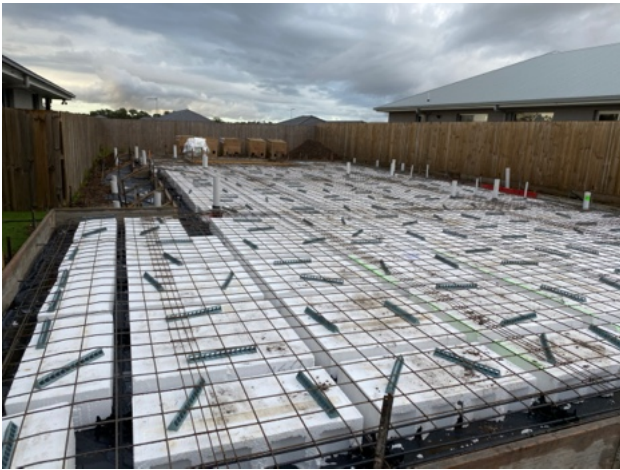

Appendix 5



Appendix 6



Appendix 7
