PM Course -
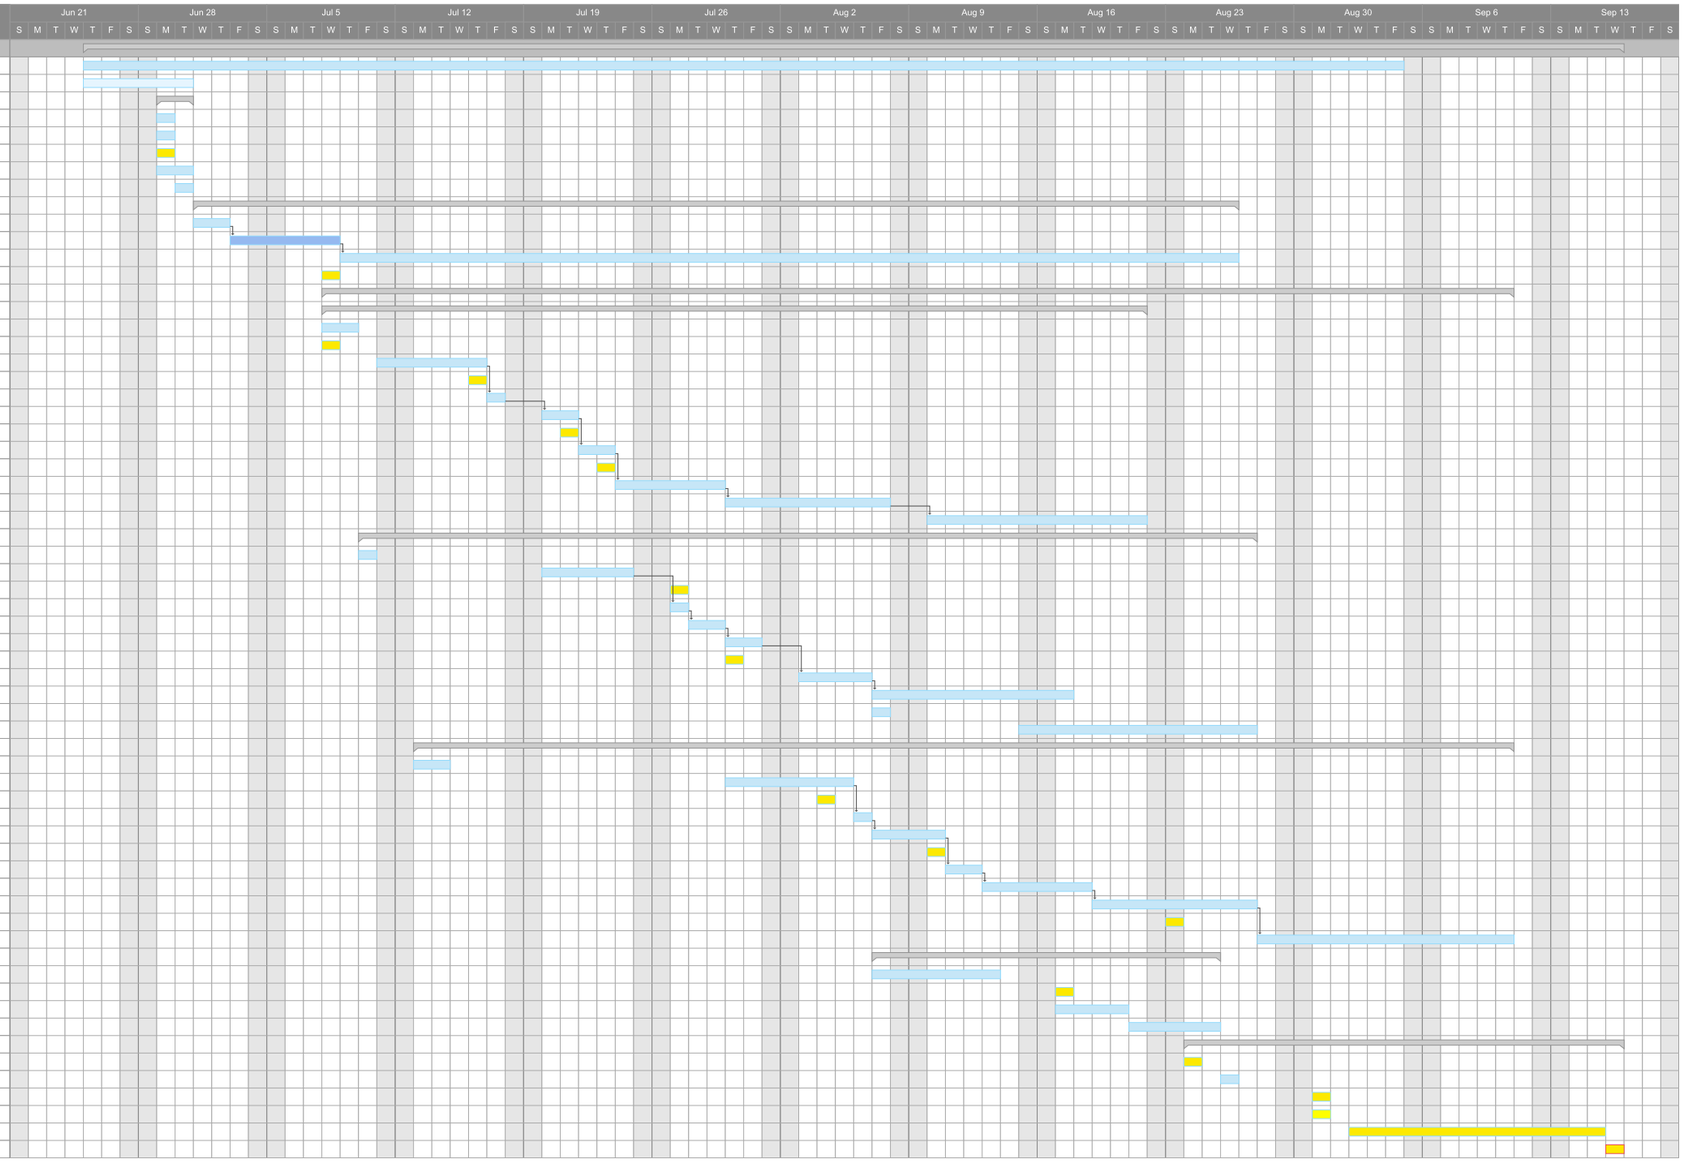
	Task Name	Duration	Start	Finish	Predecessors	% Complete	Status
1	KINGSGATE OFFICES RESTORATION	60d	25/06/20	16/09/20			Not Started
2	Project Summary	52d	25/06/20	04/09/20			
3	Project Initiation	4d	25/06/20	30/06/20			
4	Pre-Restoration	2d	29/06/20	30/06/20			
5	Obtain approvals	1d	29/06/20	29/06/20			
6	Project Pre-Start Moisture Survey	1d	29/06/20	29/06/20			
7	Weekly Site Meeting	1d	29/06/20	29/06/20			
8	Moisture survey report and submit	2d	29/06/20	30/06/20			
9	Site Set Up - Containment & Signage	1d	30/06/20	30/06/20			
10	PHASE 1 - Contents - All offices	41d	01/07/20	26/08/20			
11	Contents Removal	2d	01/07/20	02/07/20			
12	Contents Inventory & Restoration	4d	03/07/20	08/07/20	11		
13	Contents Storage	35d	09/07/20	26/08/20	12		
14	Project Management Meeting	1d	08/07/20	08/07/20			
15	PHASE 2 - Restoration Works	47d	08/07/20	10/09/20			
16	Office 1	33d	08/07/20	21/08/20			
17	Electrical Isolations	2d	08/07/20	09/07/20			
18	Weekly Site Meeting	1d	08/07/20	08/07/20			
19	Building Materials Removal	5d	11/07/20	16/07/20			
20	Project Management Meeting	1d	16/07/20	16/07/20			
21	Material Disposal	1d	17/07/20	17/07/20	19		
22	Primary Clean - Bulk Materials	2d	20/07/20	21/07/20	21		
23	Project Management Meeting	1d	21/07/20	21/07/20			
24	Secondary Clean - Remediation	2d	22/07/20	23/07/20	22		
25	Weekly Site Meeting	1d	23/07/20	23/07/20			
26	AFD Cycle	4d	24/07/20	29/07/20	24		
27	IEP Testing	7d	30/07/20	07/08/20	26		
28	Structural Drying	10d	10/08/20	21/08/20	27		
29	Office 2	35d	10/07/20	27/08/20			
30	Electrical Isolations	1d	10/07/20	10/07/20			
31	Building Materials Removal	5d	20/07/20	24/07/20			
32	Project Management Meeting	1d	27/07/20	27/07/20			
33	Material Disposal	1d	27/07/20	27/07/20	31		
34	Primary Clean - Bulk Materials	2d	28/07/20	29/07/20	33		
35	Secondary Clean - Remediation	2d	30/07/20	31/07/20	34		
36	Weekly Site Meeting	1d	30/07/20	30/07/20			
37	AFD Cycle	4d	03/08/20	06/08/20	35		
38	IEP Testing	7d	07/08/20	17/08/20	37		
39	Weekly Site Meeting	1d	07/08/20	07/08/20			
40	Structural Drying	10d	15/08/20	27/08/20			
41	Office 3	44d	13/07/20	10/09/20			
42	Electrical Isolations	2d	13/07/20	14/07/20			
43	Building Materials Removal	5d	30/07/20	05/08/20			
44	Project Management Meeting	1d	04/08/20	04/08/20			
45	Material Disposal	1d	06/08/20	06/08/20	43		
46	Primary Clean - Bulk Materials	2d	07/08/20	10/08/20	45		
47	Project Management Meeting	1d	10/08/20	10/08/20			
48	Secondary Clean - Remediation	2d	11/08/20	12/08/20	46		
49	AFD Cycle	4d	13/08/20	18/08/20	48		
50	IEP Testing	7d	19/08/20	27/08/20	49		
51	Weekly Site Meeting	1d	23/08/20	23/08/20			
52	Structural Drying	10d	28/08/20	10/09/20	50		
53	PHASE 3 - Reinstatement Works	13d	07/08/20	25/08/20			
54	Gyprock Installation	5d	07/08/20	13/08/20			
55	Project Management Meeting	1d	17/08/20	17/08/20			
56	Electrical Installation	4d	17/08/20	20/08/20			
57	Skirtings, Fittings & Fixtures Installation	3d	21/08/20	25/08/20			
58	PHASE 4 - Project Handover & Closure	18d	24/08/20	16/09/20			
59	Project Management Final Site Meeting	1d	24/08/20	24/08/20			
60	Return Contents to Premises	1d	26/08/20	26/08/20			
61	Weekly Site Meeting	1d	31/08/20	31/08/20			
62	Site Meeting with Client & Loss Adjuster	1d	31/08/20	31/08/20			
63	Finalization Project Documentation	10d	02/09/20	15/09/20			
64	Project Handover	1d	16/09/20	16/09/20
