Annexure 7
Contractor Programme

ID	Task Mode	Task Name	Duration	Start	Finish	% Comp
1		ROCKPOOL_PELICAN WATERS	1 day?	Mon 21/02/22	Mon 21/02/22	0%
2		**AUTHORITY APPROVALS**	**207 days?**	**Mon 21/02/22**	**Thu 15/12/22**	**0%**
71		**EQUIPMENT**	**350 days**	**Mon 21/02/22**	**Thu 27/07/23**	**0%**
99		**CONSTRUCTION WORKS**	**271 days**	**Mon 27/06/22**	**Fri 4/08/23**	**0%**
100		**STRUCTURE**	**161 days**	**Mon 27/06/22**	**Fri 24/02/23**	**0%**
101		**Site Establishment**	**10 days**	**Mon 27/06/22**	**Fri 8/07/22**	**0%**
108		**Civil / Piling Works**	**50 days**	**Wed 29/06/22**	**Wed 7/09/22**	**0%**
109		Scrape & Stockpile Topsoil	6 days	Wed 29/06/22	Wed 6/07/22	0%
110		Cut to Fill	2 days	Thu 7/07/22	Fri 8/07/22	0%
111		**Building Footprint**	**40 days**	**Mon 11/07/22**	**Mon 5/09/22**	**0%**
112		install piling platform	4 days	Mon 11/07/22	Thu 14/07/22	0%
113		Platform certified	1 day	Fri 15/07/22	Fri 15/07/22	0%
114		Piling	25 days	Mon 1/08/22	Mon 5/09/22	0%
115		**Carparks / Surrounds**	**22 days**	**Mon 8/08/22**	**Wed 7/09/22**	**0%**
119		**STRUCTURE**	**124 days**	**Thu 18/08/22**	**Fri 24/02/23**	**0%**
120		**Footings**	**29 days**	**Thu 18/08/22**	**Tue 27/09/22**	**0%**
121		**Lift Core**	**10 days**	**Tue 30/08/22**	**Mon 12/09/22**	**0%**
122		Detailed Excavation Lift Core	1 day	Tue 30/08/22	Tue 30/08/22	0%
123		Blinding Slab	1 day	Wed 31/08/22	Wed 31/08/22	0%
124		Waterproofing	1 day	Thu 1/09/22	Thu 1/09/22	0%
125		FRP Lift Core Slab	3 days	Fri 2/09/22	Tue 6/09/22	0%
126		Blockworkwall [inc Core Fill]	1 day	Wed 7/09/22	Wed 7/09/22	0%
127		Waterproofing	2 days	Thu 8/09/22	Fri 9/09/22	0%
128		Backfill	1 day	Mon 12/09/22	Mon 12/09/22	0%
129		**North East Slab**	**13 days**	**Thu 18/08/22**	**Mon 5/09/22**	**0%**
130		Detailed Excavation Footings	8 days	Thu 18/08/22	Mon 29/08/22	0%
131		pile trimming	8 days	Fri 19/08/22	Tue 30/08/22	0%
132		FRP footings	8 days	Tue 23/08/22	Thu 1/09/22	0%
133		In Ground services	8 days	Thu 25/08/22	Mon 5/09/22	0%
134		**Central Slab**	**13 days**	**Tue 30/08/22**	**Thu 15/09/22**	**0%**
135		Detailed Excavation Footings	8 days	Tue 30/08/22	Thu 8/09/22	0%
136		pile trimming	8 days	Wed 31/08/22	Fri 9/09/22	0%
137		FRP footings	8 days	Fri 2/09/22	Tue 13/09/22	0%
138		In Ground services	8 days	Tue 6/09/22	Thu 15/09/22	0%
139		**South West Slab**	**13 days**	**Fri 9/09/22**	**Tue 27/09/22**	**0%**
140		Detailed Excavation Footings	8 days	Fri 9/09/22	Tue 20/09/22	0%
141		pile trimming	8 days	Mon 12/09/22	Wed 21/09/22	0%
142		FRP footings	8 days	Wed 14/09/22	Fri 23/09/22	0%
143		In Ground services	8 days	Fri 16/09/22	Tue 27/09/22	0%
144		**GF Slab on ground**	**32 days**	**Tue 6/09/22**	**Thu 20/10/22**	**0%**
145		**Pour 1**	**16 days**	**Tue 6/09/22**	**Tue 27/09/22**	**0%**
146		Scrape & Install Sand Layer	2 days	Tue 6/09/22	Wed 7/09/22	0%
147		Block Walls	10 days	Thu 8/09/22	Wed 21/09/22	0%
148		Perimeter Scaffold	5 days	Thu 8/09/22	Wed 14/09/22	0%
149		FRP Concrete Columns	5 days	Thu 8/09/22	Wed 14/09/22	0%
150		Plastic & Reo	2 days	Thu 22/09/22	Fri 23/09/22	0%
151		Set downs	1 day	Mon 26/09/22	Mon 26/09/22	0%
152		Cast in Services	1 day	Mon 26/09/22	Mon 26/09/22	0%
153		Pour	1 day	Tue 27/09/22	Tue 27/09/22	0%
154		**Pour 2**	**16 days**	**Fri 16/09/22**	**Mon 10/10/22**	**0%**
155		Scrape & Install Sand Layer	2 days	Fri 16/09/22	Mon 19/09/22	0%
156		Block Walls	10 days	Tue 20/09/22	Tue 4/10/22	0%
157		Perimeter Scaffold	5 days	Tue 20/09/22	Mon 26/09/22	0%
158		FRP Concrete Columns	5 days	Tue 20/09/22	Mon 26/09/22	0%
159		Plastic & Reo	2 days	Wed 5/10/22	Thu 6/10/22	0%
160		Set downs	1 day	Fri 7/10/22	Fri 7/10/22	0%
161		Cast in Services	1 day	Fri 7/10/22	Fri 7/10/22	0%
162		Pour	1 day	Mon 10/10/22	Mon 10/10/22	0%
163		**Pour 3**	**16 days**	**Wed 28/09/22**	**Thu 20/10/22**	**0%**
164		Scrape & Install Sand Layer	2 days	Wed 28/09/22	Thu 29/09/22	0%
165		Block Walls	10 days	Fri 30/09/22	Fri 14/10/22	0%
166		Perimeter Scaffold	5 days	Fri 30/09/22	Fri 7/10/22	0%
167		FRP Concrete Columns	5 days	Fri 30/09/22	Fri 7/10/22	0%
168		Plastic & Reo	2 days	Mon 17/10/22	Tue 18/10/22	0%
169		Set downs	1 day	Wed 19/10/22	Wed 19/10/22	0%
170		Cast in Services	1 day	Wed 19/10/22	Wed 19/10/22	0%
171		Pour	1 day	Thu 20/10/22	Thu 20/10/22	0%
172		**Level 1 Slab**	**23 days**	**Wed 28/09/22**	**Mon 31/10/22**	**0%**
173		**Pour 1**	**7 days**	**Wed 28/09/22**	**Fri 7/10/22**	**0%**
174		Formwork	4 days	Wed 28/09/22	Tue 4/10/22	0%
175		Reo	4 days	Fri 30/09/22	Thu 6/10/22	0%
176		Services	3 days	Tue 4/10/22	Thu 6/10/22	0%
177		Setdown	1 day	Thu 6/10/22	Thu 6/10/22	0%
178		Pour	1 day	Fri 7/10/22	Fri 7/10/22	0%
179		**Pour 2**	**7 days**	**Tue 11/10/22**	**Wed 19/10/22**	**0%**
180		Formwork	4 days	Tue 11/10/22	Fri 14/10/22	0%
181		Reo	4 days	Thu 13/10/22	Tue 18/10/22	0%
182		Services	3 days	Fri 14/10/22	Tue 18/10/22	0%
183		Setdown	1 day	Tue 18/10/22	Tue 18/10/22	0%
184		Pour	1 day	Wed 19/10/22	Wed 19/10/22	0%
185		**Pour 3**	**7 days**	**Fri 21/10/22**	**Mon 31/10/22**	**0%**
186		Formwork	4 days	Fri 21/10/22	Wed 26/10/22	0%
187		Reo	4 days	Tue 25/10/22	Fri 28/10/22	0%
188		Services	3 days	Wed 26/10/22	Fri 28/10/22	0%
189		Setdown	1 day	Fri 28/10/22	Fri 28/10/22	0%
190		Pour	1 day	Mon 31/10/22	Mon 31/10/22	0%
191		**Level 2 Slab**	**28 days**	**Mon 10/10/22**	**Wed 16/11/22**	**0%**
192		**Pour 1**	**12 days**	**Mon 10/10/22**	**Tue 25/10/22**	**0%**
193		Scaffold	2 days	Mon 10/10/22	Tue 11/10/22	0%
194		Blockwork	4 days	Tue 11/10/22	Fri 14/10/22	0%
195		FRP columns	2 days	Wed 12/10/22	Thu 13/10/22	0%
196		Formwork	4 days	Mon 17/10/22	Thu 20/10/22	0%
197		Reo	4 days	Wed 19/10/22	Mon 24/10/22	0%
198		Services	3 days	Thu 20/10/22	Mon 24/10/22	0%
199		Setdown	1 day	Mon 24/10/22	Mon 24/10/22	0%
200		Pour	1 day	Tue 25/10/22	Tue 25/10/22	0%
201		**Pour 2**	**12 days**	**Thu 20/10/22**	**Fri 4/11/22**	**0%**
202		Scaffold	2 days	Thu 20/10/22	Fri 21/10/22	0%
203		Blockwork	4 days	Fri 21/10/22	Wed 26/10/22	0%
204		FRP columns	2 days	Mon 24/10/22	Tue 25/10/22	0%
205		Formwork	4 days	Thu 27/10/22	Tue 1/11/22	0%
206		Reo	4 days	Mon 31/10/22	Thu 3/11/22	0%
207		Services	3 days	Tue 1/11/22	Thu 3/11/22	0%
208		Setdown	1 day	Thu 3/11/22	Thu 3/11/22	0%
209		Pour	1 day	Fri 4/11/22	Fri 4/11/22	0%
210		**Pour 3**	**12 days**	**Tue 1/11/22**	**Wed 16/11/22**	**0%**
211		Scaffold	2 days	Tue 1/11/22	Wed 2/11/22	0%
212		Blockwork	4 days	Wed 2/11/22	Mon 7/11/22	0%
213		FRP columns	2 days	Thu 3/11/22	Fri 4/11/22	0%

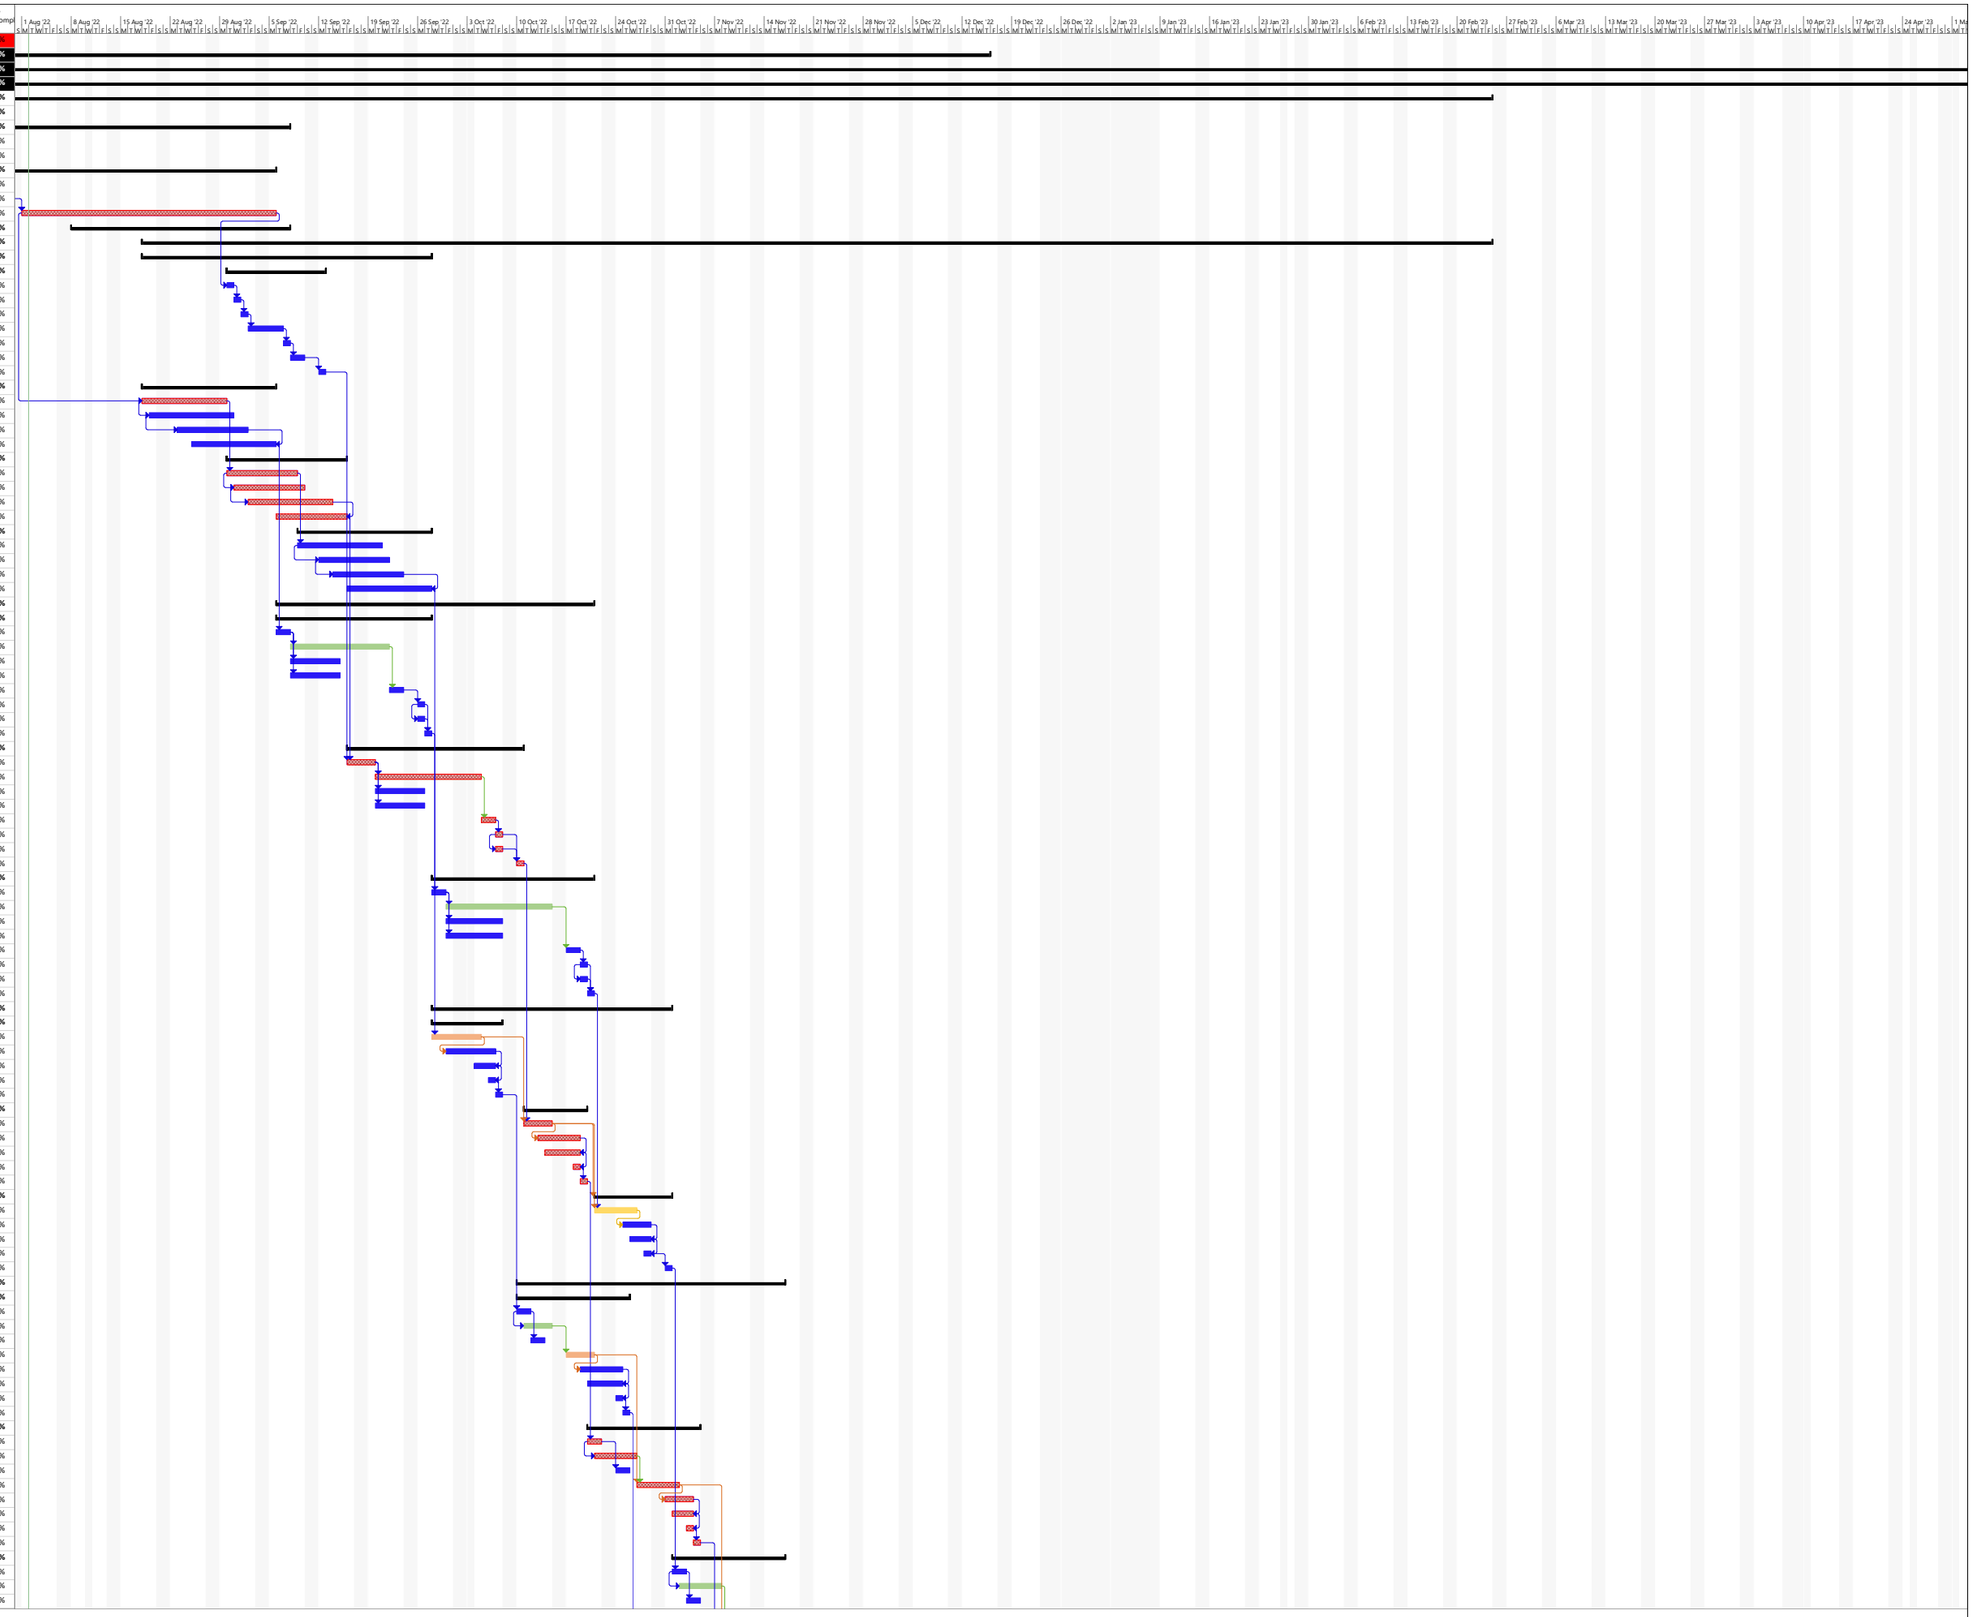

Project: Lowanna Beach Resort
Date: Tue 2/08/22

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress | Critical

ID	Task Mode	Task Name	Duration	Start	Finish	% Compl
214		Formwork	4 days	Tue 8/11/22	Fri 11/11/22	0%
215		Reo	4 days	Thu 10/11/22	Tue 15/11/22	0%
216		Services	3 days	Fri 11/11/22	Tue 15/11/22	0%
217		Setdown	1 day	Tue 15/11/22	Tue 15/11/22	0%
218		Pour	1 day	Wed 16/11/22	Wed 16/11/22	0%
219		**Level 3 Slab**	**28 days**	**Wed 26/10/22**	**Fri 2/12/22**	**0%**
220		**Pour 1**	**12 days**	**Wed 26/10/22**	**Thu 10/11/22**	**0%**
221		Scaffold	2 days	Wed 26/10/22	Thu 27/10/22	0%
222		Blockwork	4 days	Thu 27/10/22	Tue 1/11/22	0%
223		FRP columns	2 days	Fri 28/10/22	Mon 31/10/22	0%
224		Formwork	4 days	Wed 2/11/22	Mon 7/11/22	0%
225		Reo	4 days	Fri 4/11/22	Wed 9/11/22	0%
226		Services	3 days	Mon 7/11/22	Wed 9/11/22	0%
227		Setdown	1 day	Wed 9/11/22	Wed 9/11/22	0%
228		Pour	1 day	Thu 10/11/22	Thu 10/11/22	0%
229		**Pour 2**	**12 days**	**Mon 7/11/22**	**Tue 22/11/22**	**0%**
230		Scaffold	2 days	Mon 7/11/22	Tue 8/11/22	0%
231		Blockwork	4 days	Tue 8/11/22	Fri 11/11/22	0%
232		FRP columns	2 days	Wed 9/11/22	Thu 10/11/22	0%
233		Formwork	4 days	Mon 14/11/22	Thu 17/11/22	0%
234		Reo	4 days	Wed 16/11/22	Mon 21/11/22	0%
235		Services	3 days	Thu 17/11/22	Mon 21/11/22	0%
236		Setdown	1 day	Mon 21/11/22	Mon 21/11/22	0%
237		Pour	1 day	Tue 22/11/22	Tue 22/11/22	0%
238		**Pour 3**	**12 days**	**Thu 17/11/22**	**Fri 2/12/22**	**0%**
239		Scaffold	2 days	Thu 17/11/22	Fri 18/11/22	0%
240		Blockwork	4 days	Fri 18/11/22	Wed 23/11/22	0%
241		FRP columns	2 days	Mon 21/11/22	Tue 22/11/22	0%
242		Formwork	4 days	Thu 24/11/22	Tue 29/11/22	0%
243		Reo	4 days	Mon 28/11/22	Thu 1/12/22	0%
244		Services	3 days	Tue 29/11/22	Thu 1/12/22	0%
245		Setdown	1 day	Thu 1/12/22	Thu 1/12/22	0%
246		Pour	1 day	Fri 2/12/22	Fri 2/12/22	0%
247		**Level 4 Slab**	**28 days**	**Fri 11/11/22**	**Tue 20/12/22**	**0%**
248		**Pour 1**	**12 days**	**Fri 11/11/22**	**Mon 28/11/22**	**0%**
249		Scaffold	2 days	Fri 11/11/22	Mon 14/11/22	0%
250		Blockwork	4 days	Mon 14/11/22	Thu 17/11/22	0%
251		FRP columns	2 days	Tue 15/11/22	Wed 16/11/22	0%
252		Formwork	4 days	Fri 18/11/22	Wed 23/11/22	0%
253		Reo	4 days	Tue 22/11/22	Fri 25/11/22	0%
254		Services	3 days	Wed 23/11/22	Fri 25/11/22	0%
255		Setdown	1 day	Fri 25/11/22	Fri 25/11/22	0%
256		Pour	1 day	Mon 28/11/22	Mon 28/11/22	0%
257		**Pour 2**	**12 days**	**Wed 23/11/22**	**Thu 8/12/22**	**0%**
258		Scaffold	2 days	Wed 23/11/22	Thu 24/11/22	0%
259		Blockwork	4 days	Thu 24/11/22	Tue 29/11/22	0%
260		FRP columns	2 days	Fri 25/11/22	Mon 28/11/22	0%
261		Formwork	4 days	Wed 30/11/22	Mon 5/12/22	0%
262		Reo	4 days	Fri 2/12/22	Wed 7/12/22	0%
263		Services	3 days	Mon 5/12/22	Wed 7/12/22	0%
264		Setdown	1 day	Wed 7/12/22	Wed 7/12/22	0%
265		Pour	1 day	Thu 8/12/22	Thu 8/12/22	0%
266		**Pour 3**	**12 days**	**Mon 5/12/22**	**Tue 20/12/22**	**0%**
267		Scaffold	2 days	Mon 5/12/22	Tue 6/12/22	0%
268		Blockwork	4 days	Tue 6/12/22	Fri 9/12/22	0%
269		FRP columns	2 days	Wed 7/12/22	Thu 8/12/22	0%
270		Formwork	4 days	Mon 12/12/22	Thu 15/12/22	0%
271		Reo	4 days	Wed 14/12/22	Mon 19/12/22	0%
272		Services	3 days	Thu 15/12/22	Mon 19/12/22	0%
273		Setdown	1 day	Mon 19/12/22	Mon 19/12/22	0%
274		Pour	1 day	Tue 20/12/22	Tue 20/12/22	0%
275		**Level 5 Slab**	**28 days**	**Tue 29/11/22**	**Fri 20/01/23**	**0%**
276		**Pour 1**	**12 days**	**Tue 29/11/22**	**Wed 14/12/22**	**0%**
277		Scaffold	2 days	Tue 29/11/22	Wed 30/11/22	0%
278		Blockwork	4 days	Wed 30/11/22	Mon 5/12/22	0%
279		FRP columns	2 days	Thu 1/12/22	Fri 2/12/22	0%
280		Formwork	4 days	Tue 6/12/22	Fri 9/12/22	0%
281		Reo	4 days	Thu 8/12/22	Tue 13/12/22	0%
282		Services	3 days	Fri 9/12/22	Tue 13/12/22	0%
283		Setdown	1 day	Tue 13/12/22	Tue 13/12/22	0%
284		Pour	1 day	Wed 14/12/22	Wed 14/12/22	0%
285		**Pour 2**	**12 days**	**Fri 9/12/22**	**Tue 10/01/23**	**0%**
286		Scaffold	2 days	Fri 9/12/22	Mon 12/12/22	0%
287		Blockwork	4 days	Mon 12/12/22	Thu 15/12/22	0%
288		FRP columns	2 days	Tue 13/12/22	Wed 14/12/22	0%
289		Formwork	4 days	Fri 16/12/22	Wed 21/12/22	0%
290		Reo	4 days	Tue 20/12/22	Mon 9/01/23	0%
291		Services	3 days	Wed 21/12/22	Mon 9/01/23	0%
292		Setdown	1 day	Mon 9/01/23	Mon 9/01/23	0%
293		Pour	1 day	Tue 10/01/23	Tue 10/01/23	0%
294		**Pour 3**	**12 days**	**Wed 21/12/22**	**Fri 20/01/23**	**0%**
295		Scaffold	2 days	Wed 21/12/22	Thu 22/12/22	0%
296		Blockwork	4 days	Thu 22/12/22	Wed 11/01/23	0%
297		FRP columns	2 days	Mon 9/01/23	Tue 10/01/23	0%
298		Formwork	4 days	Thu 12/01/23	Tue 17/01/23	0%
299		Reo	4 days	Mon 16/01/23	Thu 19/01/23	0%
300		Services	3 days	Tue 17/01/23	Thu 19/01/23	0%
301		Setdown	1 day	Thu 19/01/23	Thu 19/01/23	0%
302		Pour	1 day	Fri 20/01/23	Fri 20/01/23	0%
303		**Level 6 Slab & Roof**	**40 days**	**Thu 15/12/22**	**Fri 24/02/23**	**0%**
304		**Pour 1**	**20 days**	**Thu 15/12/22**	**Fri 27/01/23**	**0%**
305		Scaffold	2 days	Thu 15/12/22	Fri 16/12/22	0%
306		Blockwork	4 days	Fri 16/12/22	Wed 21/12/22	0%
307		FRP columns	2 days	Mon 19/12/22	Tue 20/12/22	0%
308		**Stair Lid**	**4 days**	**Thu 22/12/22**	**Wed 11/01/23**	**0%**
309		Formwork	2 days	Thu 22/12/22	Mon 9/01/23	0%
310		Reo	1 day	Tue 10/01/23	Tue 10/01/23	0%
311		Pour	1 day	Wed 11/01/23	Wed 11/01/23	0%
312		Truss Install [inc Purlins]	4 days	Thu 12/01/23	Tue 17/01/23	0%
313		Safety Wire	2 days	Wed 18/01/23	Thu 19/01/23	0%
314		Sarking & Roof sheets	3 days	Fri 20/01/23	Tue 24/01/23	0%
315		Gutters	2 days	Wed 25/01/23	Fri 27/01/23	0%
316		**Pour 2**	**32 days**	**Wed 11/01/23**	**Fri 24/02/23**	**0%**
317		Scaffold	2 days	Wed 11/01/23	Thu 12/01/23	0%
318		Blockwork	4 days	Thu 12/01/23	Tue 17/01/23	0%
319		FRP columns	2 days	Fri 13/01/23	Mon 16/01/23	0%
320		**Plant Deck**	**7 days**	**Wed 18/01/23**	**Fri 27/01/23**	**0%**
321		Formwork	4 days	Wed 18/01/23	Mon 23/01/23	0%
322		Reo	2 days	Tue 24/01/23	Wed 25/01/23	0%

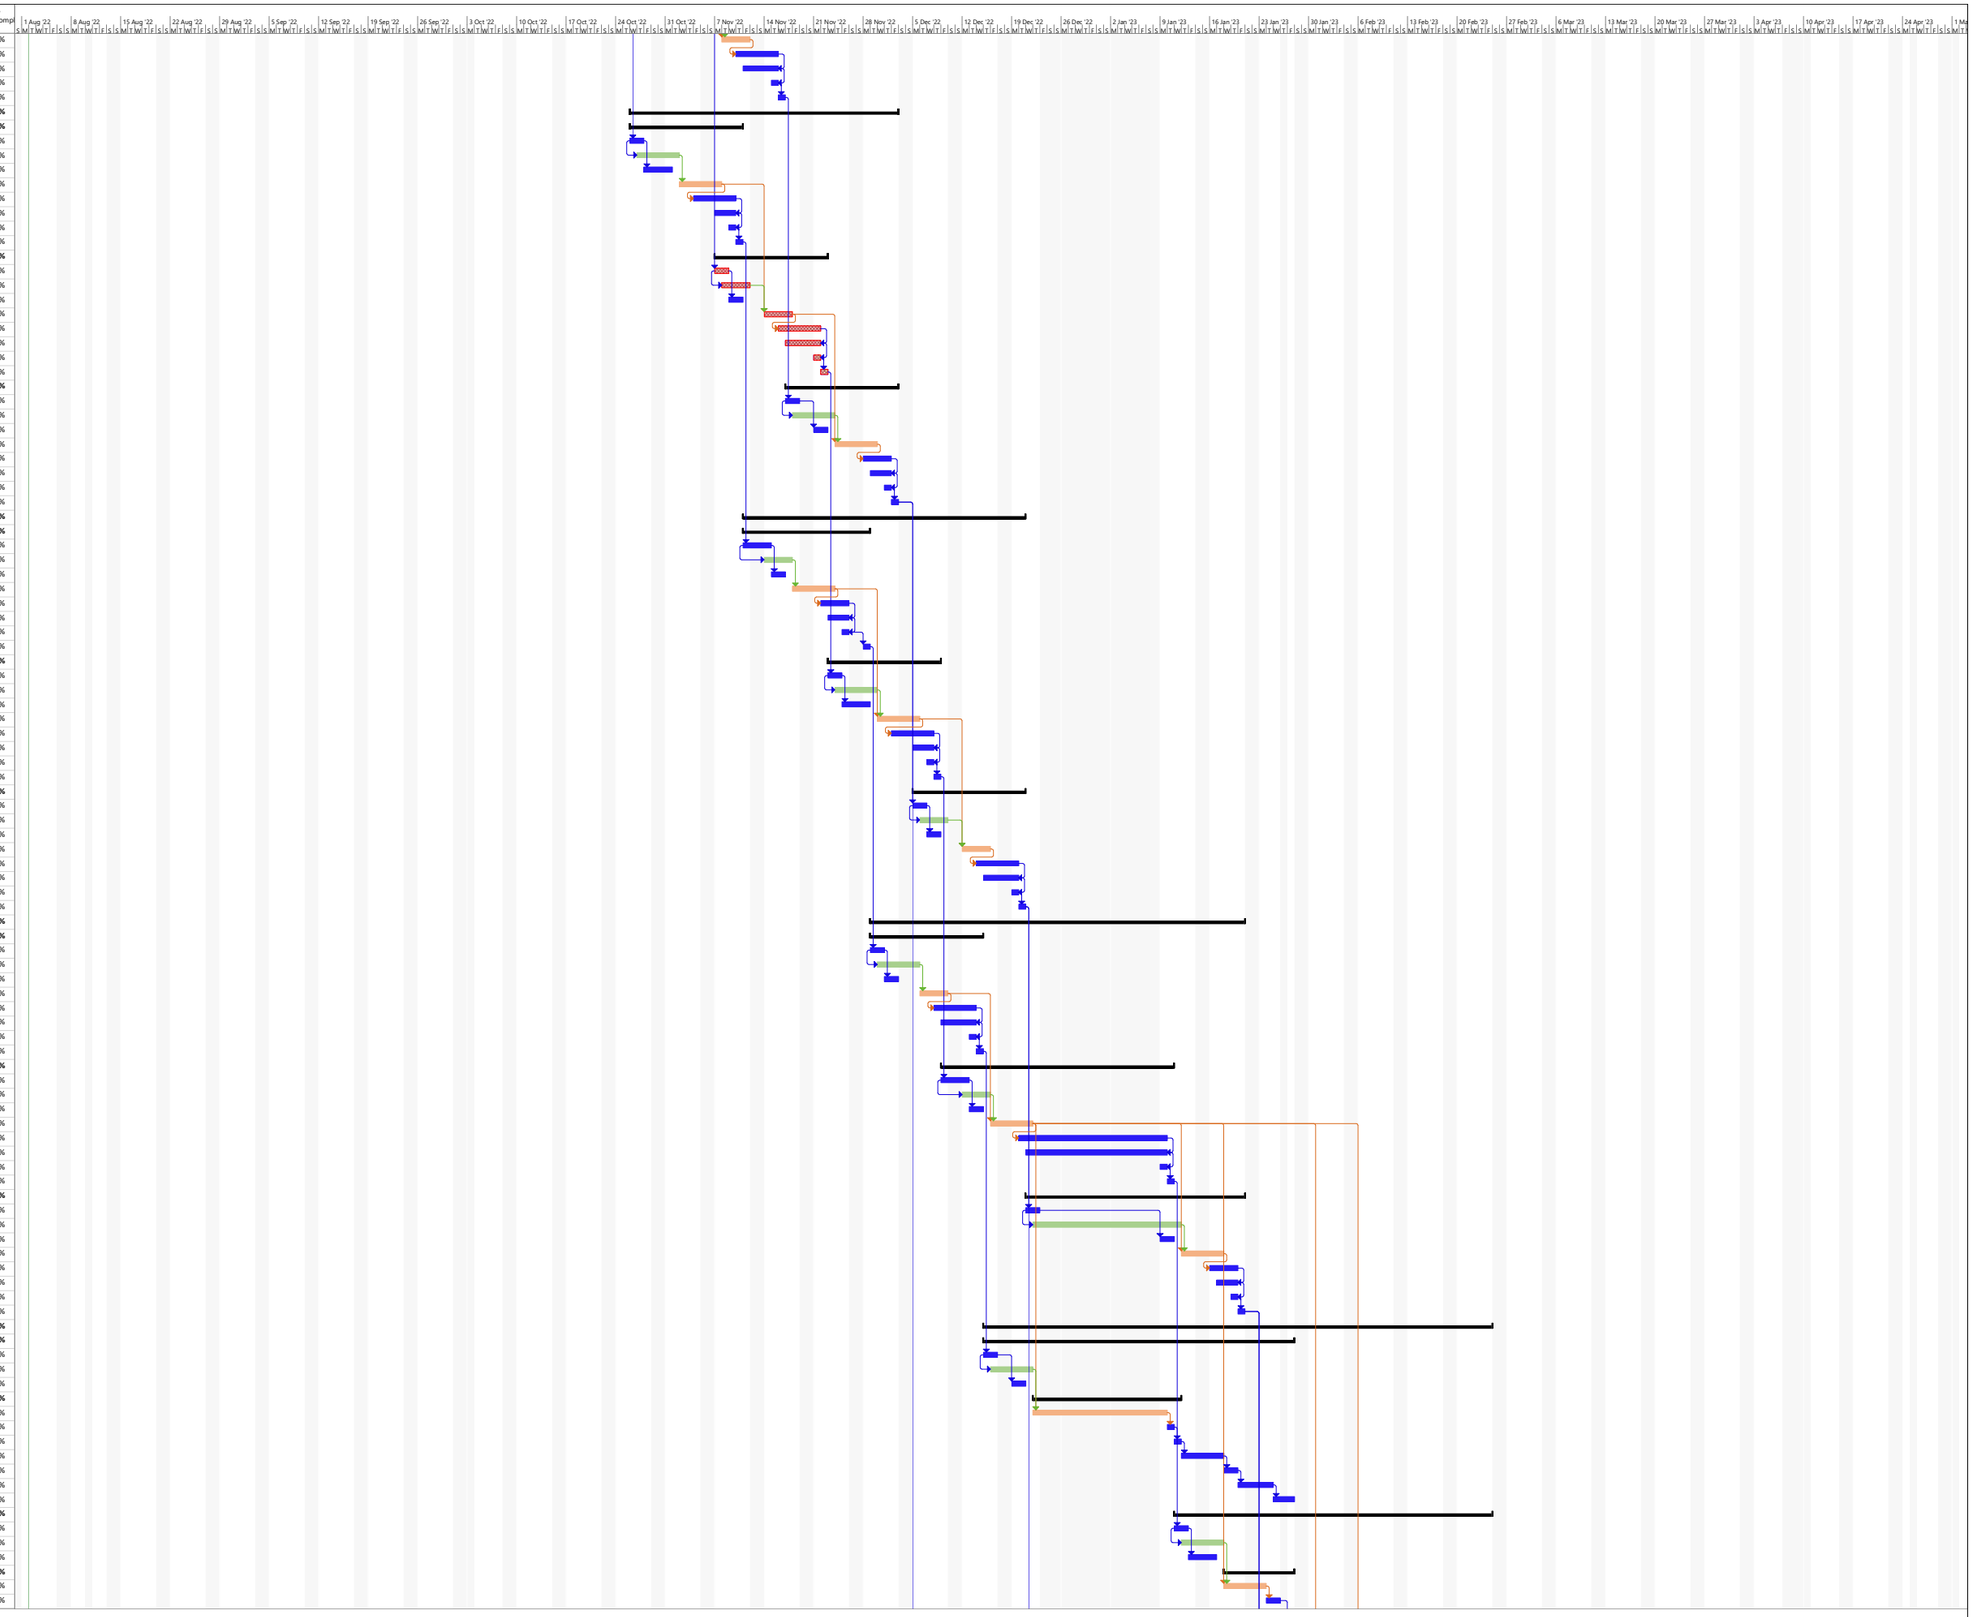

Project: Lowanna Beach Resort
Date: Tue 2/08/22

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress | Critical

ID	Task Mode	Task Name	Duration	Start	Finish	% Compl
323		Pour	1 day	Fri 27/01/23	Fri 27/01/23	0%
324		**Stair Lid & Lift Core Lid**	**20 days**	**Mon 30/01/23**	**Fri 24/02/23**	**0%**
325		Scaffold	2 days	Mon 30/01/23	Tue 31/01/23	0%
326		Blockwork	4 days	Tue 31/01/23	Fri 3/02/23	0%
327		Formwork	2 days	Mon 6/02/23	Tue 7/02/23	0%
328		Reo	1 day	Wed 8/02/23	Wed 8/02/23	0%
329		Pour	1 day	Thu 9/02/23	Thu 9/02/23	0%
330		Truss Install [inc Purlins]	4 days	Fri 10/02/23	Wed 15/02/23	0%
331		Safety Wire	2 days	Thu 16/02/23	Fri 17/02/23	0%
332		Sarking & Roof sheets	3 days	Mon 20/02/23	Wed 22/02/23	0%
333		Gutters	2 days	Thu 23/02/23	Fri 24/02/23	0%
334		**Pour 3**	**20 days**	**Mon 23/01/23**	**Mon 20/02/23**	**0%**
335		Scaffold	2 days	Mon 23/01/23	Tue 24/01/23	0%
336		Blockwork	4 days	Tue 24/01/23	Mon 30/01/23	0%
337		FRP columns	2 days	Wed 25/01/23	Fri 27/01/23	0%
338		**Stair Lid**	**15 days**	**Tue 31/01/23**	**Mon 20/02/23**	**0%**
339		Formwork	2 days	Tue 31/01/23	Wed 1/02/23	0%
340		Reo	1 day	Thu 2/02/23	Thu 2/02/23	0%
341		Pour	1 day	Fri 3/02/23	Fri 3/02/23	0%
342		Truss Install [inc Purlins]	4 days	Mon 6/02/23	Thu 9/02/23	0%
343		Safety Wire	2 days	Fri 10/02/23	Mon 13/02/23	0%
344		Sarking & Roof sheets	3 days	Tue 14/02/23	Thu 16/02/23	0%
345		Gutters	2 days	Fri 17/02/23	Mon 20/02/23	0%
346		**Formwork Stripping**	**44 days**	**Mon 5/12/22**	**Mon 20/02/23**	**0%**
347		GF	6 days	Mon 5/12/22	Mon 12/12/22	0%
348		Level 1	5 days	Wed 21/12/22	Wed 11/01/23	0%
349		Level 2	5 days	Mon 23/01/23	Mon 30/01/23	0%
350		Level 3	5 days	Tue 31/01/23	Mon 6/02/23	0%
351		level 4	5 days	Tue 7/02/23	Mon 13/02/23	0%
352		Level 5	5 days	Tue 14/02/23	Mon 20/02/23	0%
353		**FAÇADE**	**58 days**	**Tue 31/01/23**	**Mon 24/04/23**	**0%**
354		**Level 5 & 6**	**17 days**	**Tue 31/01/23**	**Wed 22/02/23**	**0%**
355		Render	6 days	Tue 31/01/23	Tue 7/02/23	0%
356		Paint [inc Caulk]	6 days	Thu 2/02/23	Thu 9/02/23	0%
357		**Fitoff**	**6 days**	**Mon 6/02/23**	**Mon 13/02/23**	**0%**
358		Downpipes	1 day	Fri 10/02/23	Fri 10/02/23	0%
359		Signage	2 days	Fri 10/02/23	Mon 13/02/23	0%
360		Balustrades	5 days	Mon 6/02/23	Fri 10/02/23	0%
361		Sunshades	5 days	Mon 6/02/23	Fri 10/02/23	0%
362		Vents	1 day	Fri 10/02/23	Fri 10/02/23	0%
363		Clean	2 days	Tue 14/02/23	Wed 15/02/23	0%
364		Builders Defects	1 day	Thu 16/02/23	Thu 16/02/23	0%
365		Defect Rectification	2 days	Fri 17/02/23	Mon 20/02/23	0%
366		Scaffold Drop	2 days	Tue 21/02/23	Wed 22/02/23	0%
367		**Level 4**	**17 days**	**Mon 13/02/23**	**Tue 7/03/23**	**0%**
368		Render	6 days	Mon 13/02/23	Mon 20/02/23	0%
369		Paint [inc Caulk]	6 days	Wed 15/02/23	Wed 22/02/23	0%
370		**Fitoff**	**6 days**	**Fri 17/02/23**	**Fri 24/02/23**	**0%**
376		Clean	2 days	Mon 27/02/23	Tue 28/02/23	0%
377		Builders Defects	1 day	Wed 1/03/23	Wed 1/03/23	0%
378		Defect Rectification	2 days	Thu 2/03/23	Fri 3/03/23	0%
379		Scaffold Drop	2 days	Mon 6/03/23	Tue 7/03/23	0%
380		**Level 3**	**17 days**	**Fri 24/02/23**	**Mon 20/03/23**	**0%**
381		Render	6 days	Fri 24/02/23	Fri 3/03/23	0%
382		Paint [inc Caulk]	6 days	Tue 28/02/23	Tue 7/03/23	0%
383		**Fitoff**	**6 days**	**Thu 2/03/23**	**Thu 9/03/23**	**0%**
384		Downpipes	1 day	Wed 8/03/23	Wed 8/03/23	0%
385		Signage	2 days	Wed 8/03/23	Thu 9/03/23	0%
386		Balustrades	5 days	Thu 2/03/23	Wed 8/03/23	0%
387		Sunshades	5 days	Thu 2/03/23	Wed 8/03/23	0%
388		Vents	1 day	Wed 8/03/23	Wed 8/03/23	0%
389		Clean	2 days	Fri 10/03/23	Mon 13/03/23	0%
390		Builders Defects	1 day	Tue 14/03/23	Tue 14/03/23	0%
391		Defect Rectification	2 days	Wed 15/03/23	Thu 16/03/23	0%
392		Scaffold Drop	2 days	Fri 17/03/23	Mon 20/03/23	0%
393		**Level 2**	**17 days**	**Thu 9/03/23**	**Fri 31/03/23**	**0%**
394		Render	6 days	Thu 9/03/23	Thu 16/03/23	0%
395		Paint [inc Caulk]	6 days	Mon 13/03/23	Mon 20/03/23	0%
396		**Fitoff**	**6 days**	**Wed 15/03/23**	**Wed 22/03/23**	**0%**
397		Downpipes	1 day	Tue 21/03/23	Tue 21/03/23	0%
398		Signage	2 days	Tue 21/03/23	Wed 22/03/23	0%
399		Balustrades	5 days	Wed 15/03/23	Tue 21/03/23	0%
400		Sunshades	5 days	Wed 15/03/23	Tue 21/03/23	0%
401		Vents	1 day	Tue 21/03/23	Tue 21/03/23	0%
402		Clean	2 days	Thu 23/03/23	Fri 24/03/23	0%
403		Builders Defects	1 day	Mon 27/03/23	Mon 27/03/23	0%
404		Defect Rectification	2 days	Tue 28/03/23	Wed 29/03/23	0%
405		Scaffold Drop	2 days	Thu 30/03/23	Fri 31/03/23	0%
406		**Level 1**	**18 days**	**Mon 20/03/23**	**Fri 14/04/23**	**0%**
407		Render	6 days	Mon 20/03/23	Mon 27/03/23	0%
408		Paint [inc Caulk]	6 days	Wed 22/03/23	Wed 29/03/23	0%
409		**Fitoff**	**6 days**	**Fri 24/03/23**	**Fri 31/03/23**	**0%**
410		Downpipes	1 day	Thu 30/03/23	Thu 30/03/23	0%
411		Signage	2 days	Thu 30/03/23	Fri 31/03/23	0%
412		Balustrades	5 days	Fri 24/03/23	Thu 30/03/23	0%
413		Sunshades	5 days	Fri 24/03/23	Thu 30/03/23	0%
414		Vents	1 day	Thu 30/03/23	Thu 30/03/23	0%
415		Clean	2 days	Mon 3/04/23	Tue 4/04/23	0%
416		Builders Defects	1 day	Wed 5/04/23	Wed 5/04/23	0%
417		Defect Rectification	2 days	Thu 6/04/23	Tue 11/04/23	0%
418		Scaffold Drop	3 days	Wed 12/04/23	Fri 14/04/23	0%
419		**Level G**	**15 days**	**Fri 31/03/23**	**Mon 24/04/23**	**0%**
420		Render	6 days	Fri 31/03/23	Tue 11/04/23	0%
421		Paint [inc Caulk]	6 days	Tue 4/04/23	Thu 13/04/23	0%
422		**Fitoff**	**6 days**	**Thu 6/04/23**	**Mon 17/04/23**	**0%**
423		Downpipes	1 day	Fri 14/04/23	Fri 14/04/23	0%
424		Signage	2 days	Fri 14/04/23	Mon 17/04/23	0%
425		Balustrades	5 days	Thu 6/04/23	Fri 14/04/23	0%
426		Sunshades	5 days	Thu 6/04/23	Fri 14/04/23	0%
427		Vents	1 day	Fri 14/04/23	Fri 14/04/23	0%
428		Clean	2 days	Tue 18/04/23	Wed 19/04/23	0%
429		Builders Defects	1 day	Thu 20/04/23	Thu 20/04/23	0%
430		Defect Rectification	2 days	Fri 21/04/23	Mon 24/04/23	0%
431		**FIT OUT**	**108 days**	**Tue 13/12/22**	**Fri 2/06/23**	**0%**
559		**LANDSCAPE WORKS**	**67 days**	**Wed 3/05/23**	**Fri 4/08/23**	**0%**
604		**Commissioning /Project completion**	**37 days**	**Thu 20/04/23**	**Wed 14/06/23**	**0%**
614						
615		scaffold	28 wks	Thu 1/09/22	Mon 3/04/23	0%

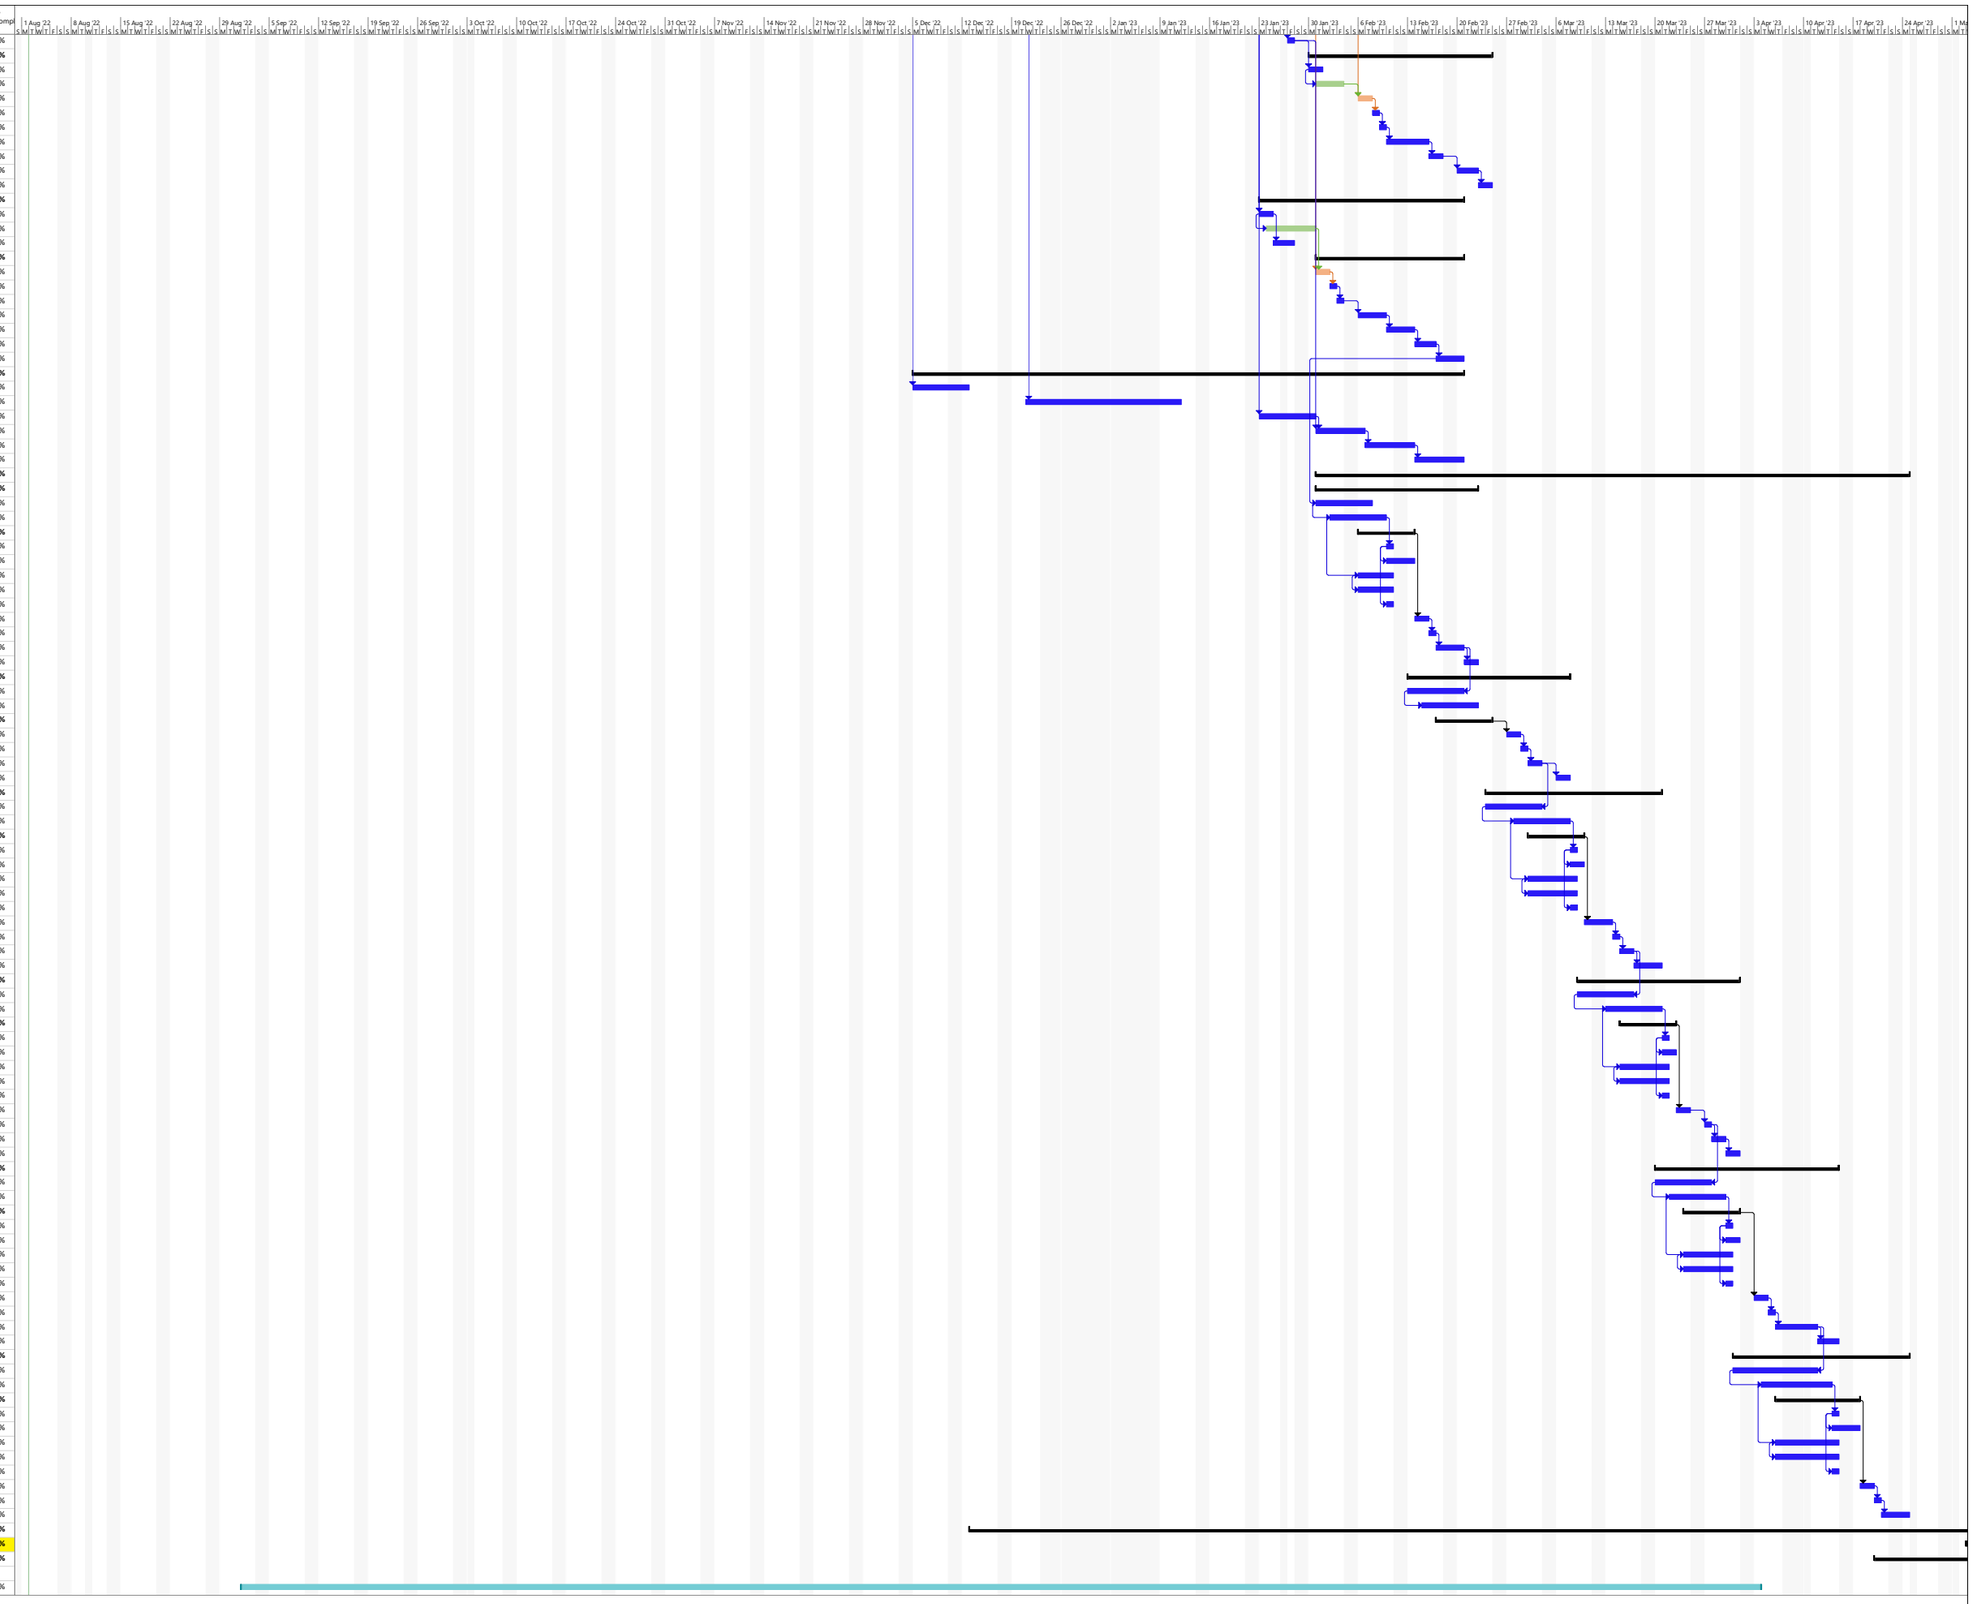

Project: Lowanna Beach Resort
Date: Tue 2/08/22

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress | Critical
