Gant Chart

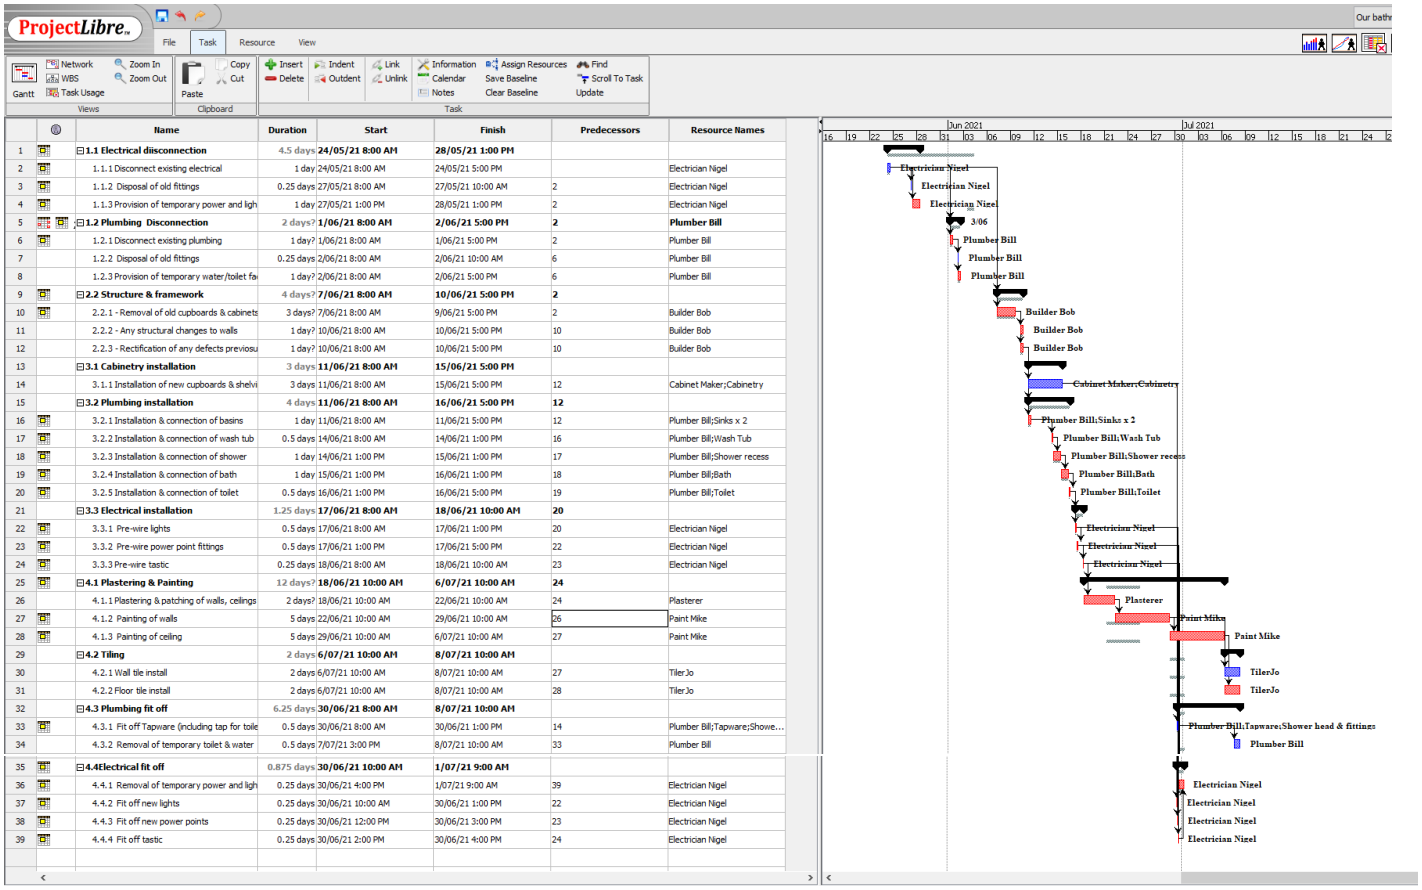

	Name	Duration	Start	Finish	Predecessors	Resource Names
1	**1.1 Electrical diisconnection**	4.5 days	**24/05/21 8:00 AM**	**28/05/21 1:00 PM**		
2	1.1.1 Disconnect existing electrical	1 day	24/05/21 8:00 AM	24/05/21 5:00 PM		Electrician Nigel
3	1.1.2 Disposal of old fittings	0.25 days	27/05/21 8:00 AM	27/05/21 10:00 AM	2	Electrician Nigel
4	1.1.3 Provision of temporary power and ligh	1 day	27/05/21 1:00 PM	28/05/21 1:00 PM	2	Electrician Nigel
5	**1.2 Plumbing Disconnection**	2 days?	**1/06/21 8:00 AM**	**2/06/21 5:00 PM**	**2**	**Plumber Bill**
6	1.2.1 Disconnect existing plumbing	1 day?	1/06/21 8:00 AM	1/06/21 5:00 PM	2	Plumber Bill
7	1.2.2 Disposal of old fittings	0.25 days	2/06/21 8:00 AM	2/06/21 10:00 AM	6	Plumber Bill
8	1.2.3 Provision of temporary water/toilet fa	1 day?	2/06/21 8:00 AM	2/06/21 5:00 PM	6	Plumber Bill
9	**2.2 Structure & framework**	4 days?	**7/06/21 8:00 AM**	**10/06/21 5:00 PM**	**2**	
10	2.2.1 - Removal of old cupboards & cabinets	3 days?	7/06/21 8:00 AM	9/06/21 5:00 PM	2	Builder Bob
11	2.2.2 - Any structural changes to walls	1 day?	10/06/21 8:00 AM	10/06/21 5:00 PM	10	Builder Bob
12	2.2.3 - Rectification of any defects previosu	1 day?	10/06/21 8:00 AM	10/06/21 5:00 PM	10	Builder Bob
13	**3.1 Cabinetry installation**	3 days	**11/06/21 8:00 AM**	**15/06/21 5:00 PM**		
14	3.1.1 Installation of new cupboards & shelvi	3 days	11/06/21 8:00 AM	15/06/21 5:00 PM	12	Cabinet Maker;Cabinetry
15	**3.2 Plumbing installation**	4 days	**11/06/21 8:00 AM**	**16/06/21 5:00 PM**	**12**	
16	3.2.1 Installation & connection of basins	1 day	11/06/21 8:00 AM	11/06/21 5:00 PM	12	Plumber Bill;Sinks x 2
17	3.2.2 Installation & connection of wash tub	0.5 days	14/06/21 8:00 AM	14/06/21 1:00 PM	16	Plumber Bill;Wash Tub
18	3.2.3 Installation & connection of shower	1 day	14/06/21 1:00 PM	15/06/21 1:00 PM	17	Plumber Bill;Shower recess
19	3.2.4 Installation & connection of bath	1 day	15/06/21 1:00 PM	16/06/21 1:00 PM	18	Plumber Bill;Bath
20	3.2.5 Installation & connection of toilet	0.5 days	16/06/21 1:00 PM	16/06/21 5:00 PM	19	Plumber Bill;Toilet
21	**3.3 Electrical installation**	1.25 days	**17/06/21 8:00 AM**	**18/06/21 10:00 AM**	**20**	
22	3.3.1 Pre-wire lights	0.5 days	17/06/21 8:00 AM	17/06/21 1:00 PM	20	Electrician Nigel
23	3.3.2 Pre-wire power point fittings	0.5 days	17/06/21 1:00 PM	17/06/21 5:00 PM	22	Electrician Nigel
24	3.3.3 Pre-wire tastic	0.25 days	18/06/21 8:00 AM	18/06/21 10:00 AM	23	Electrician Nigel
25	**4.1 Plastering & Painting**	12 days?	**18/06/21 10:00 AM**	**6/07/21 10:00 AM**	**24**	
26	4.1.1 Plastering & patching of walls, ceilings	2 days?	18/06/21 10:00 AM	22/06/21 10:00 AM	24	Plasterer
27	4.1.2 Painting of walls	5 days	22/06/21 10:00 AM	29/06/21 10:00 AM	26	Paint Mike
28	4.1.3 Painting of ceiling	5 days	29/06/21 10:00 AM	6/07/21 10:00 AM	27	Paint Mike
29	**4.2 Tiling**	2 days	**6/07/21 10:00 AM**	**8/07/21 10:00 AM**		
30	4.2.1 Wall tile install	2 days	6/07/21 10:00 AM	8/07/21 10:00 AM	27	TilerJo
31	4.2.2 Floor tile install	2 days	6/07/21 10:00 AM	8/07/21 10:00 AM	28	TilerJo
32	**4.3 Plumbing fit off**	6.25 days	**30/06/21 8:00 AM**	**8/07/21 10:00 AM**		
33	4.3.1 Fit off Tapware (including tap for toile	0.5 days	30/06/21 8:00 AM	30/06/21 1:00 PM	14	Plumber Bill;Tapware;Showe...
34	4.3.2 Removal of temporary toilet & water	0.5 days	7/07/21 3:00 PM	8/07/21 10:00 AM	33	Plumber Bill
35	**4.4Electrical fit off**	0.875 days	**30/06/21 10:00 AM**	**1/07/21 9:00 AM**		
36	4.4.1 Removal of temporary power and ligh	0.25 days	30/06/21 4:00 PM	1/07/21 9:00 AM	39	Electrician Nigel
37	4.4.2 Fit off new lights	0.25 days	30/06/21 10:00 AM	30/06/21 1:00 PM	22	Electrician Nigel
38	4.4.3 Fit off new power points	0.25 days	30/06/21 12:00 PM	30/06/21 3:00 PM	23	Electrician Nigel
39	4.4.4 Fit off tastic	0.25 days	30/06/21 2:00 PM	30/06/21 4:00 PM	24	Electrician Nigel
