redkat

Red Kat Pty Ltd

PO Box 342, EVERTON PARK Q 4053
E: admin@redkat.net.au

© Ryan Readdy 2016. All rights reserved.

Torview Street Rochedale

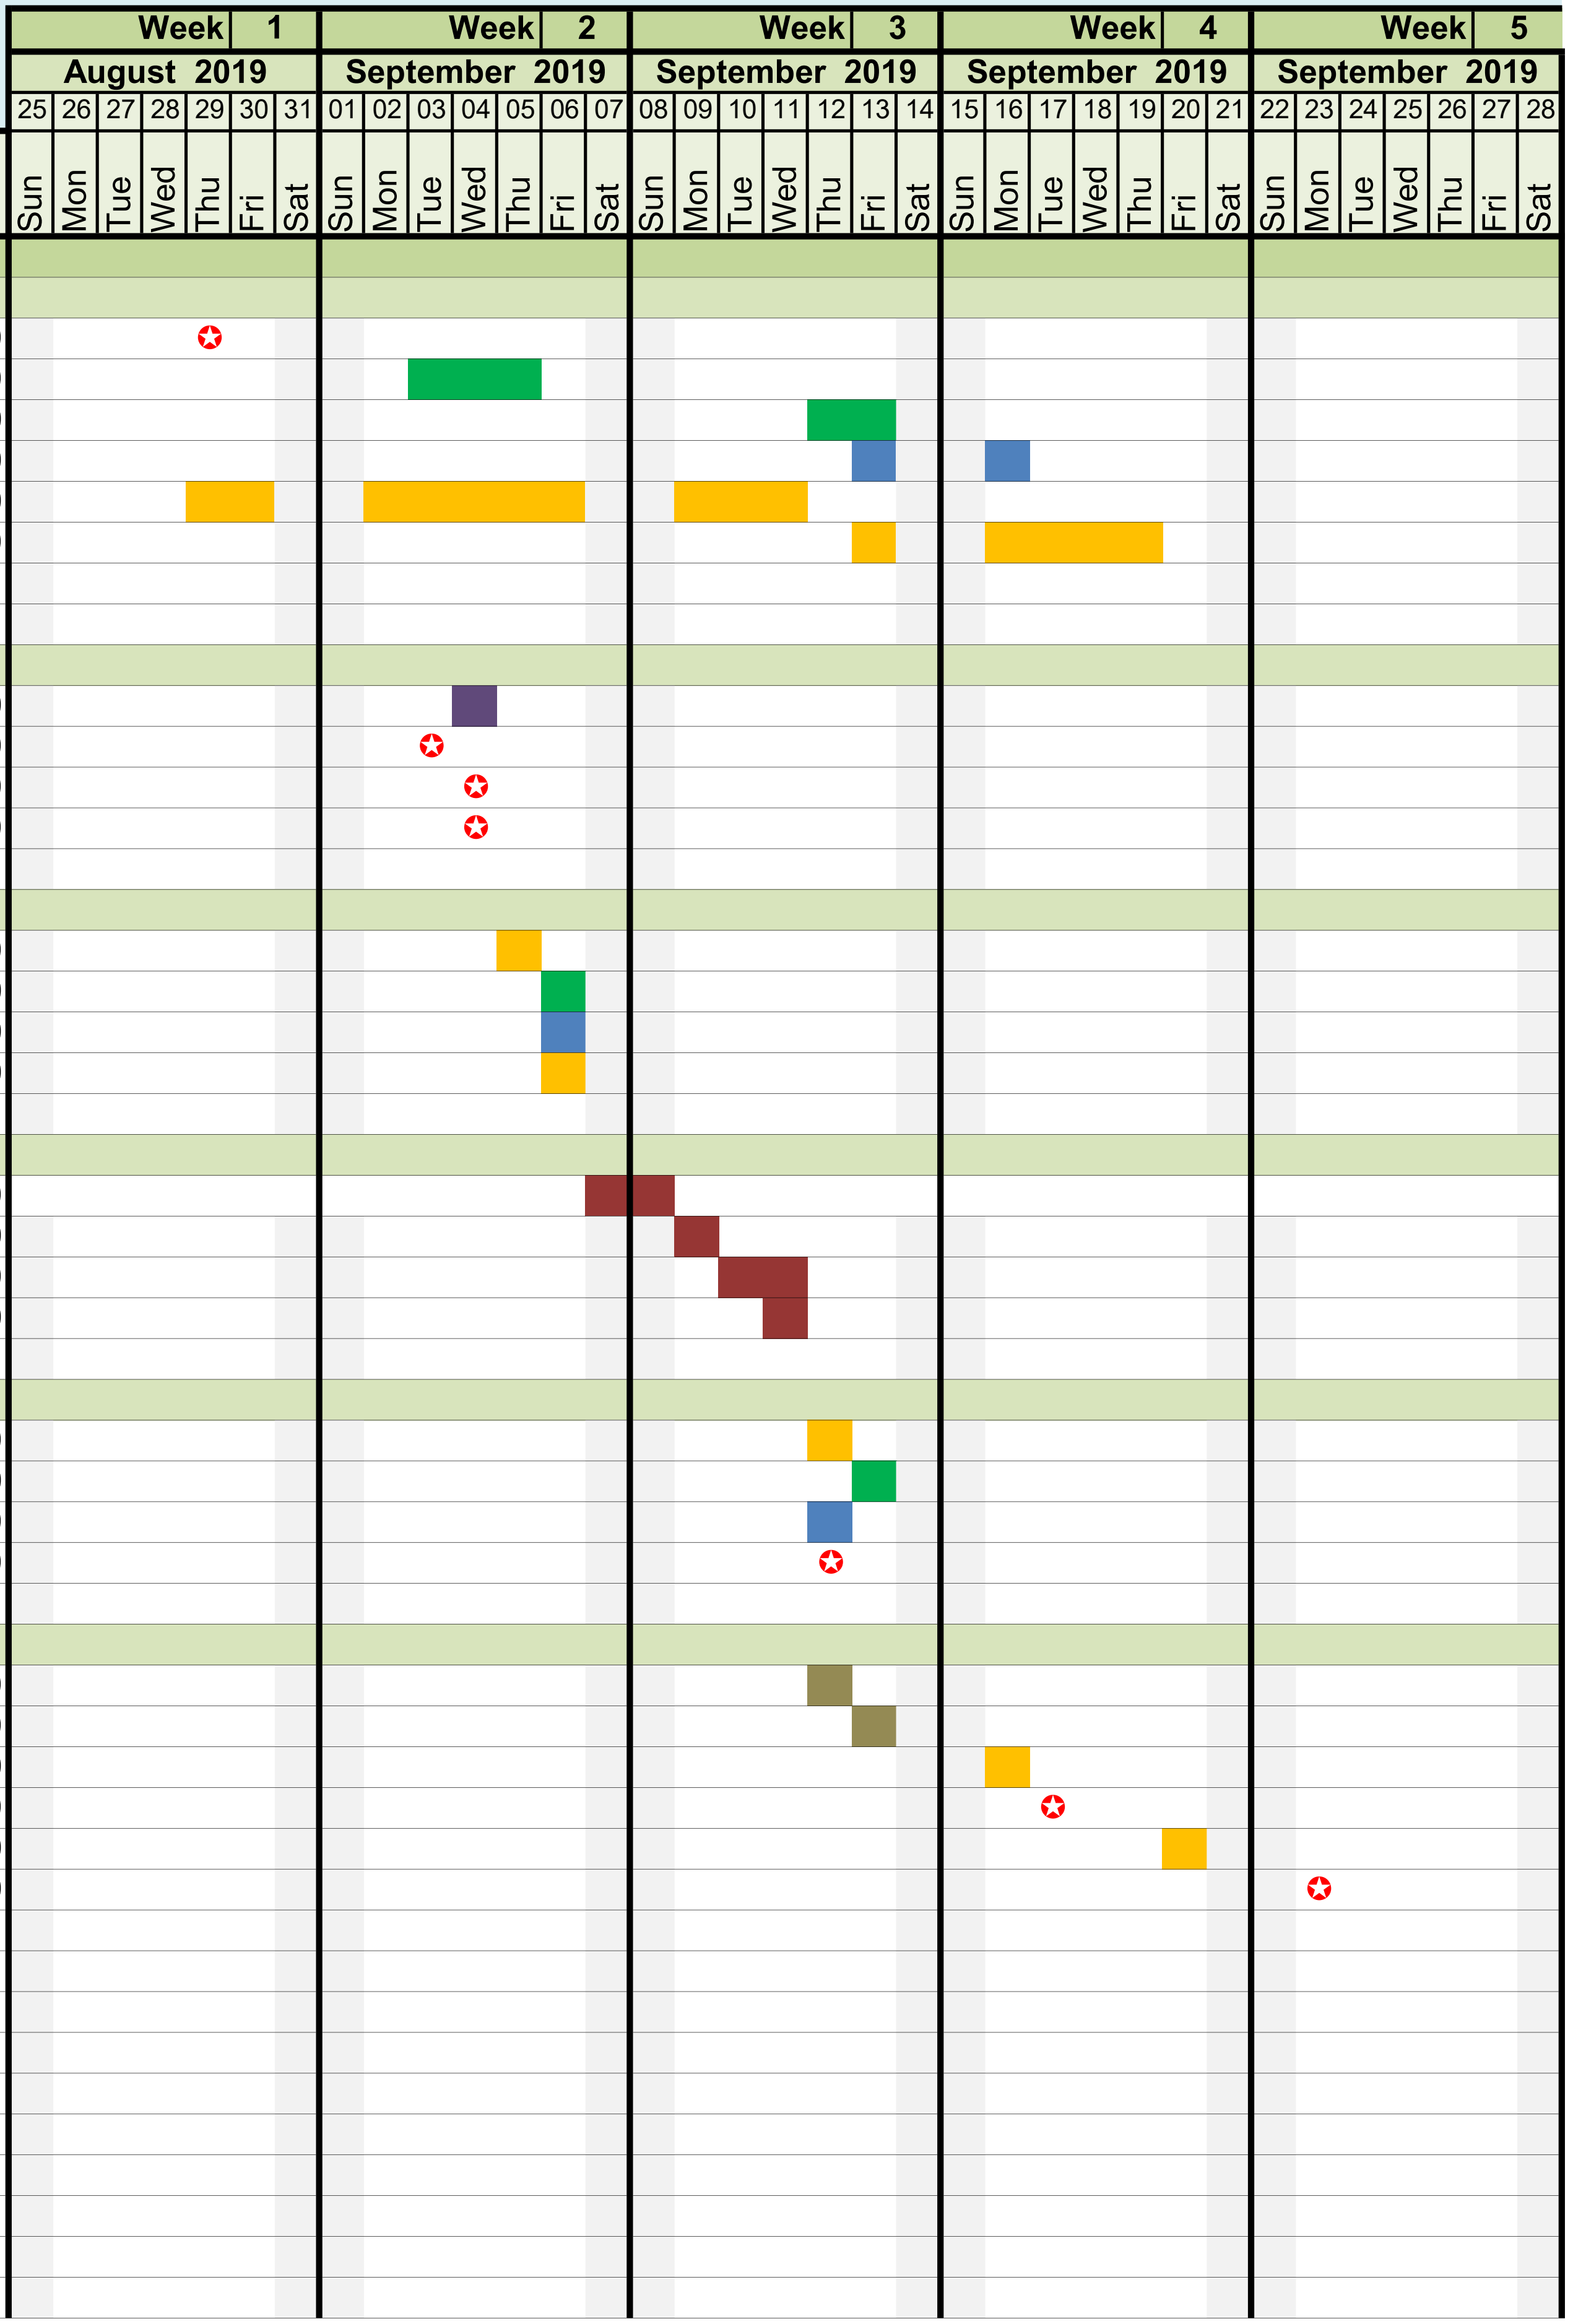Task ID #	Task Description	Predecessor	Lag	Duration	Start	Finish
1	**Torview Street Rochedale**					
2	Procurement					
3	Signoff of project FFE schedule			0	Thu - 29 Aug 2019	Thu - 29 Aug 2019
4	Plumbing in wall FFE		5	3	Tue - 03 Sep 2019	Thu - 05 Sep 2019
5	Plumbing fixtures		14	2	Thu - 12 Sep 2019	Fri - 13 Sep 2019
6	Electrical Lights, switches, 3 in 1		15	2	Fri - 13 Sep 2019	Mon - 16 Sep 2019
7	Cabinetry			10	Thu - 29 Aug 2019	Wed - 11 Sep 2019
8	Shower screen	33		5	Fri - 13 Sep 2019	Thu - 19 Sep 2019
9						
10						
11	Demolition					
12	Commencement of works (demolition)		6	1	Wed - 04 Sep 2019	Wed - 04 Sep 2019
13	Skip bin delivery	12	-2	0	Tue - 03 Sep 2019	Tue - 03 Sep 2019
14	Plumbing Disconnection	12	-1	0	Wed - 04 Sep 2019	Wed - 04 Sep 2019
15	Electrical Disconnection	12	-1	0	Wed - 04 Sep 2019	Wed - 04 Sep 2019
16						
17	Roughin Works					
18	Carpentry	12		1	Thu - 05 Sep 2019	Thu - 05 Sep 2019
19	Plumbing	18		1	Fri - 06 Sep 2019	Fri - 06 Sep 2019
20	Electrical	19	-1	1	Fri - 06 Sep 2019	Fri - 06 Sep 2019
21	Sheeting of bathroom	20	-1	1	Fri - 06 Sep 2019	Fri - 06 Sep 2019
22						
23	Tiling Works					
24	Water proofing	21		2	Sat - 07 Sep 2019	Sun - 08 Sep 2019
25	Screeding	24		1	Mon - 09 Sep 2019	Mon - 09 Sep 2019
26	Tiling and grouting	25		2	Tue - 10 Sep 2019	Wed - 11 Sep 2019
27	Silicone	26	-1	1	Wed - 11 Sep 2019	Wed - 11 Sep 2019
28						
29	Fitoff					
30	Install vanity and mirror cabinets	27		1	Thu - 12 Sep 2019	Thu - 12 Sep 2019
31	Plumbing Fitoff	30		1	Fri - 13 Sep 2019	Fri - 13 Sep 2019
32	Electrical Fitoff	27		1	Thu - 12 Sep 2019	Thu - 12 Sep 2019
33	Site measure of shower screen	26		0	Thu - 12 Sep 2019	Thu - 12 Sep 2019
34						
35	Finishing works					
36	Cornice ceiling patch	27		1	Thu - 12 Sep 2019	Thu - 12 Sep 2019
37	Painting	32		1	Fri - 13 Sep 2019	Fri - 13 Sep 2019
38	Final Clean	37		1	Mon - 16 Sep 2019	Mon - 16 Sep 2019
39	Defects	38		0	Tue - 17 Sep 2019	Tue - 17 Sep 2019
40	Install shower screen	8		1	Fri - 20 Sep 2019	Fri - 20 Sep 2019
41	Project Close out with owner	40		0	Mon - 23 Sep 2019	Mon - 23 Sep 2019
42						
43						
44						
45						
46						
47						
48						
49						
50						
51
