Bruce Highway Upgrade - Deception Bay Road Interchange

Contract Number CN-12858

BMD constructions
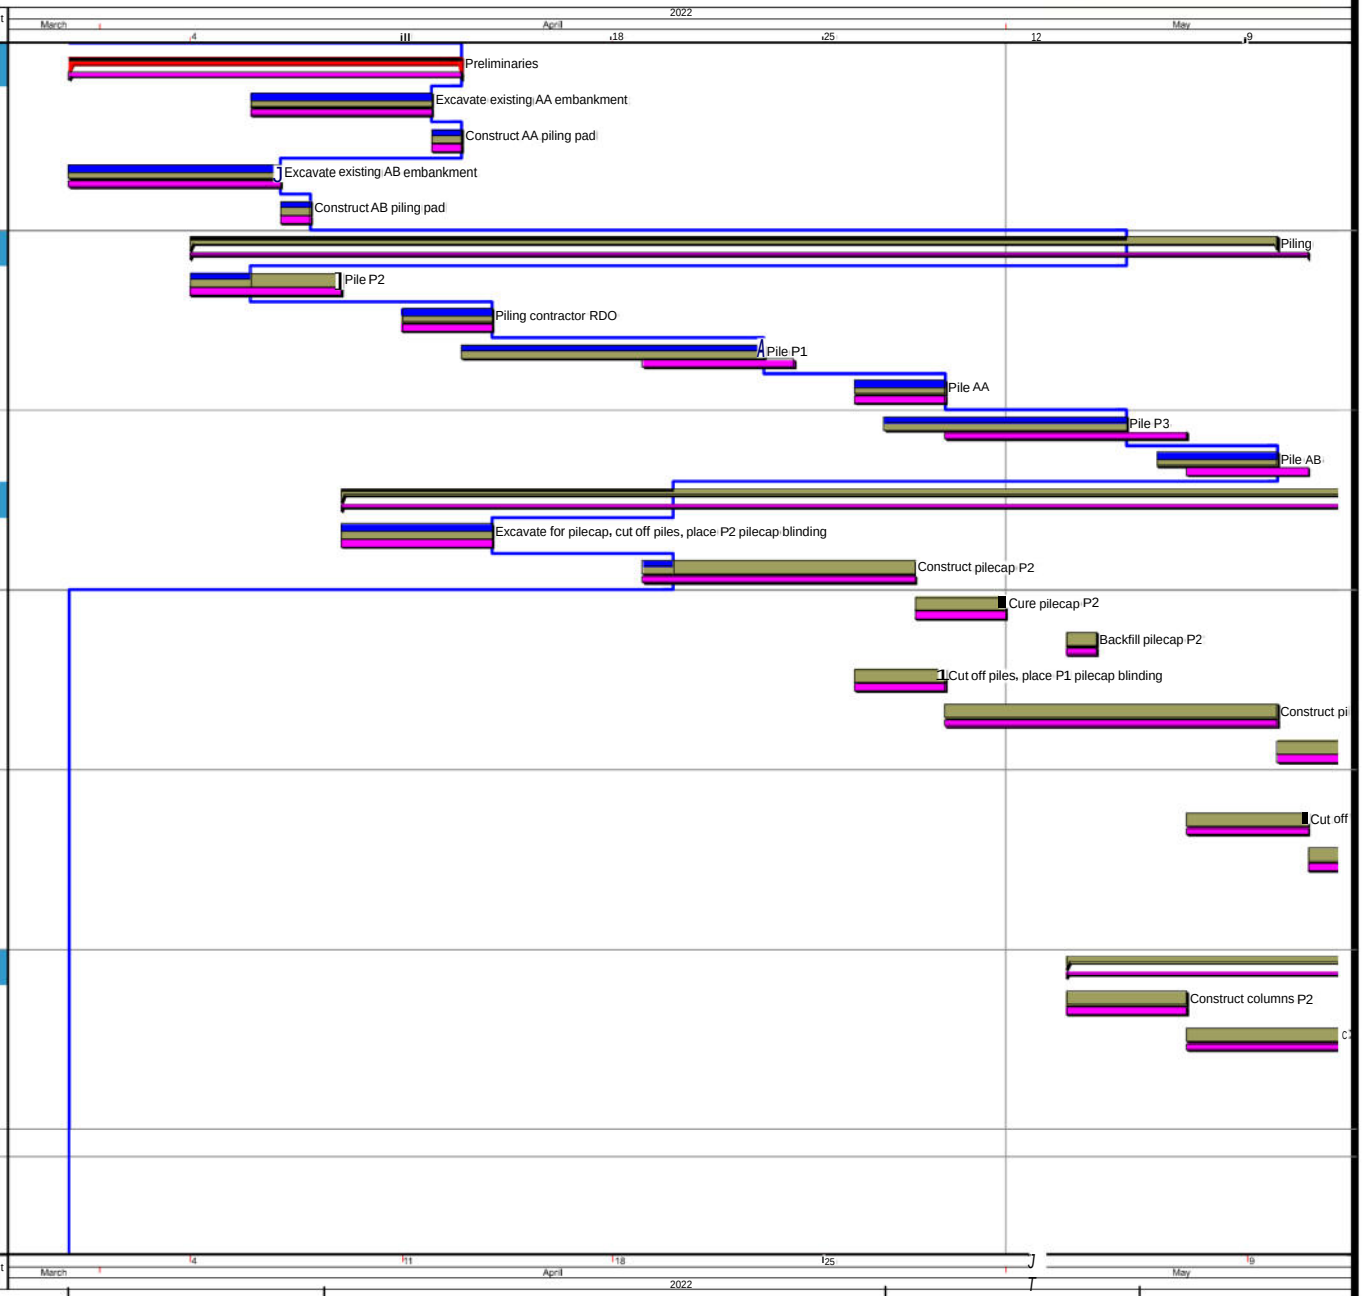
Line	Unique Task ID	Name	Duration	Start	Finish	Total float	Predecessors	Successors	Overall percent complete
1	A187300	Preliminaries	10d	31 Mar 22	12 Apr 22				100.00
2	A187400	Excavate existing AA embankment	5d	06 Apr 22	11 Apr 22	7d	ns, ns	3	100.00
3	A187500	Construct AA piling pad	1d	12 Apr 22	12 Apr 22	7d	2	10	100.00
4	A187600	Excavate existing AB embankment	5d	31 Mar 22	06 Apr 22	41d	ns	5	100.00
5	A187700	Construct AB piling pad	1d	07 Apr 22	07 Apr 22	41d	4	12	100.00
6	A187800	Piling	24d	04 Apr 22	09 May 22	23d			90.91
7	A187900	Pile P2	5d	04 Apr 22	08 Apr 22	2d	ns	8, 9, 14	50.00
8	A187901	Piling contractor RDO	3d	11 Apr 22	13 Apr 22	1d	7	9	100.00
9	A188000	Pile P1	5d	13 Apr 22	22 Apr 22	1d	7, 8	18, 10	100.00
10	A188100	Pile AA	3d	26 Apr 22	28 Apr 22	1d	3, 9	35, 11	100.00
11	A188200	Pile P3	5d	27 Apr 22	04 May 22	1d	10	22, 12	100.00
12	A188300	Pile AB	3d	06 May 22	09 May 22	23d	5, 11	47	100.00
13	A188400	Pilecaps	30d	09 Apr 22	23 May 22	1d			10.00
14	A188500	Excavate for pilecap, cut off piles, place P2 pilecap blinding	4d	09 Apr 22	13 Apr 22	12d	7	15	100.00
15	A188600	Construct pilecap P2	7d	19 Apr 22	27 Apr 22	12d	14	16, 27 FF 7ed	20.00
16	A188700	Cure pilecap P2	3d	28 Apr 22	30 Apr 22	16d	15	17	
17	A188800	Backfill pilecap P2	1d	03 May 22	03 May 22	11d	16	27 SS	
18	A188900	Cut off piles, place P1 pilecap blinding	3d	26 Apr 22	28 Apr 22	5d	9	19	
19	A189000	Construct pilecap P1	7d	29 Apr 22	09 May 22	5d	18	20, 29 FF 7ed	
20	A189100	Cure pilecap P1	3d	10 May 22	12 May 22	7d	19	21	
21	A189200	Backfill pilecap P1	1d	13 May 22	13 May 22	5d	20	29 SS	
22	A189300	Cut off piles, place P3 pilecap blinding	3d	07 May 22	10 May 22	1d	11	23	
23	A189400	Construct pilecap P3	7d	11 May 22	19 May 22	1d	22	24, 31 FF 7ed	
24	A189500	Cure pilecap P3	3d	20 May 22	22 May 22	1d	23	25	
25	A189600	Backfill pilecap P3	1d	23 May 22	23 May 22	1d	24	31 SS	
26	A189700	Pier columns	23d	03 May 22	31 May 22	1d			
27	A189800	Construct columns P2	4d	03 May 22	06 May 22	11d	17 SS, 15 FF 7ed	28	
28	A189900	Cure columns P2	5d	07 May 22	11 May 22	14d	27	59, 31 -2d	
29	A190000	Construct columns P1	4d	13 May 22	18 May 22	5d	21 SS, 19 FF 7ed	30	
30	A190100	Cure columns P1	5d	19 May 22	23 May 22	6d	29	66
