[redacted]

# Design & Construction Programme REV P (status as at 7th Sept 22)

[redacted]

| ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|
| 1 | [redacted] | 339.65 days | Fri 17/09/21 | Fri 10/03/23 |
| 2 | **KEY MILESTONES** | **339 days** | **Fri 17/09/21** | **Thu 9/03/23** |
| 3 | Anticipated Contract Award | 1 day | Fri 17/09/21 | Fri 17/09/21 |
| 4 | Site Possession | 1 day | Fri 8/10/21 | Fri 8/10/21 |
| 5 | Forecast Handover of Gaming Lounge | 0 days | Wed 8/02/23 | Wed 8/02/23 |
| 6 | Contract Date For Practical Completion | 0 days | Thu 9/03/23 | Thu 9/03/23 |
| 7 | **OFF SITE WORKS** | **222 days** | **Fri 17/09/21** | **Fri 2/09/22** |
| 8 | **TENDER** | **22 days** | **Fri 17/09/21** | **Thu 21/10/21** |
| 9 | Anticipated Letter Of Acceptance | 0 days | Fri 17/09/21 | Fri 17/09/21 |
| 10 | Mobilisation | 18 days | Fri 24/09/21 | Thu 21/10/21 |
| 11 | **APPROVALS** | **107 days** | **Thu 23/09/21** | **Thu 17/03/22** |
| 62 | **KEY PROCUREMENT** | **217 days** | **Mon 27/09/21** | **Fri 2/09/22** |
| 98 | **ONSITE WORKS** | **310.65 days** | **Tue 2/11/21** | **Fri 10/03/23** |
| 99 | **SITE ESTABLISHMENT** | **28.5 days** | **Tue 2/11/21** | **Tue 14/12/21** |
| 100 | Site Fencing & Shade Cloth | 4 days | Tue 2/11/21 | Fri 5/11/21 |
| 101 | Site offices & Amenities | 10 days | Mon 29/11/21 | Mon 13/12/21 |
| 102 | Temporary Connections | 2 days | Fri 10/12/21 | Tue 14/12/21 |
| 103 | **STRUCTURE & ENVELOPE** | **306.65 days** | **Tue 9/11/21** | **Fri 10/03/23** |
| 104 | Site Survey & Services Investigations | 6 days | Tue 9/11/21 | Tue 16/11/21 |
| 105 | Excavate Basement | 30 days | Wed 24/11/21 | Fri 18/02/22 |
| 106 | EOT 03 - WET WEATHER ON 15th & 16th FEBRUARY 202 | 2 days | Tue 15/02/22 | Wed 16/02/22 |
| 107 | EOT 04 - WET WEATHER ON 23rd FEBRUARY through to and including 1st MARCH 2022 | 5 days | Wed 23/02/22 | Tue 1/03/22 |
| 108 | EOT 05 - WET WEATHER ON 2nd MARCH through to and including 4th MARCH 2022 | 3 days | Wed 2/03/22 | Fri 4/03/22 |
| 109 | EOT 06 - WET WEATHER on 11th March 2022 | 1 day | Fri 11/03/22 | Fri 11/03/22 |
| 110 | Footings to Retaining Wall system | 17 days | Tue 11/01/22 | Tue 22/02/22 |
| 111 | Retaining Wall system installation | 10 days | Tue 25/01/22 | Fri 11/03/22 |
| 112 | Create Piling Platform | 2 days | Fri 14/01/22 | Mon 17/01/22 |
| 113 | Piling to Perimeter | 4 days | Mon 24/01/22 | Fri 28/01/22 |
| 114 | Inground Drainage (Stormwater & Sewer) | 18 days | Wed 19/01/22 | Thu 24/03/22 |
| 115 | Connections | 3 days | Fri 25/03/22 | Tue 29/03/22 |
| 116 | Construct Detention Tank Base | 12 days | Wed 23/02/22 | Wed 8/06/22 |
| 117 | Head Beam to top retaining wall system | 15 days | Mon 28/02/22 | Mon 21/03/22 |
| 118 | Pad Footings | 25 days | Tue 18/01/22 | Mon 4/04/22 |
| 119 | Backfill to underside of slab on ground - Basement | 10 days | Mon 21/02/22 | Fri 8/04/22 |
| 120 | FRP Columns | 15 days | Thu 10/03/22 | Mon 4/04/22 |
| 121 | Loadbearing Blockwork walls | 10 days | Thu 31/03/22 | Thu 14/04/22 |
| 122 | EOT 07 - WET WEATHER on 28th March 2022 | 1 day | Mon 28/03/22 | Mon 28/03/22 |
| 123 | Formwork to Ground Floor Slab - Pour 1 | 9 days | Thu 7/04/22 | Tue 26/04/22 |
| 124 | Bottom Reo. To Ground Floor Slab - Pour 1 | 3 days | Tue 19/04/22 | Fri 22/04/22 |
| 125 | P.T. Strands to Ground Floor Slab - Pour 1 | 3 days | Thu 21/04/22 | Wed 27/04/22 |
| 126 | Cast In services to Ground Floor Slab - Pour 1 | 3 days | Fri 22/04/22 | Fri 29/04/22 |
| 127 | Top Reo to Ground Floor Slab - Pour 1 | 3 days | Wed 27/04/22 | Tue 3/05/22 |
| 128 | Pour Concrete to Ground Floor Slab - Pour 1 | 1 day | Tue 3/05/22 | Wed 4/05/22 |
| 129 | Tension Slab to Ground Floor Slab - Pour 1 | 1 day | Tue 10/05/22 | Wed 11/05/22 |
| 130 | EOT 08 - WET WEATHER on 26th & 28th March 2022 | 2 days | Tue 26/04/22 | Wed 27/04/22 |
| 131 | Formwork to Ground Floor Slab - Pour 2 | 8 days | Fri 22/04/22 | Mon 9/05/22 |
| 132 | Bottom Reo. To Ground Floor Slab - Pour 2 | 3 days | Tue 3/05/22 | Mon 9/05/22 |
| 133 | P.T. Strands to Ground Floor Slab - Pour 2 | 3 days | Thu 5/05/22 | Wed 11/05/22 |
| 134 | Cast In services to Ground Floor Slab - Pour 2 | 3 days | Fri 6/05/22 | Wed 11/05/22 |
| 135 | Top Reo to Ground Floor Slab - Pour 2 | 3 days | Tue 10/05/22 | Fri 13/05/22 |
| 136 | Pour Concrete to Ground Floor Slab - Pour 2 | 1 day | Fri 13/05/22 | Mon 16/05/22 |
| 137 | EOT 09 - WET WEATHER from 9th to13th May inclusive | 5 days | Mon 9/05/22 | Fri 13/05/22 |
| 138 | Tension Slab to Ground Floor Slab - Pour 2 | 1 day | Mon 16/05/22 | Tue 17/05/22 |
| 139 | EOT 10 - WET WEATHER intermittent from 23rd to 25th May inclusive | 2 days | Mon 23/05/22 | Wed 25/05/22 |
| 140 | Formwork to Ground Floor Slab - Pour 3 | 8 days | Fri 6/05/22 | Tue 31/05/22 |
| 141 | Bottom Reo. To Ground Floor Slab - Pour 3 | 3 days | Fri 27/05/22 | Tue 31/05/22 |
| 142 | P.T. Strands to Ground Floor Slab - Pour 3 | 3 days | Tue 31/05/22 | Thu 2/06/22 |
| 143 | Cast In services to Ground Floor Slab - Pour 3 | 3 days | Wed 1/06/22 | Fri 3/06/22 |
| 144 | Top Reo to Ground Floor Slab - Pour 3 | 3 days | Thu 2/06/22 | Mon 6/06/22 |
| 145 | Pour Concrete to Ground Floor Slab - Pour 3 | 1 day | Tue 7/06/22 | Tue 7/06/22 |
| 146 | Tension Slab to Ground Floor Slab - Pour 3 | 1 day | Tue 14/06/22 | Tue 14/06/22 |
| 147 | Formwork to Ground Floor Slab - Pour 4 | 11 days | Mon 4/07/22 | Tue 19/07/22 |
| 148 | Bottom Reo. To Ground Floor Slab - Pour 4 | 4 days | Wed 20/07/22 | Mon 25/07/22 |

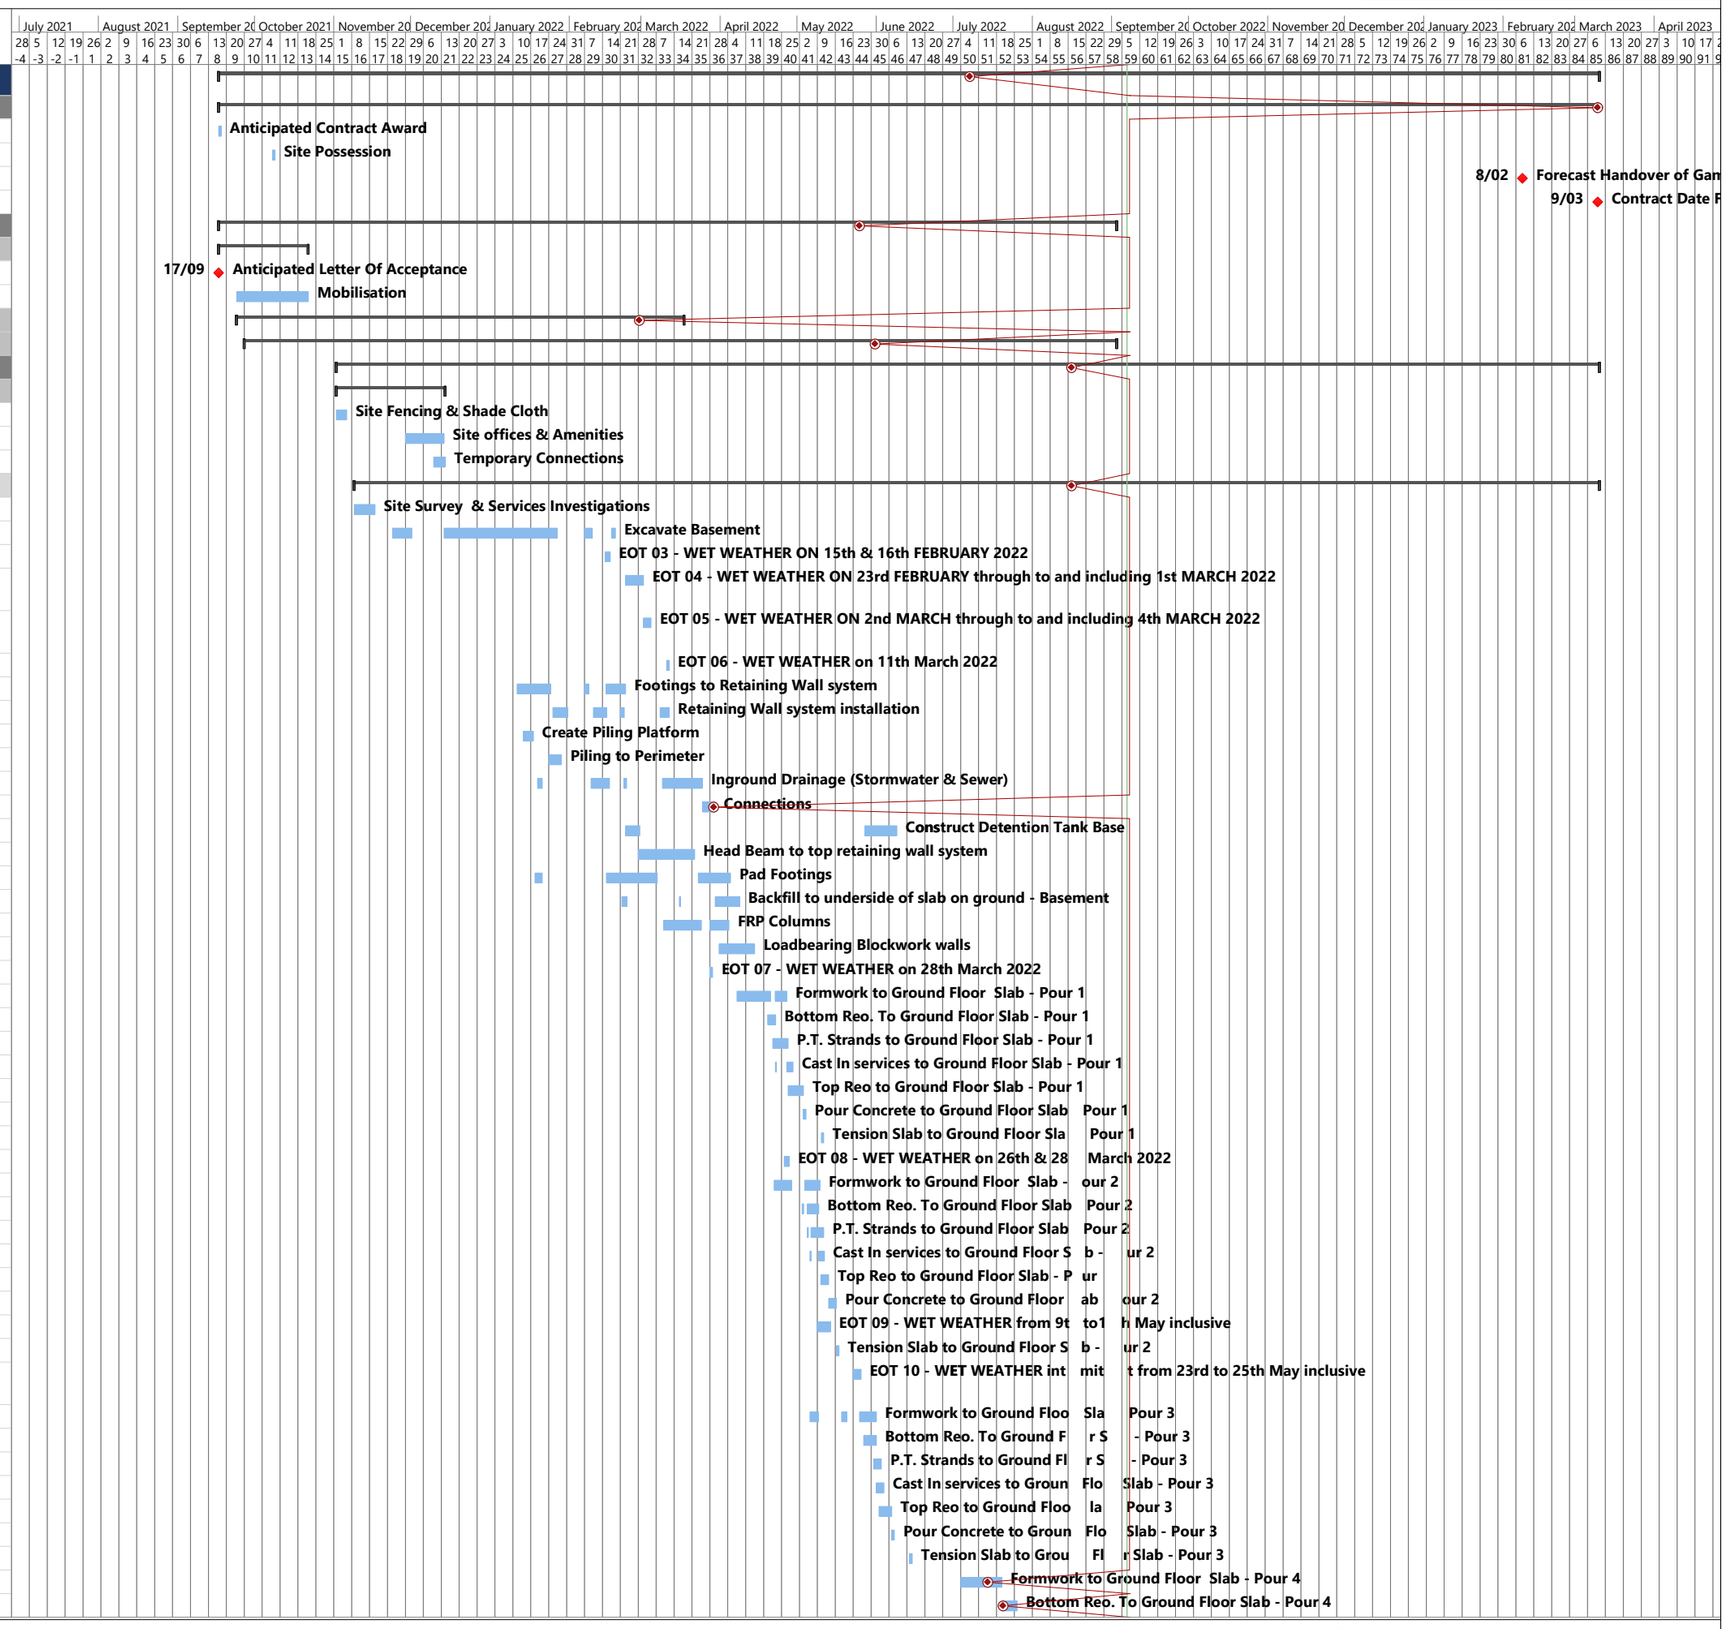


1. This Programme is based on a 5 working day week
2. Non working day allowance made for public hoildays, Christmas Shutdown



Printed: Wed 07/09/22 by CM | Data Date: Wed 7/09/22
Filename: [redacted] - Contract Programme Revision P [redacted]
