Construction Program including critical path
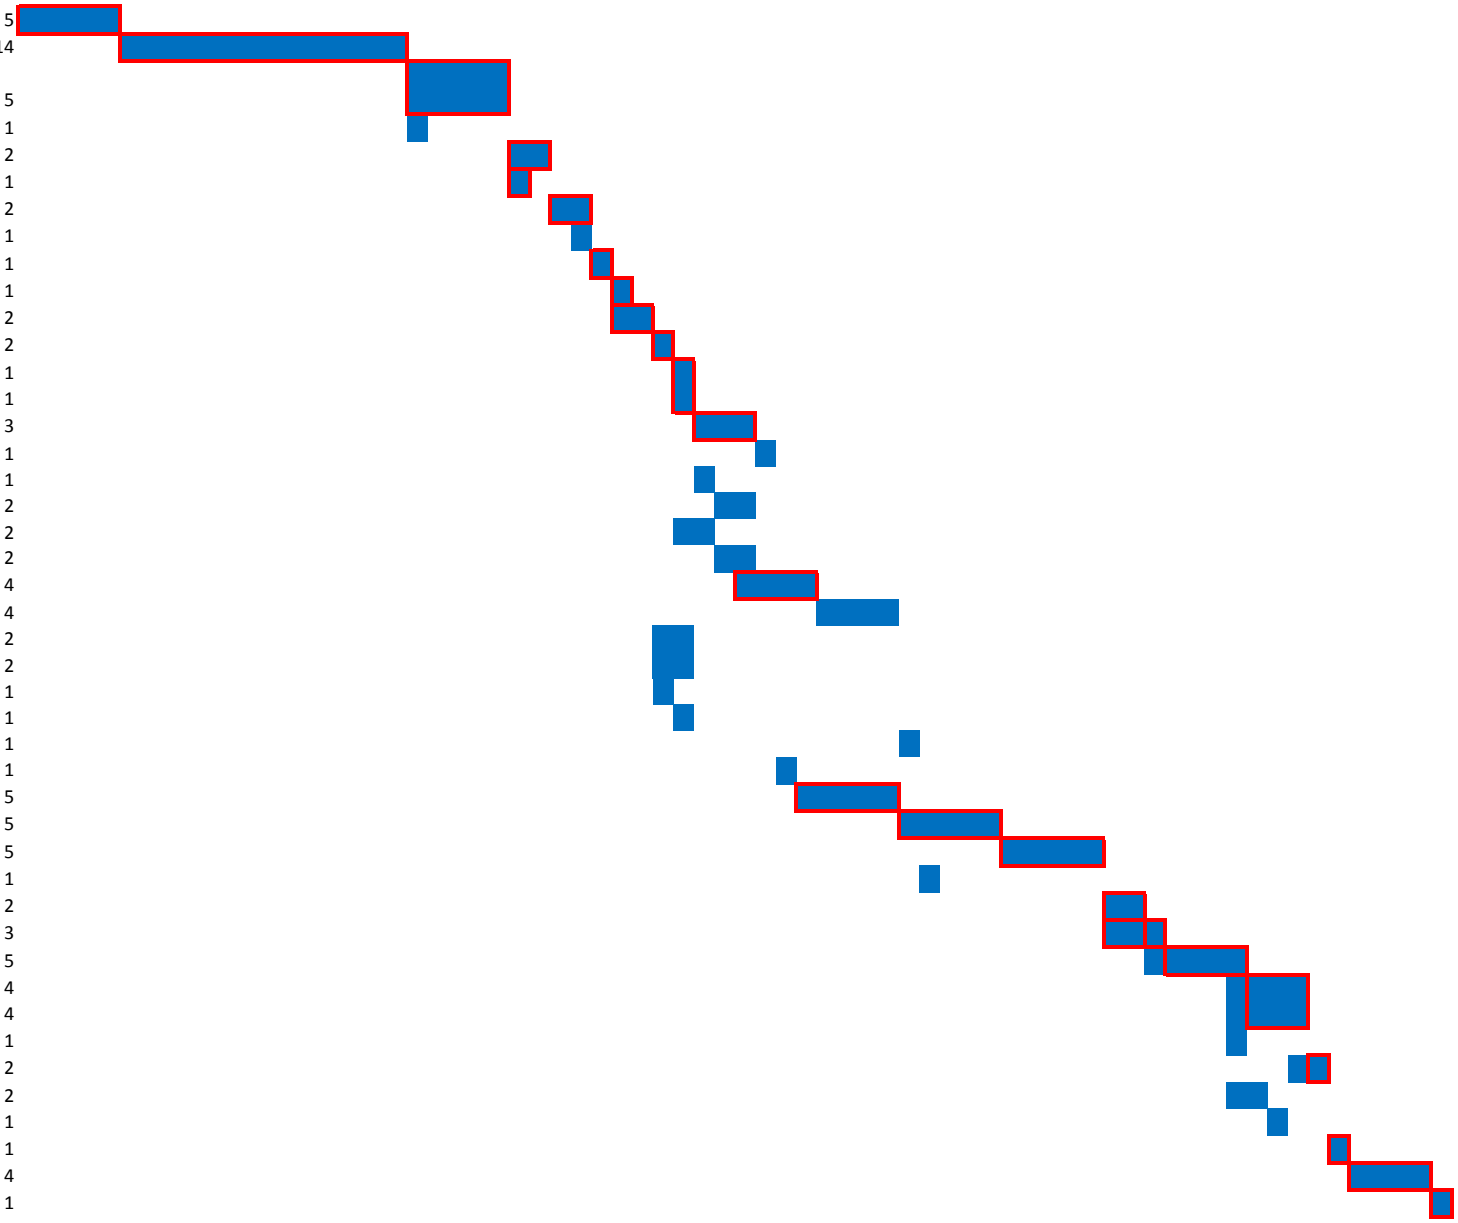
ID	Task Name	Duration
1	allowance for rain dealys	5
2	BA approvals/pumbing approval	14
	Site (13T) preparation 100mm	
3	scrape, site shed/toilet	5
4	survey	1
5	internal drainage	2
6	internal power	1
7	form and steel	2
8	pest control	1
9	pour	1
10	delivery frames	1
11	erect ground frames	2
12	stand trusses	2
13	hang scaffold	1
14	fascia gutter	1
15	metal roofing	3
16	remove hang scaffold	1
17	deliver windows	1
18	frame tie down	2
19	ceiling battens	2
20	install sisilation and windows	2
21	external cladding	4
22	paint external cladding	4
23	plumbing rough in	2
24	electrical rough in	2
25	AC roughin	1
26	frame inspection	1
27	garage door	1
28	pre-sheet inspection	1
29	insulation, wall and ceiling linings	5
30	cornice and setting	5
31	carpentry fixout	5
32	waterproofing	1
33	install kitchen and vanities	2
34	bed and tile wet areas	3
35	internal painting	5
36	electrical fit off	4
37	plumbing fitoff	4
38	ac fit off	1
39	doors, hardware and accessories	2
40	shower screens and mirrors	2
41	robes	1
42	clean	1
43	flooring	4
44	sparkle clean	1
